



**DISCLAIMER**

THE USE OF AND RELIANCE UPON THIS RECORDED-DATA BY THE HEREIN NAMED COMPANY (AND ANY OF ITS AFFILIATES, PARTNERS, REPRESENTATIVES, AGENTS, CONSULTANTS AND EMPLOYEES) IS SUBJECT TO THE TERMS AND CONDITIONS AGREED UPON BETWEEN SCHLUMBERGER AND THE COMPANY, INCLUDING: (a) RESTRICTIONS ON USE OF THE RECORDED-DATA; (b) DISCLAIMERS AND WAIVERS OF WARRANTIES AND REPRESENTATIONS REGARDING COMPANY'S USE OF AND RELIANCE UPON THE RECORDED-DATA; AND (c) CUSTOMER'S FULL AND SOLE RESPONSIBILITY FOR ANY INFERENCE DRAWN OR DECISION MADE IN CONNECTION WITH THE USE OF THIS RECORDED-DATA.

OTHER SERVICES1  
 OS1: HRLA/HLDS  
 OS2: FMS  
 OS3: DSI  
 OS4: MSS

**REMARKS: RUN NUMBER 1**

Hole drilled with RCB coring bit and bottom hole assembly (BHA). 9 7/8 " BS  
 Free-Fall Funnel deployed for re-entry without casing.  
 Bit placed at 96.5mbsf (driller's depth) prior to logging; logs tied into Run 1, Pass 2 bit depth due to low GR at sea bed.  
 Hole was displaced to water-based mud prior to logging.  
 Tools run as per tool sketch with upper section (HNCS & HLDS) eccentered using HLDS caliper and lower section (HRLA & MSS) separated with knuckle joints and centralized using modified MCD inline bowsprings.  
 HLDS data is valid for the first pass, but density data from the second pass is invalid due to caliper failure.  
 Hole obstructed at a depth of 368.6mbsf; tools unable to pass below this depth; logs recorded from this depth up.  
 Bit found at 96.5mbsf; used as tie-in reference for all logs in this hole.  
 MSS Deep Reading (DR) sensor only was run centralized below HRLA.  
 Borehole corrections applied using corrected HLDS caliper (LCAL) for 1st up pass; Bit Size (BS) used for downlog and 2nd pass.  
 Logs recorded in real-time with depth zero at drill floor; final depth adjusted to have zero at sea floor for core compatibilit  
 Depth reference for this hole was the second pass of the first run; all other logs tied into that pass.


RUN 1			RUN 2		
SERVICE ORDER #:			SERVICE ORDER #:		
PROGRAM VERSION: 19C0-187			PROGRAM VERSION:		
FLUID LEVEL:			FLUID LEVEL:		
LOGGED INTERVAL	START	STOP	LOGGED INTERVAL	START	STOP

**EQUIPMENT DESCRIPTION**

RUN 1	RUN 2
<b>SURFACE EQUIPMENT</b>	
GSR-U 616008 WITM (EDTS)-A	

RUN 1	RUN 2
<b>DOWNHOLE EQUIPMENT</b>	
LEH-QT	32.79
LEH-QT 301	
AH-369	31.90
EDTC-B	31.46
EDTH-B 8303	

MDSB EDTC  
 Mud Tempe  
 CTEM  
 Gamma Ray  
 EFTB DIAG  
 TelStatus

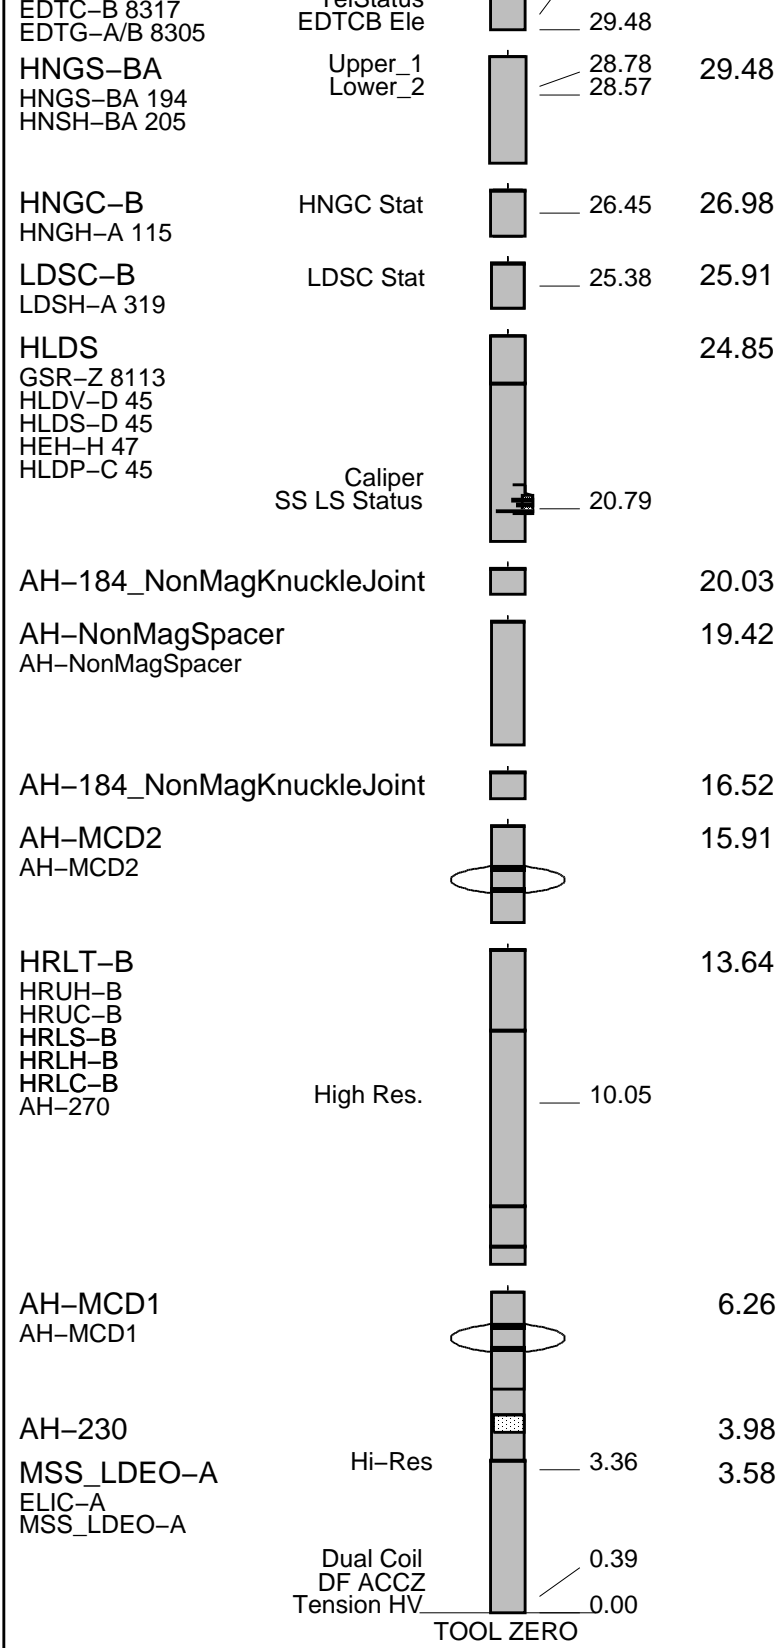

MAXIMUM STRING DIAMETER 3.75 IN  
 MEASUREMENTS RELATIVE TO TOOL ZERO  
 ALL LENGTHS IN METERS

Production String	(in)	(m)	Well Schematic	(m)	(in)	Casing String

Kelly Bushing Elevation


Derrick Floor Elevation

Mean Sea Level

-3173.0

-3173.0

-3162.2

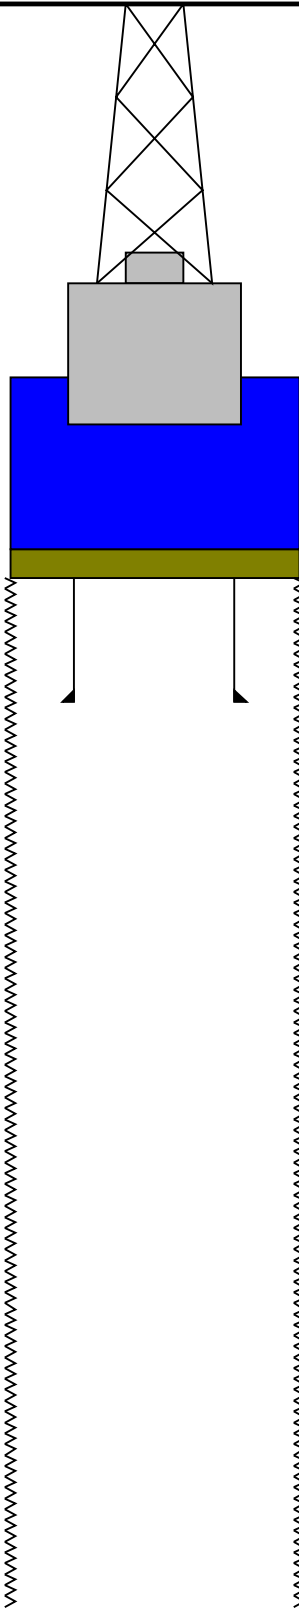

0.0

96.5

529.8

5.500

4.000

9.875

Sea Bed

Bit

Total Depth - Driller

**Schlumberger**

**Downlog**

MAXIS Field Log

**Input DLIS Files**

DEFAULT	Flip_MSS_LDEO_HRLA_018LUP	PRODUCER	26-Sep-2014 09:46	3557.9 M	3120.4 M
---------	---------------------------	----------	-------------------	----------	----------

**Output DLIS Files**

DEFAULT	MSS_LDEO_HRLA_LDL_042PUP	FN:59	PRODUCER	26-Sep-2014 11:37	382.1 M	-11.6 M
CLIENT	MSS_LDEO_HRLA_LDL_042PUC	FN:60	CUSTOMER	26-Sep-2014 11:37	382.1 M	-11.6 M

**OP System Version: 19C0-187**

MSS_LDEO-A	19C0-187	HRLT-B	19C0-187
HLDS	19C0-187	LDSC-B	19C0-187
HNGC-B	19C0-187	HNGS-BA	19C0-187
EDTC-B	SKK-5169-EDTCB		

PIP SUMMARY

Time Mark Every 60 S

**HNGS Spectroscopy Gamma Ray (HSGR)**  
(GAPI) 0 40

**Area1**  
From HCGR to HSGR

**HNGS Borehole Potassium (HBHK)**  
-0.05 (----) 0.05

**HNGS Computed Gamma Ray (HCGR)**  
(GAPI) 0 40

**Calibrated Downhole Force (CDF) (LBF)**  
3000 0


**HNGS Uranium (HURA)**  
(PPM) -5 10


**HLDS Caliper (LCAL)**  
(IN) 0 20

**Tension (TENS) (LBF)**  
10000 0



**HNGS Thorium (HTHO)**  
(PPM) 5 25


**HNGS Potassium (HFK)**  
(PPM) -0.01 (----) 0.04

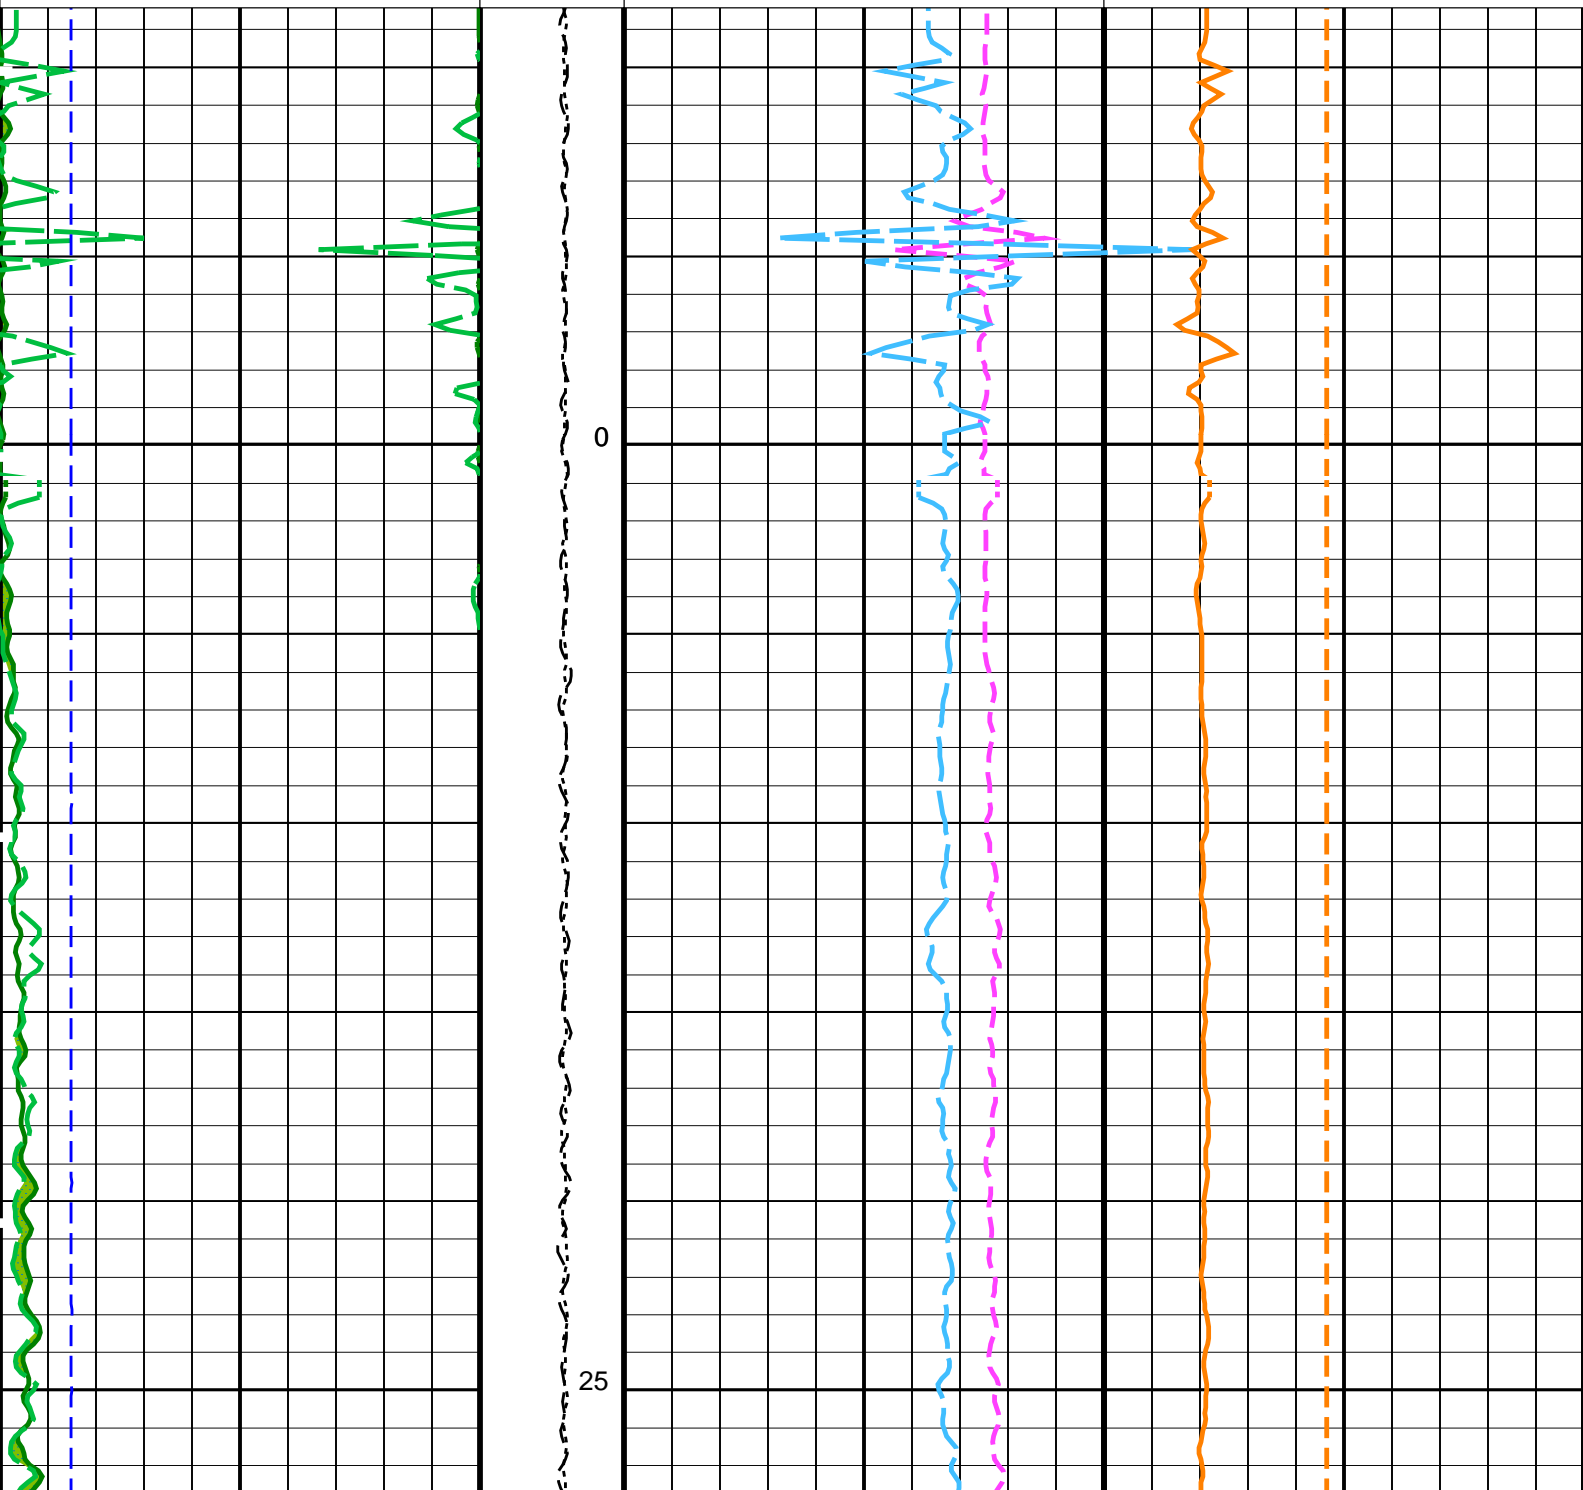


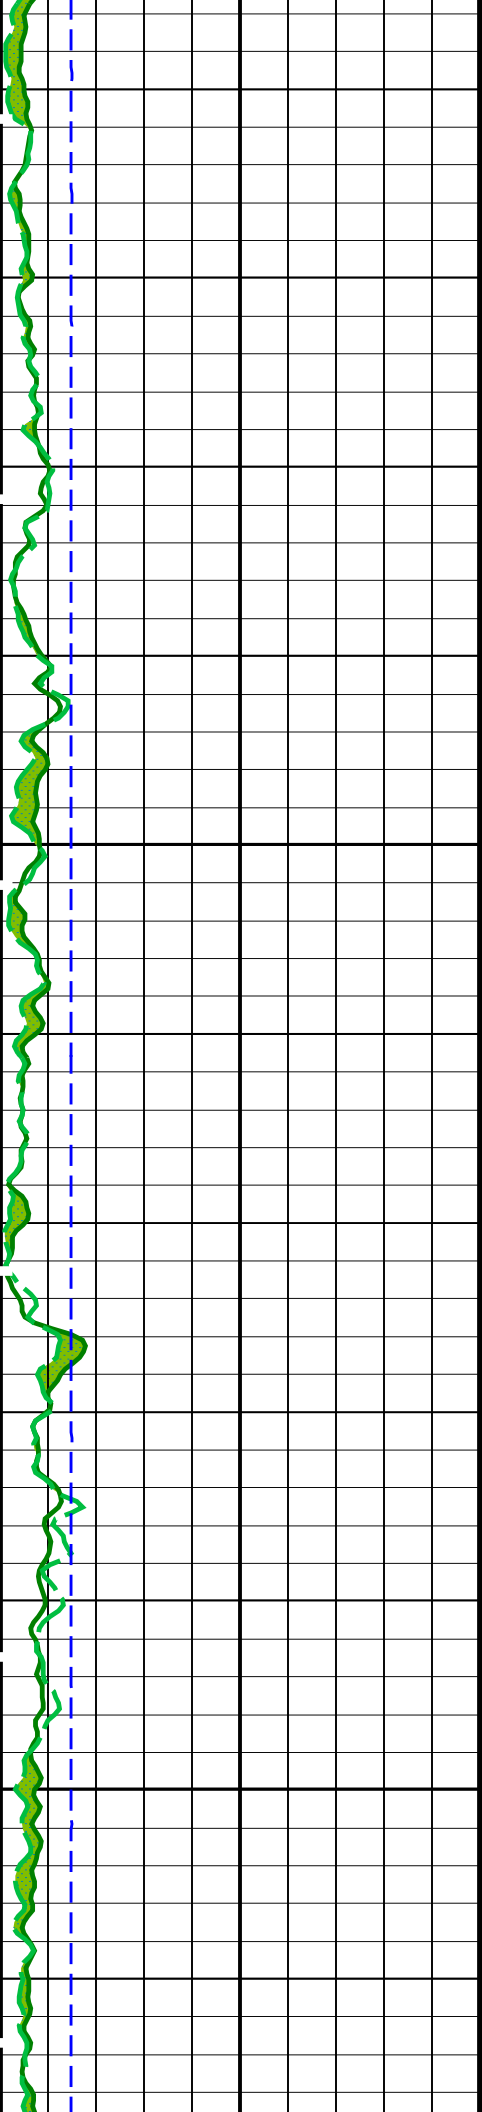


50  
75

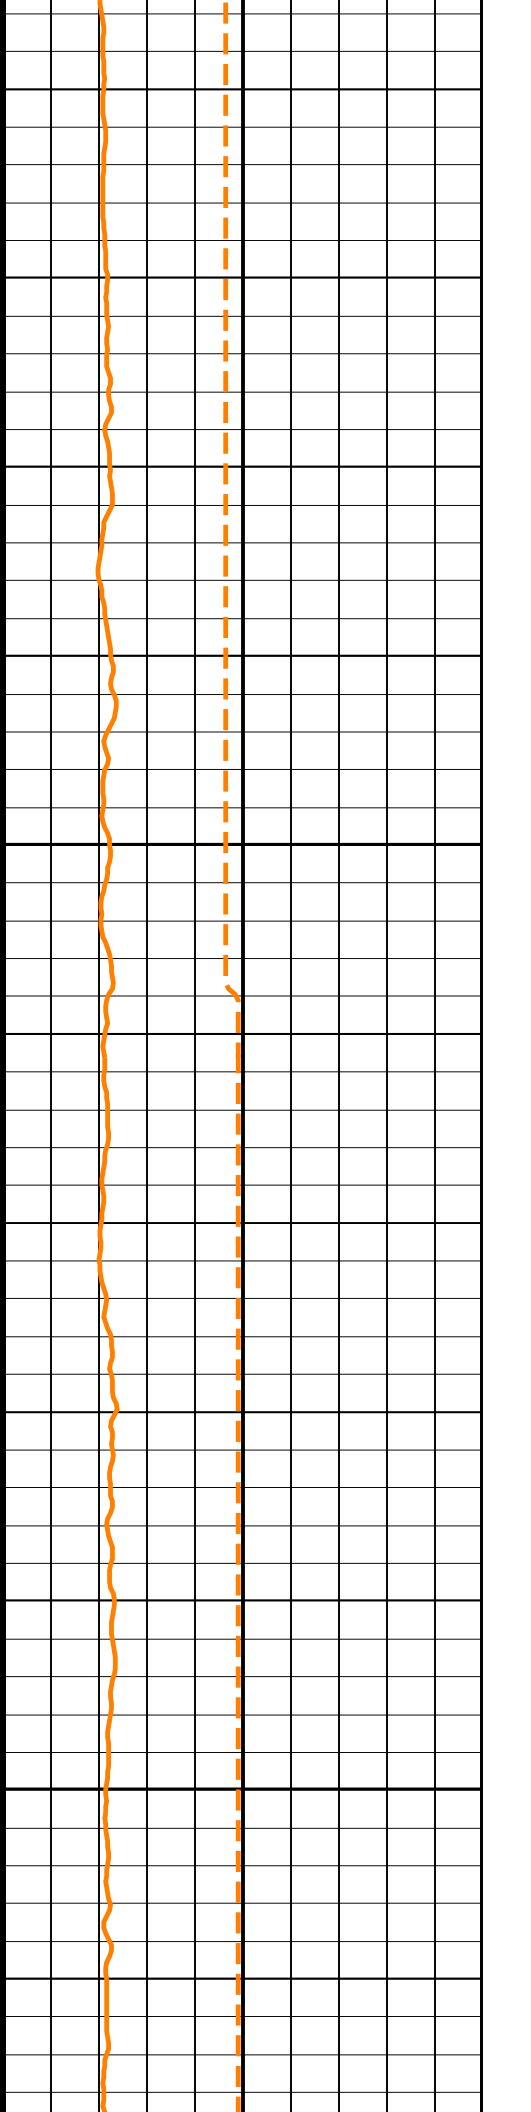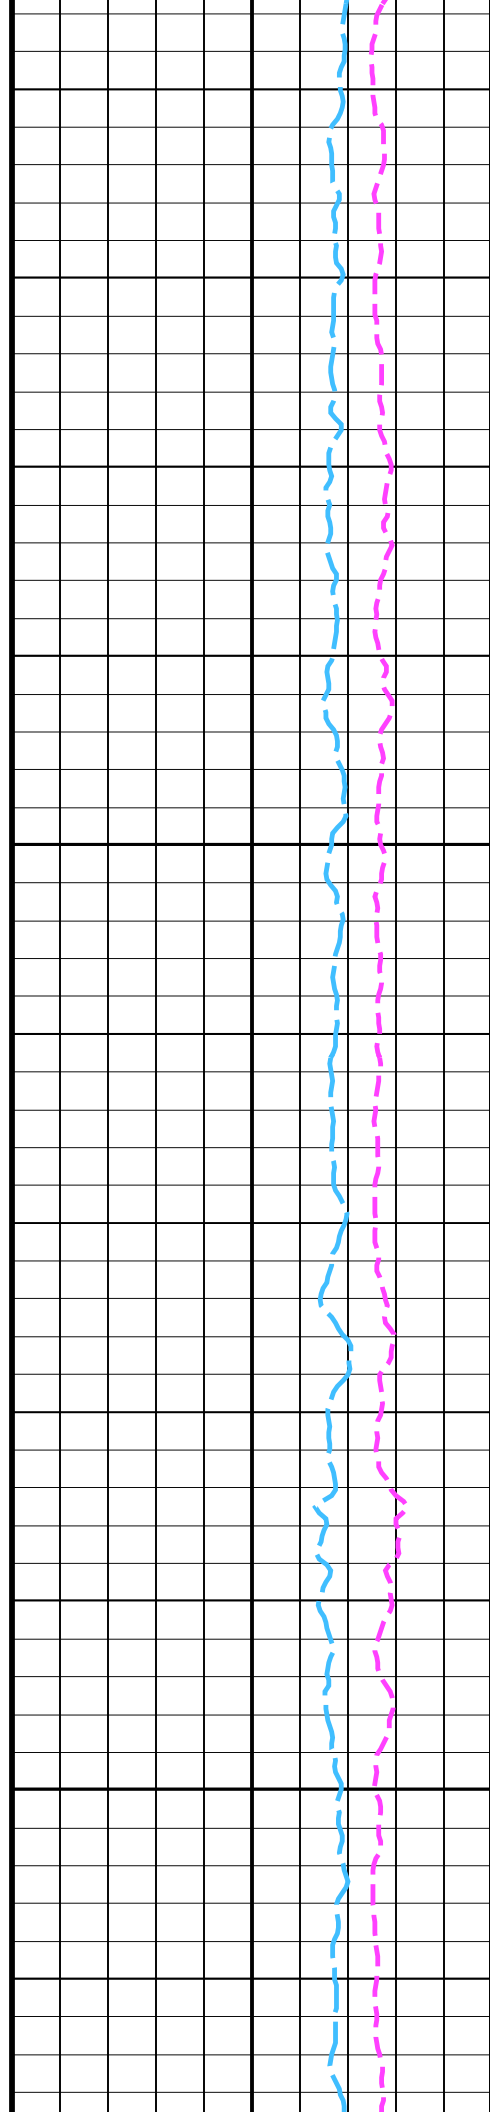


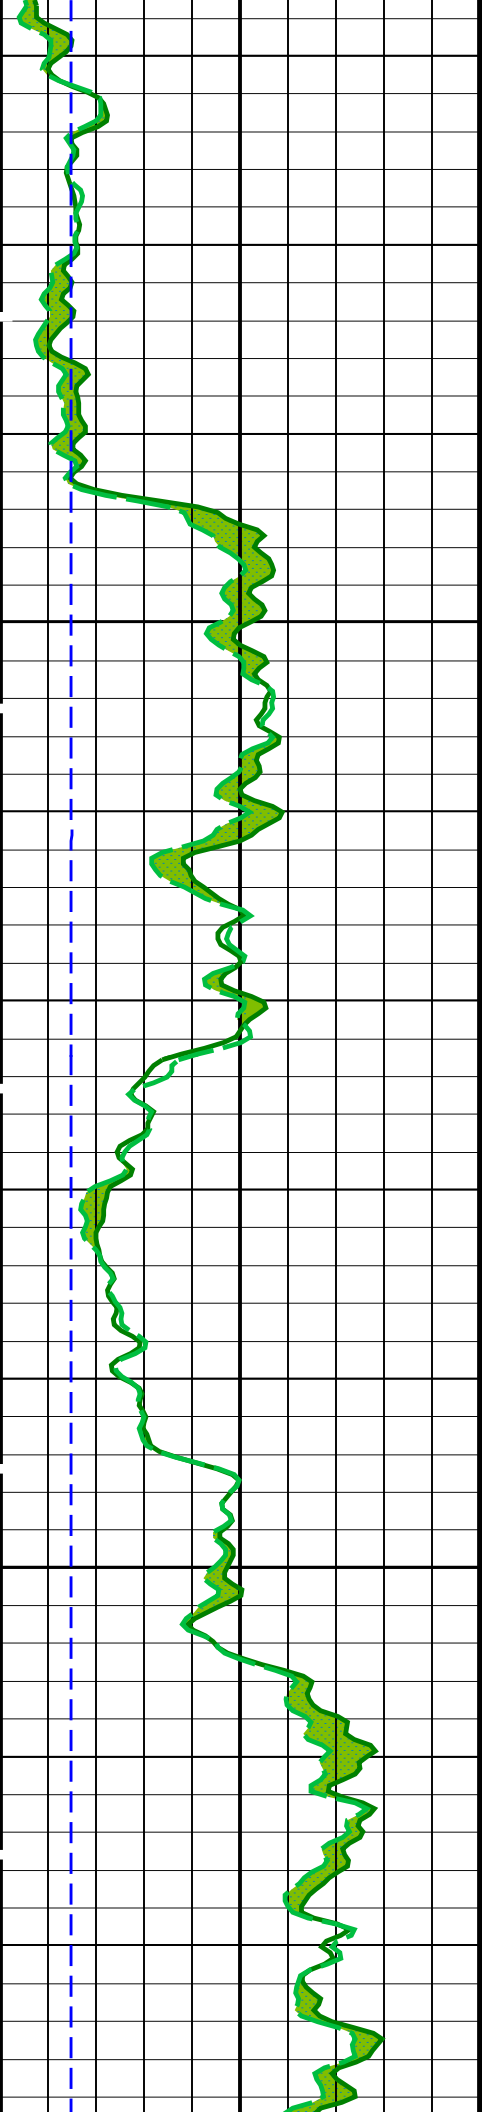



100  
125

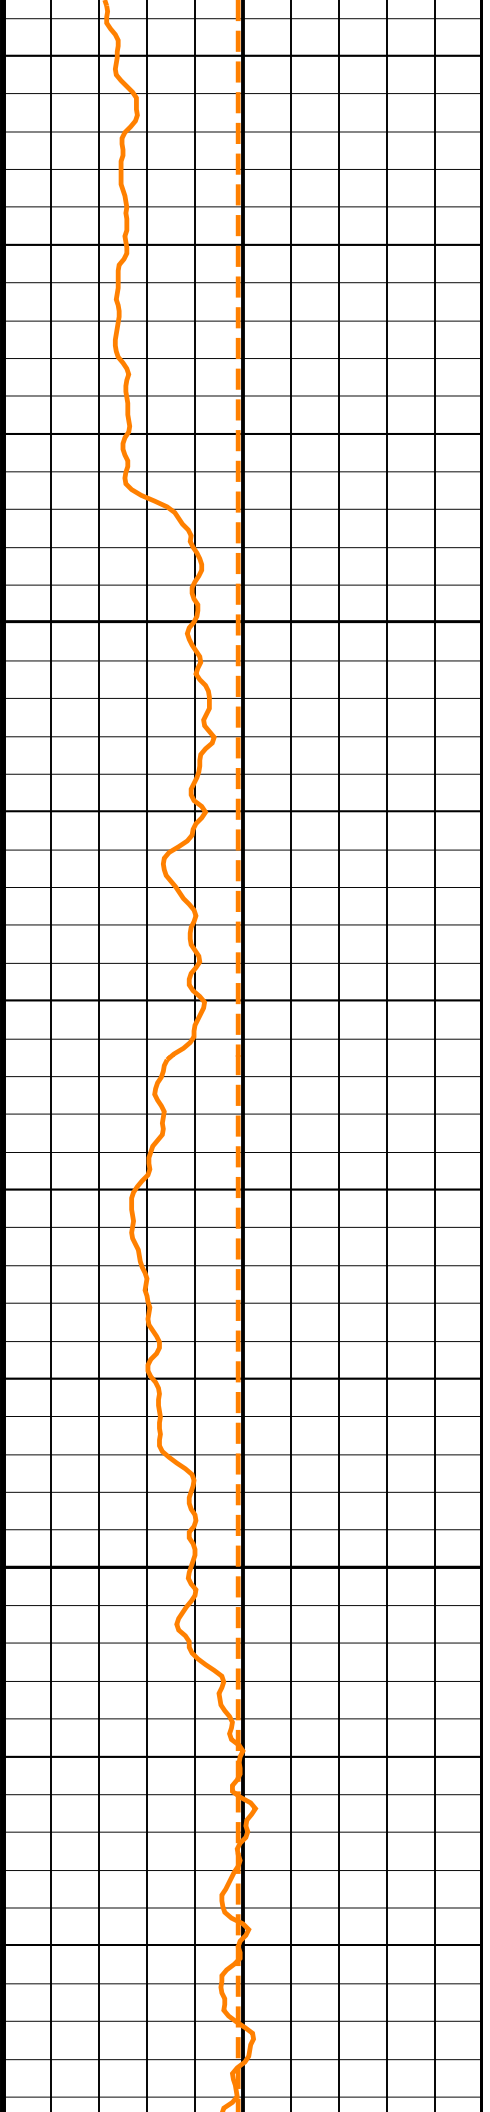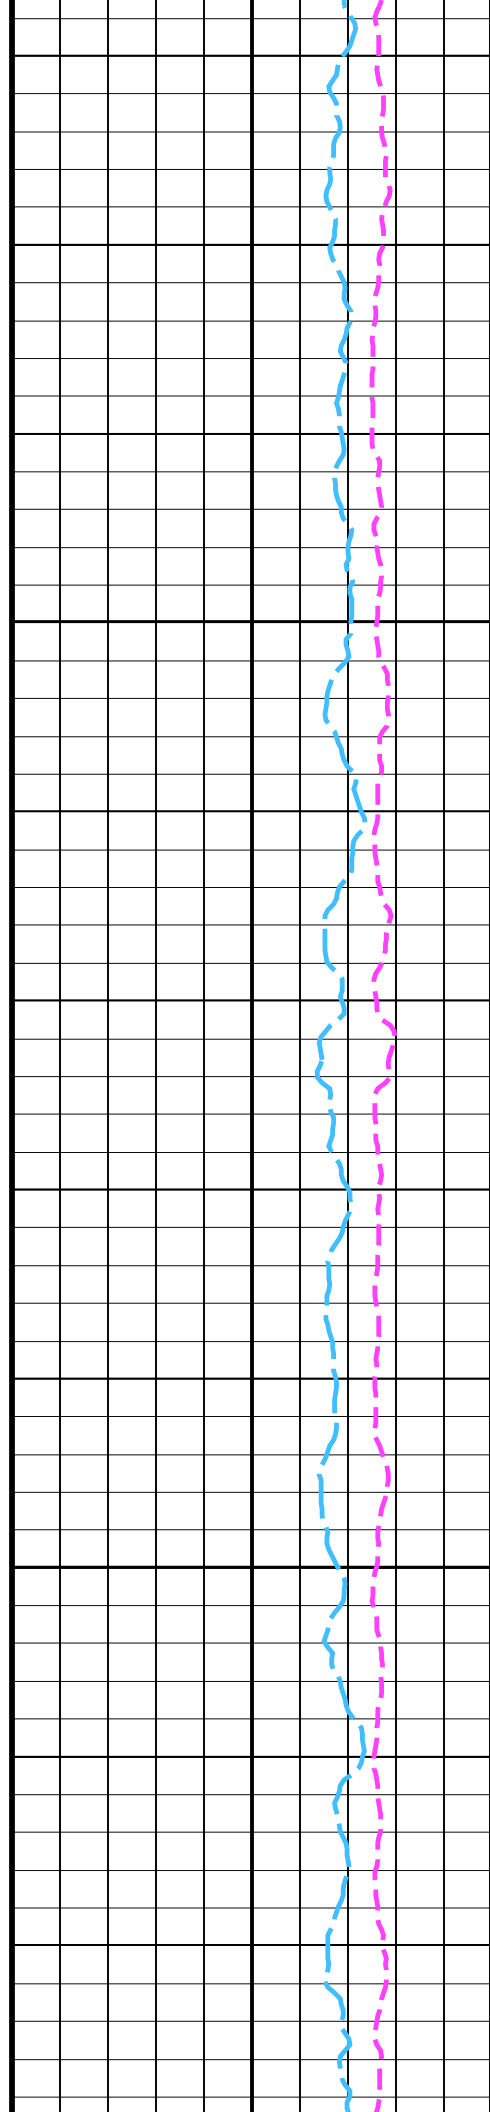






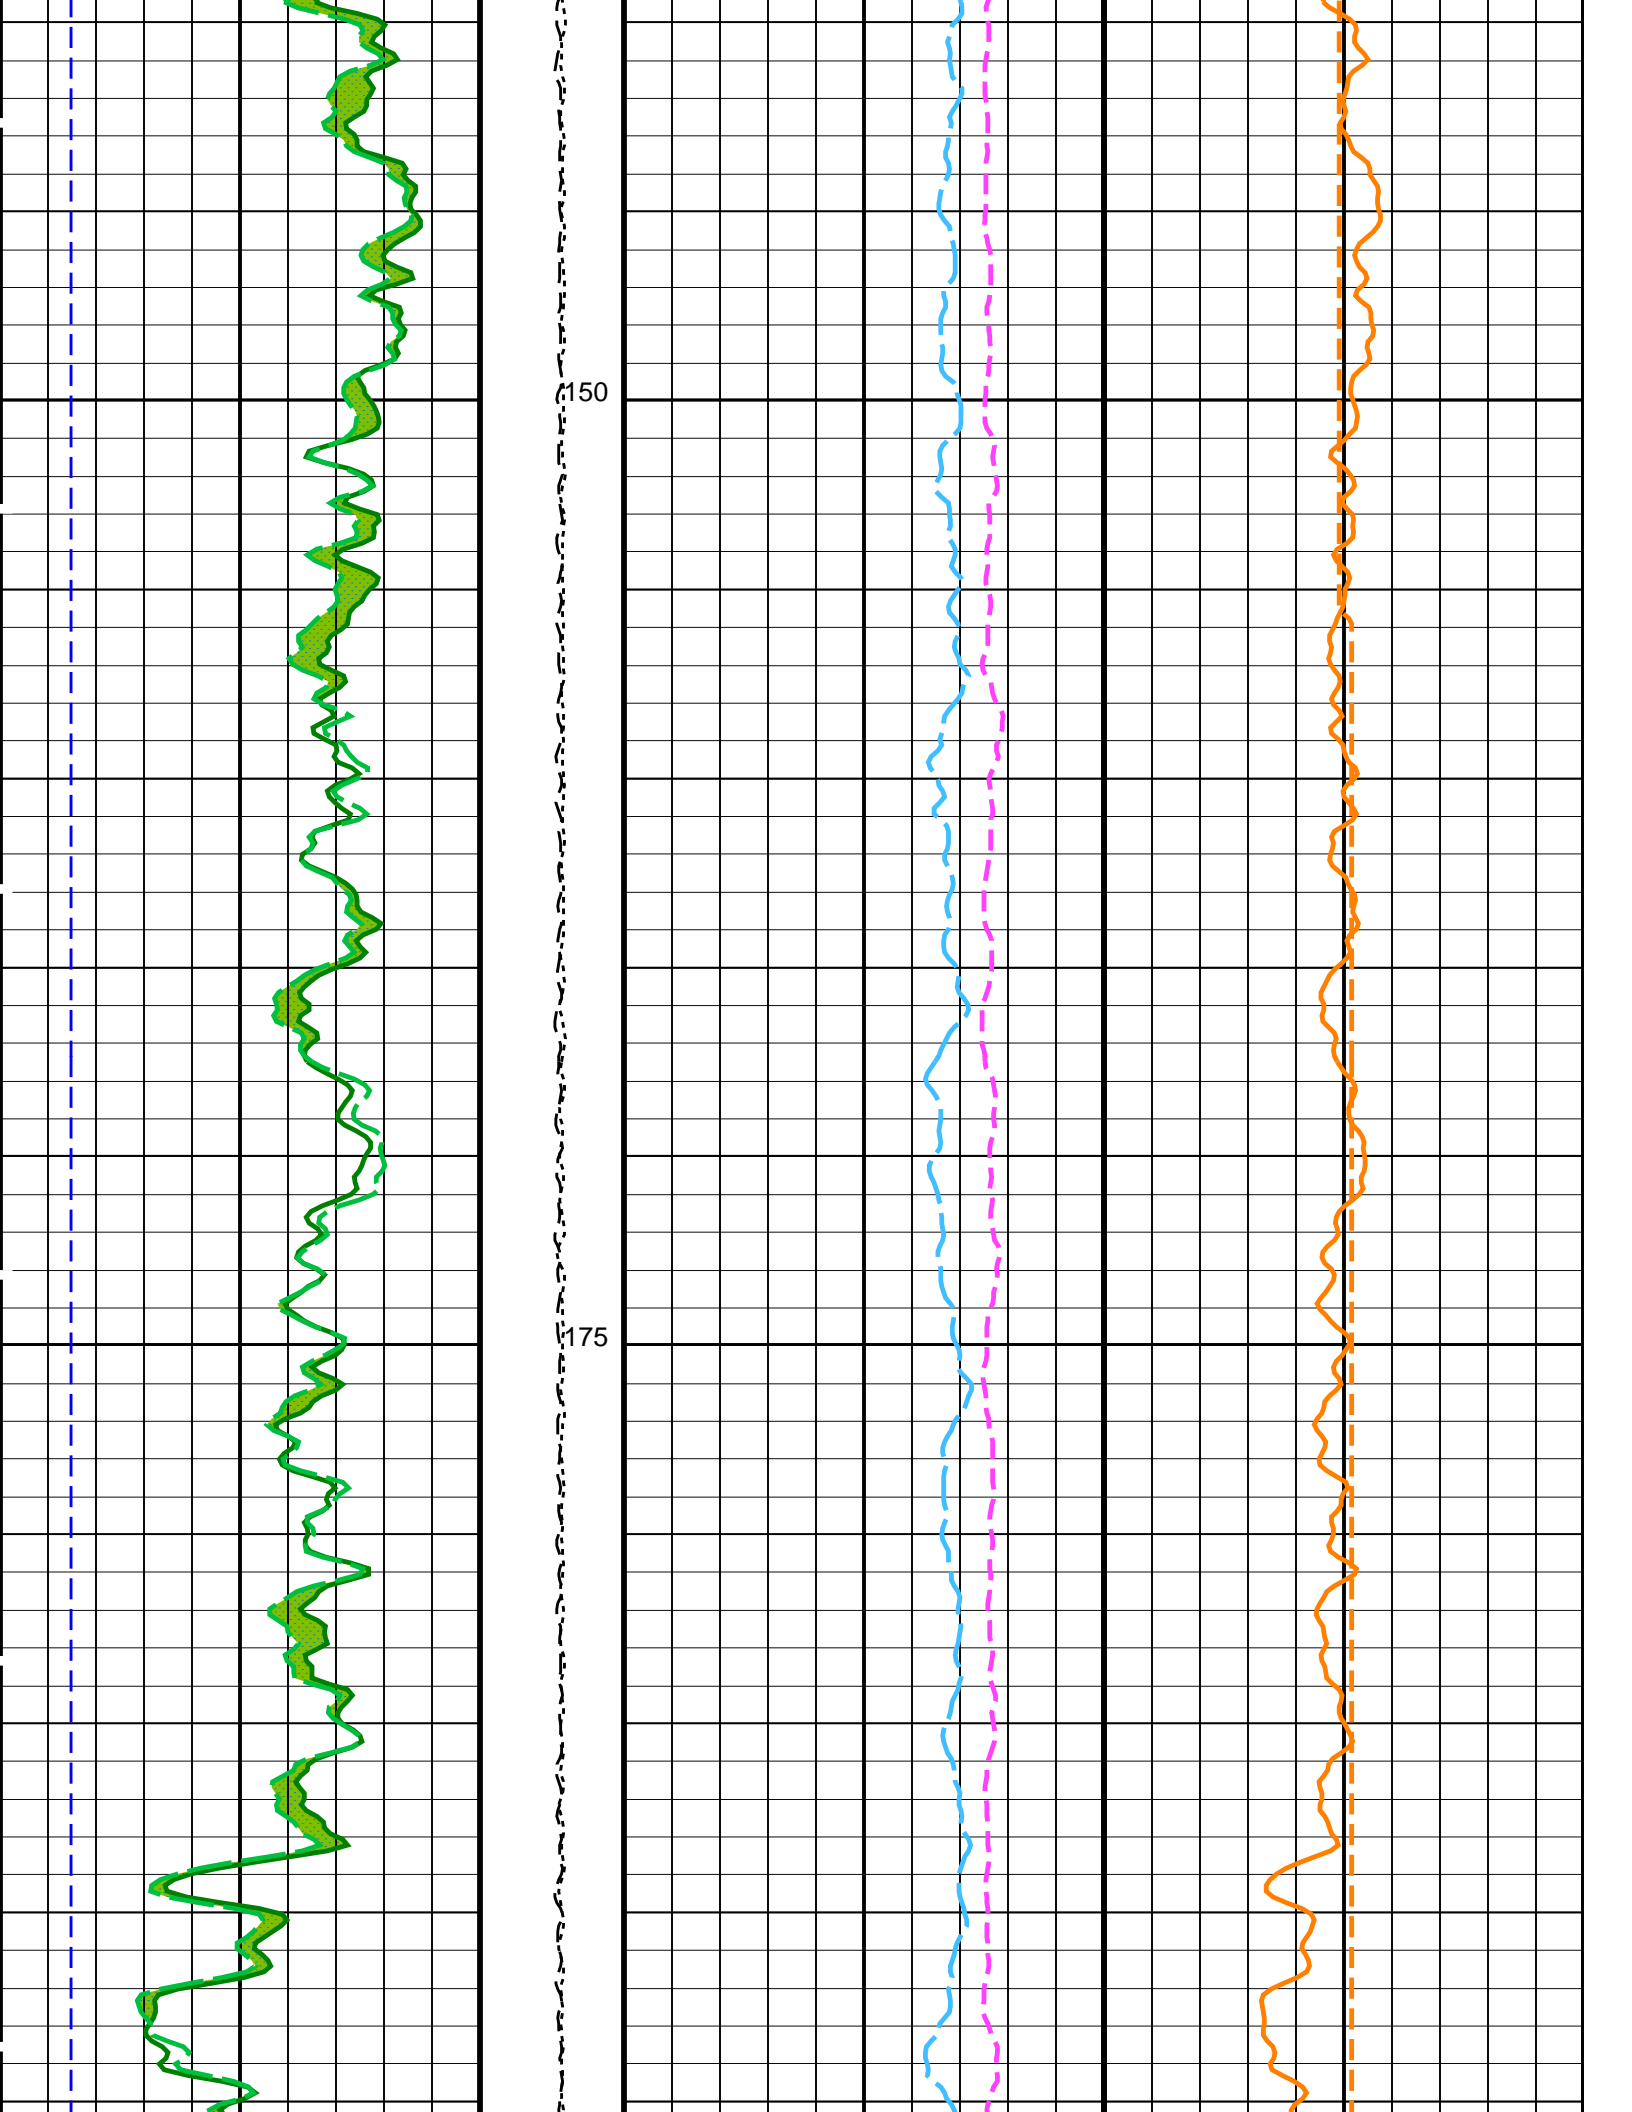

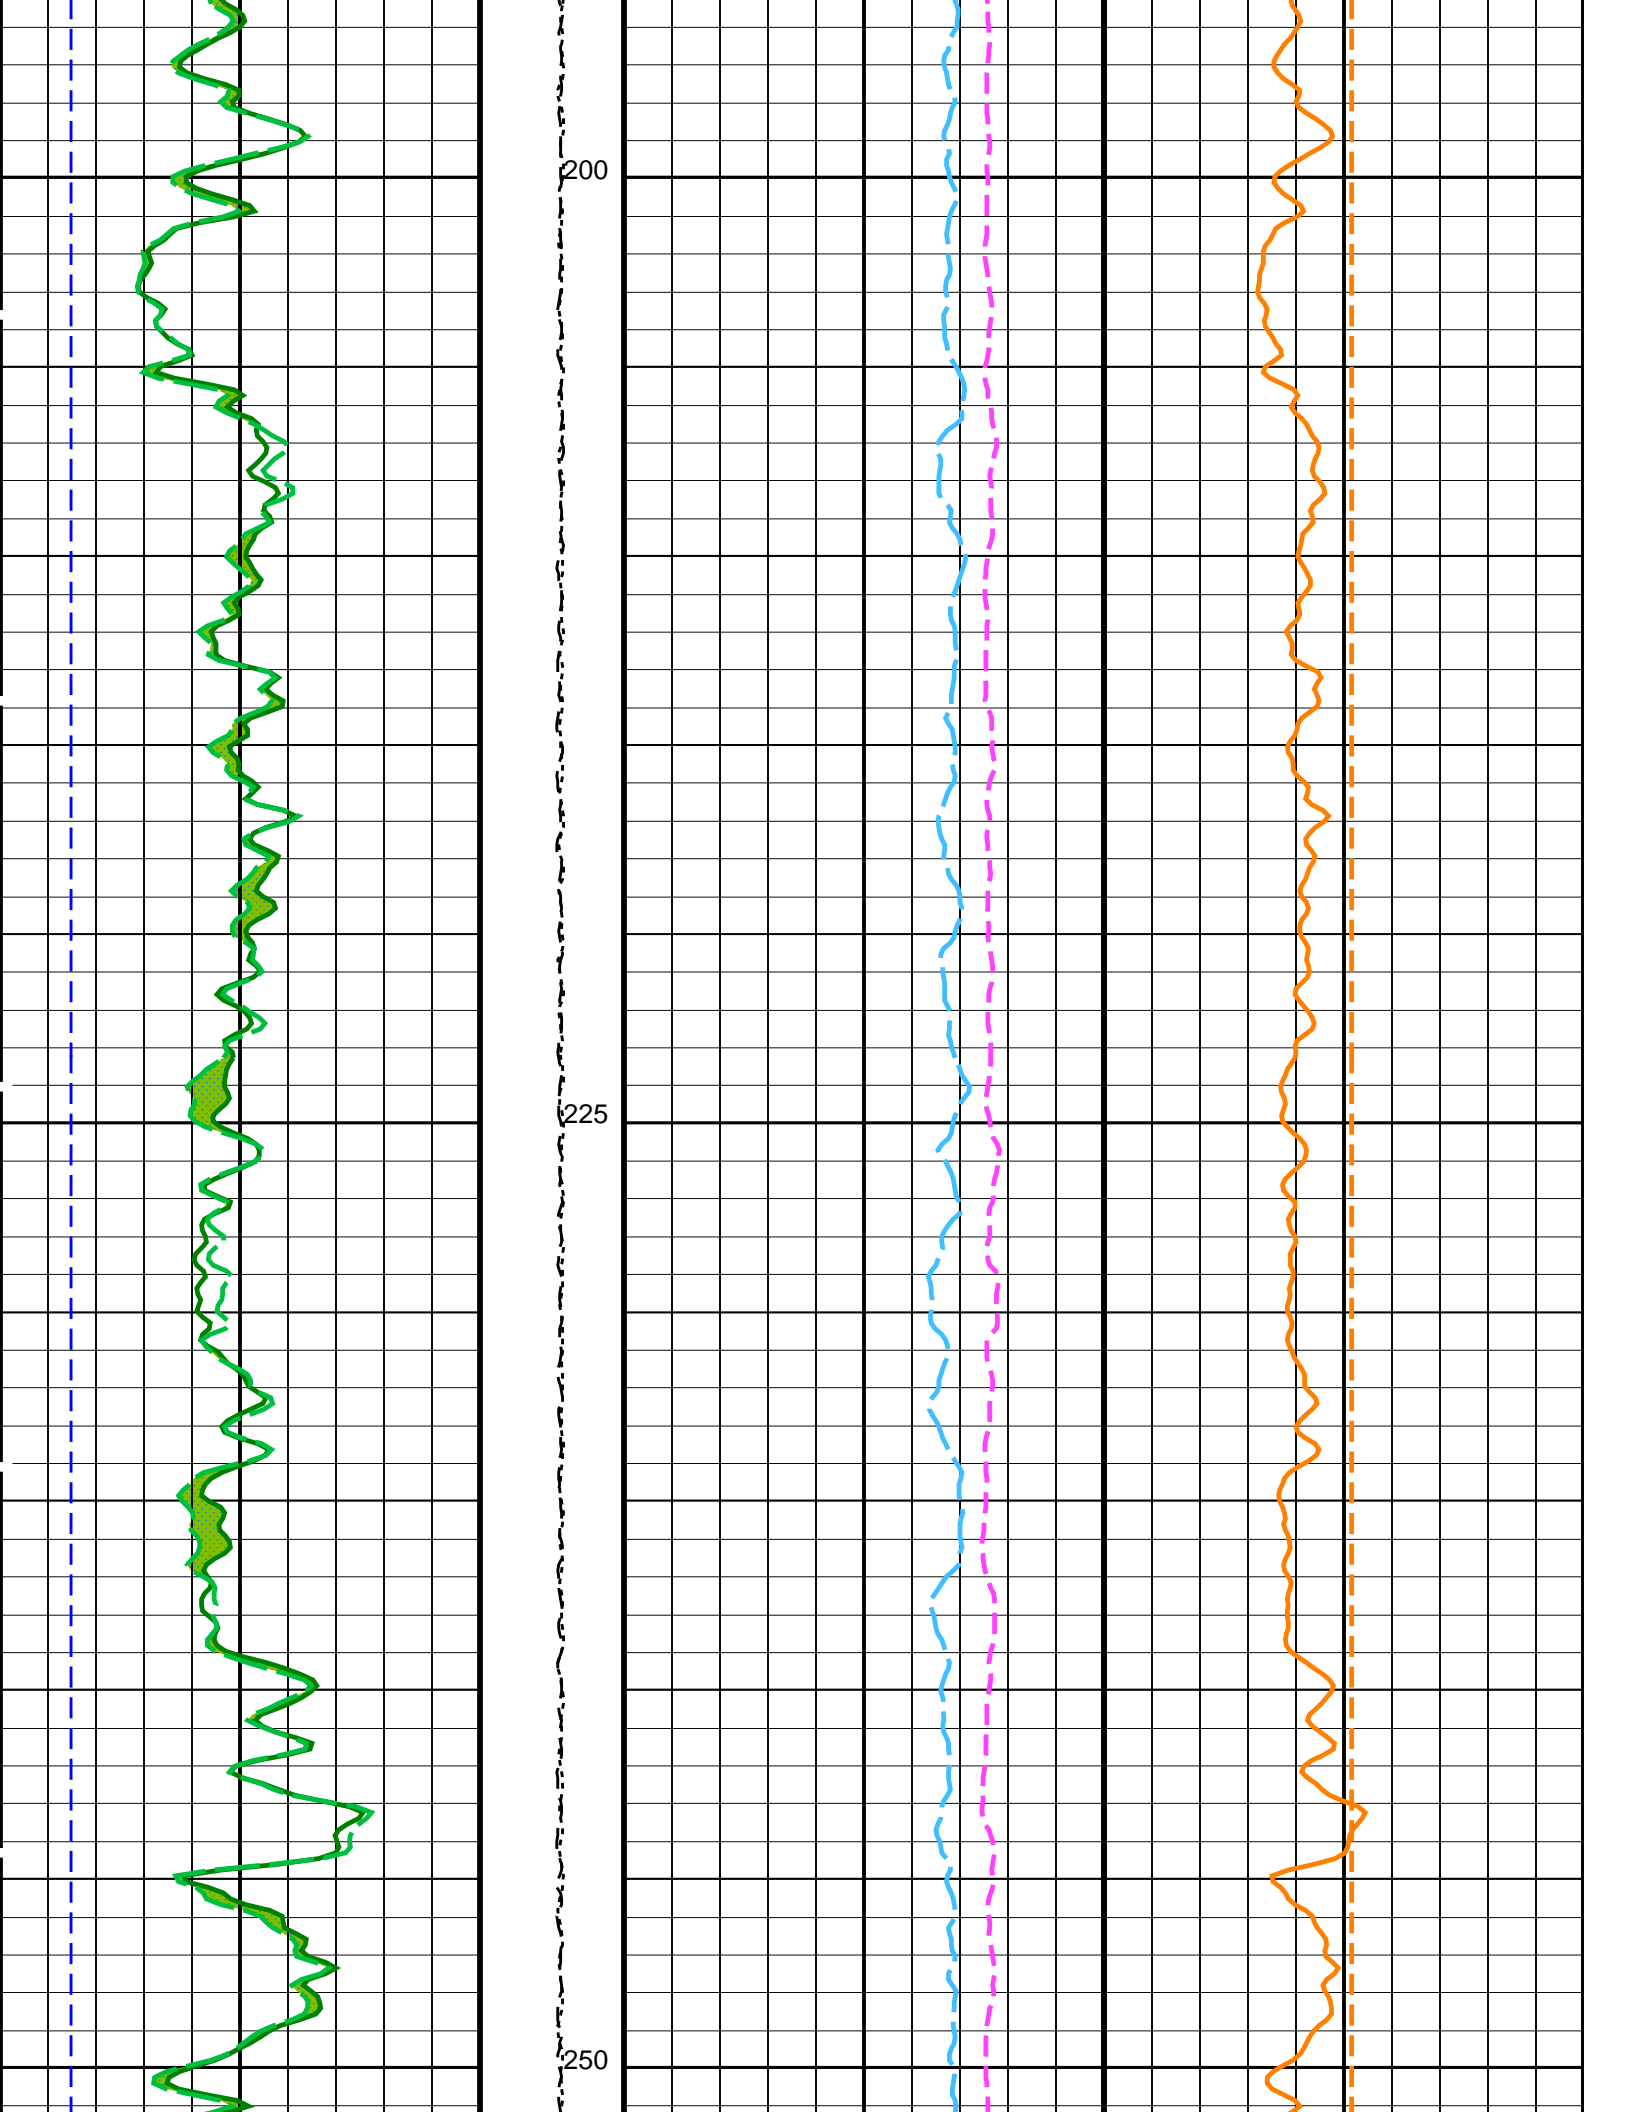

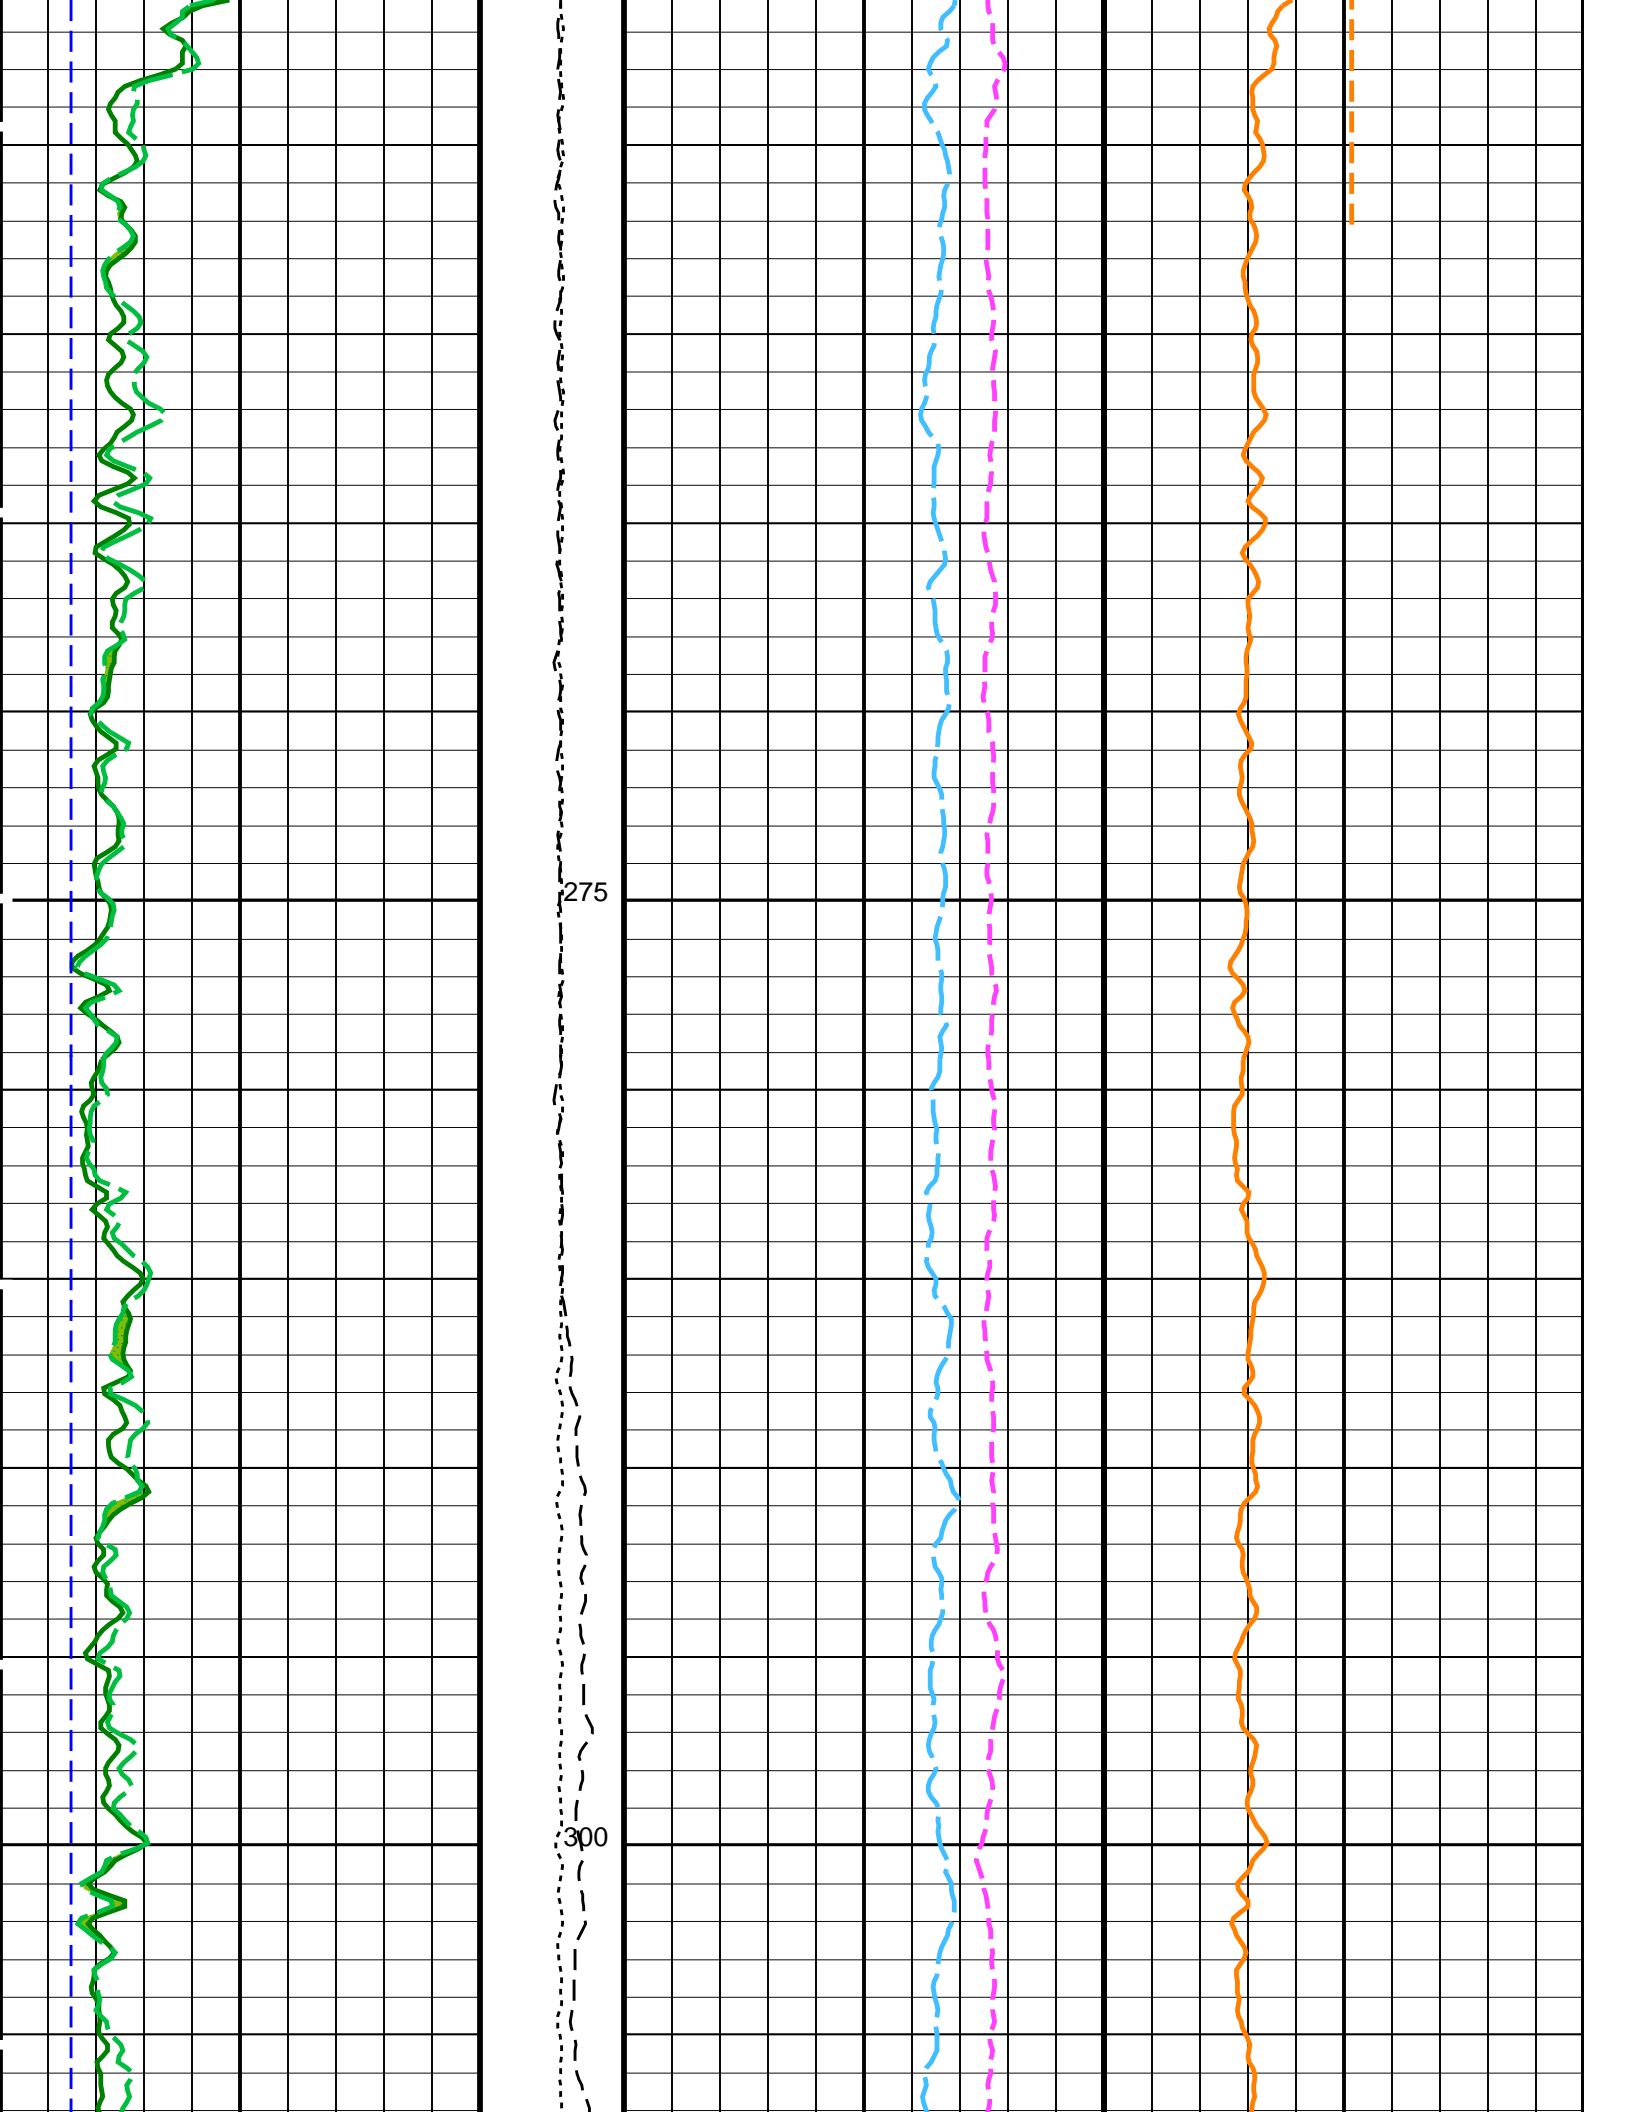

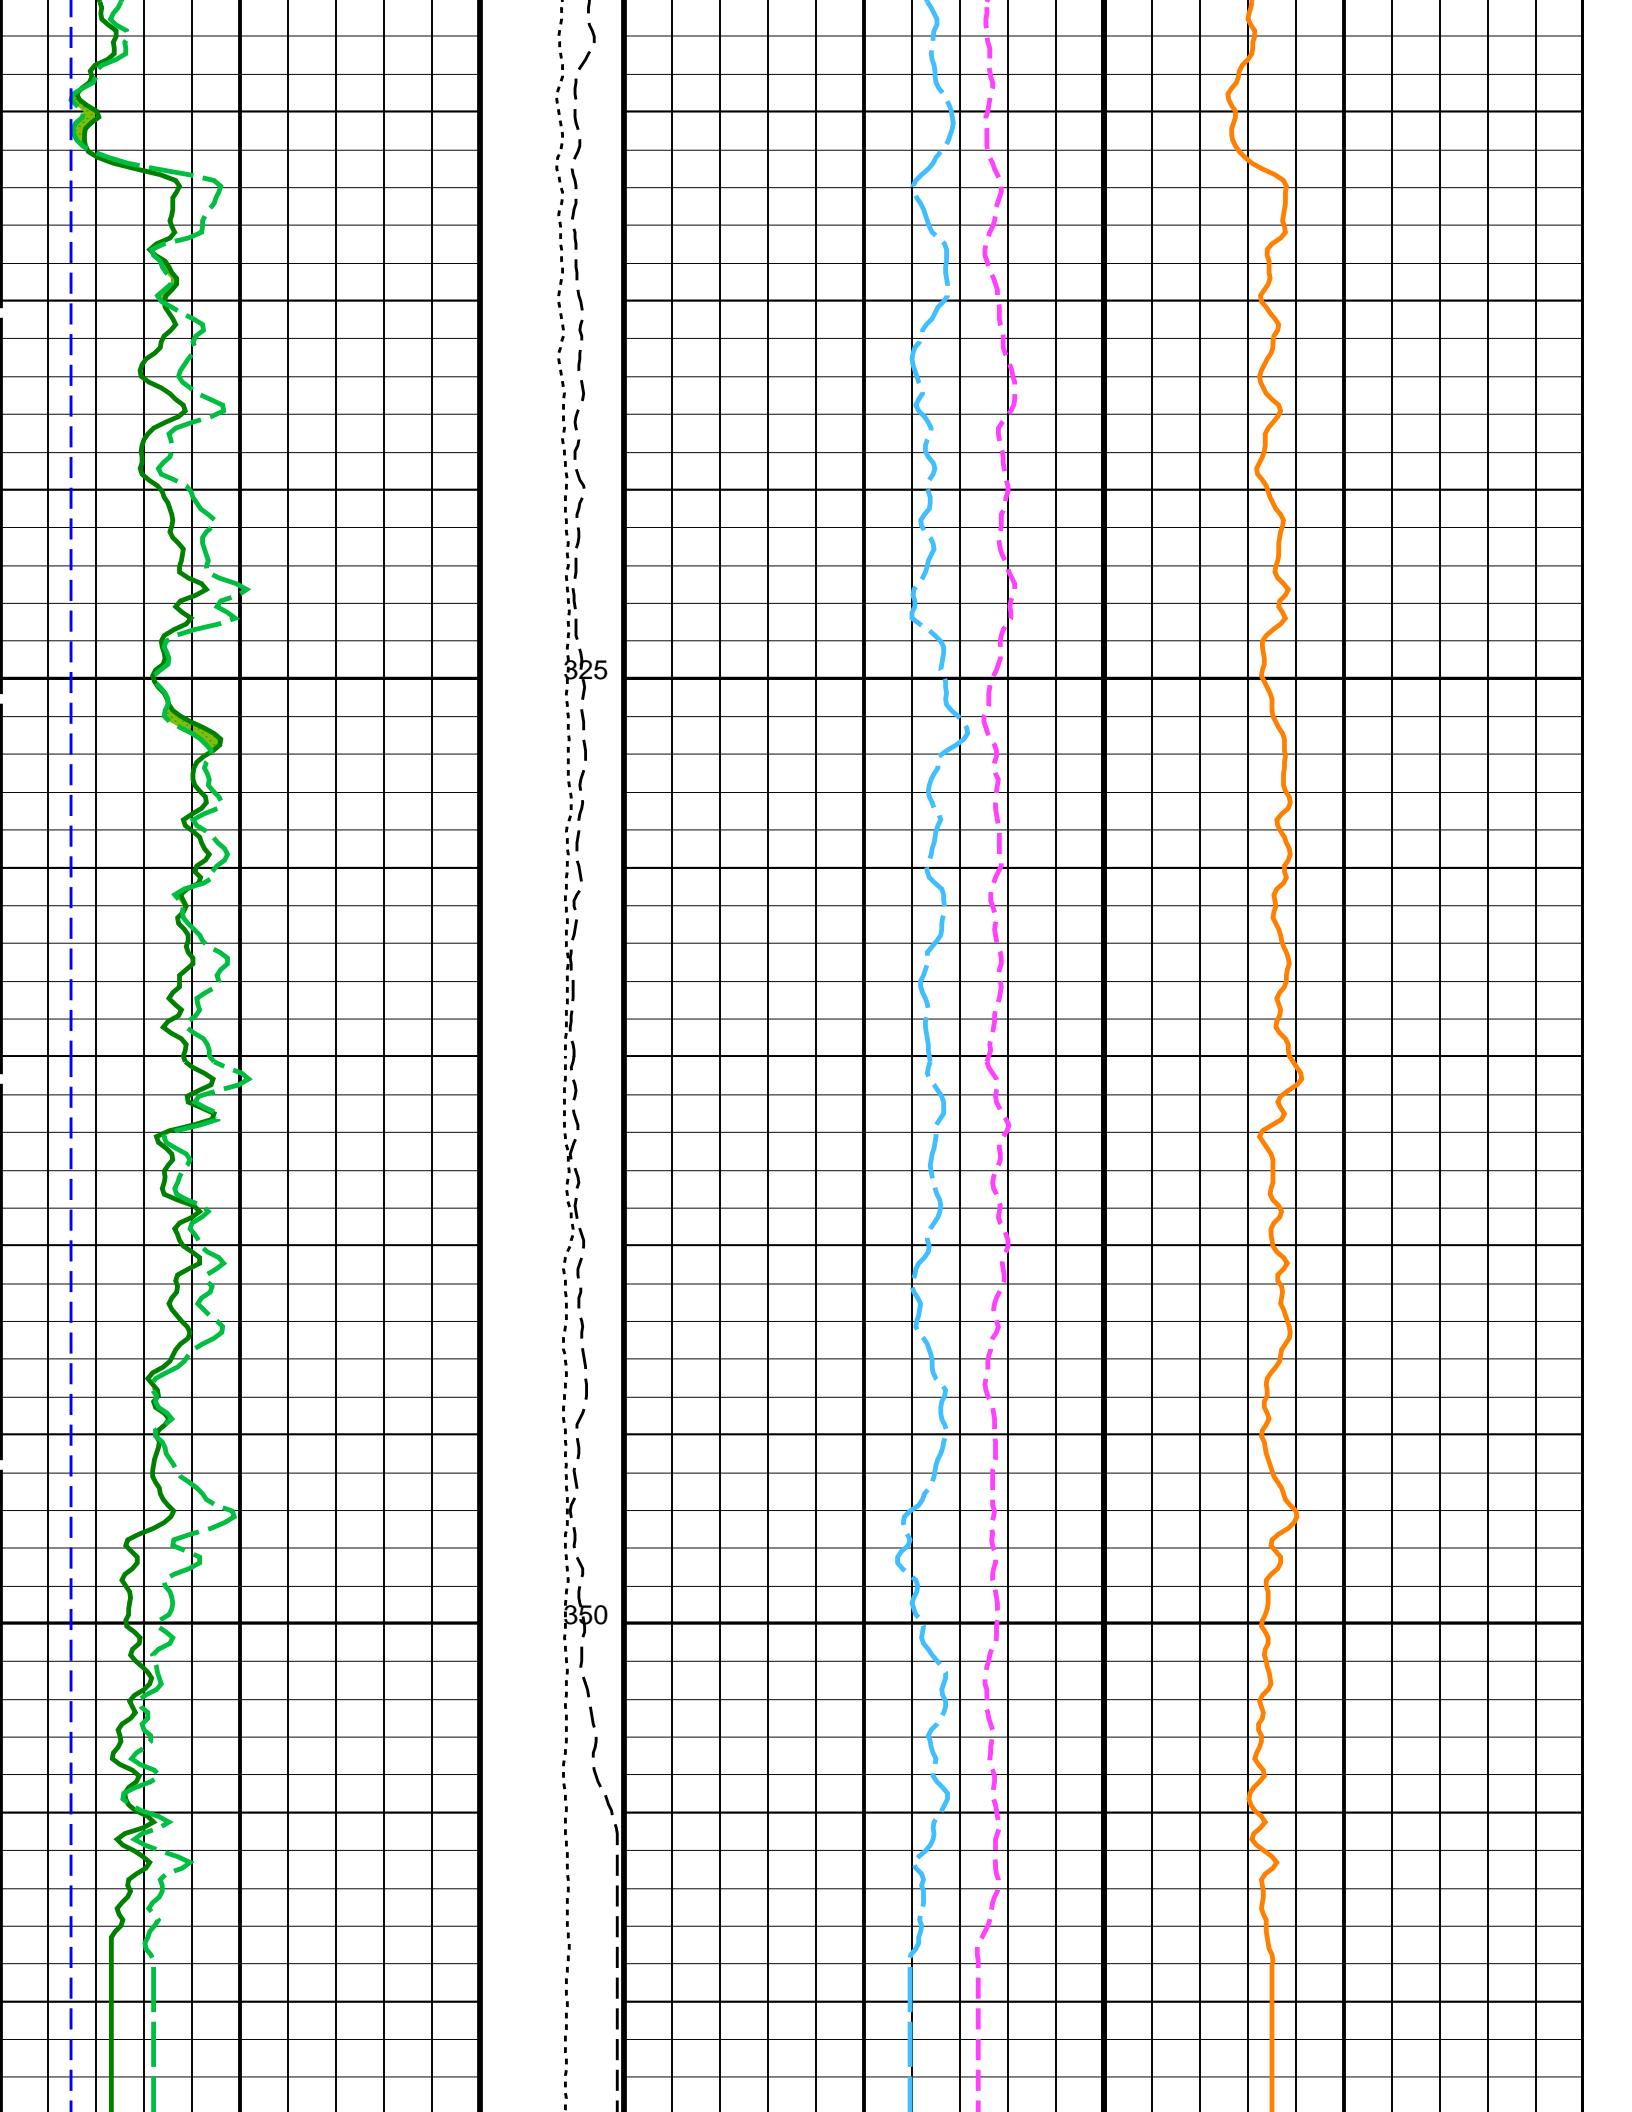

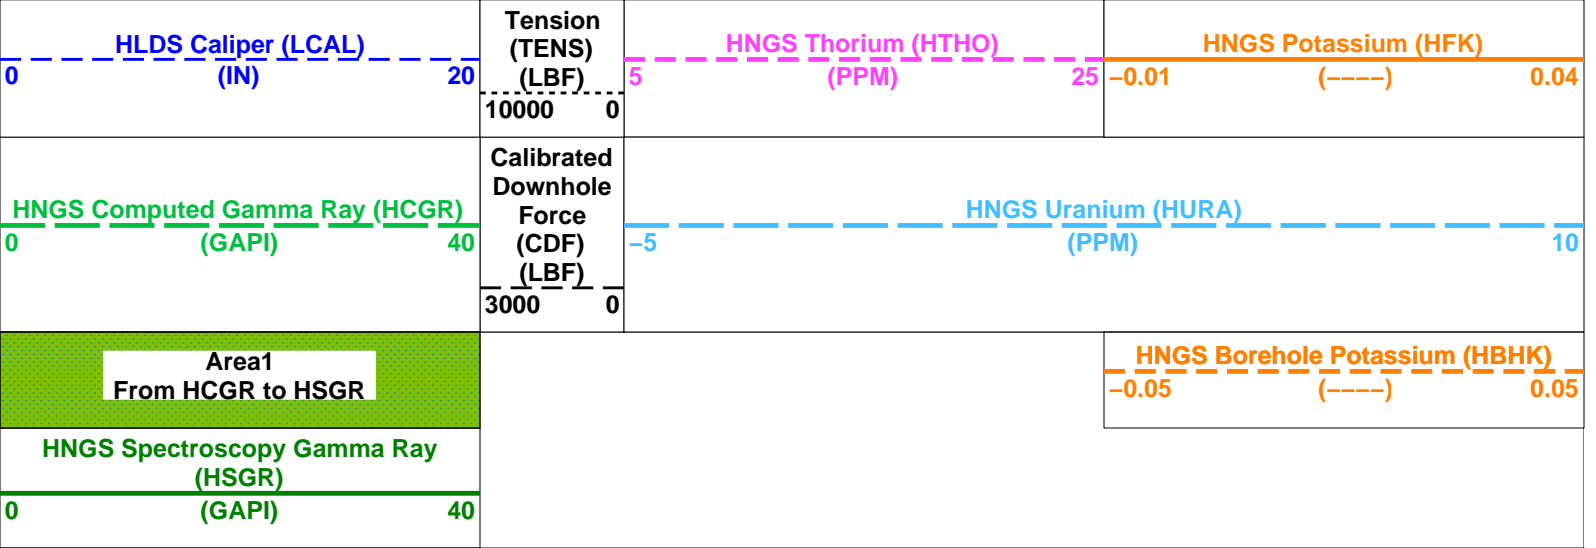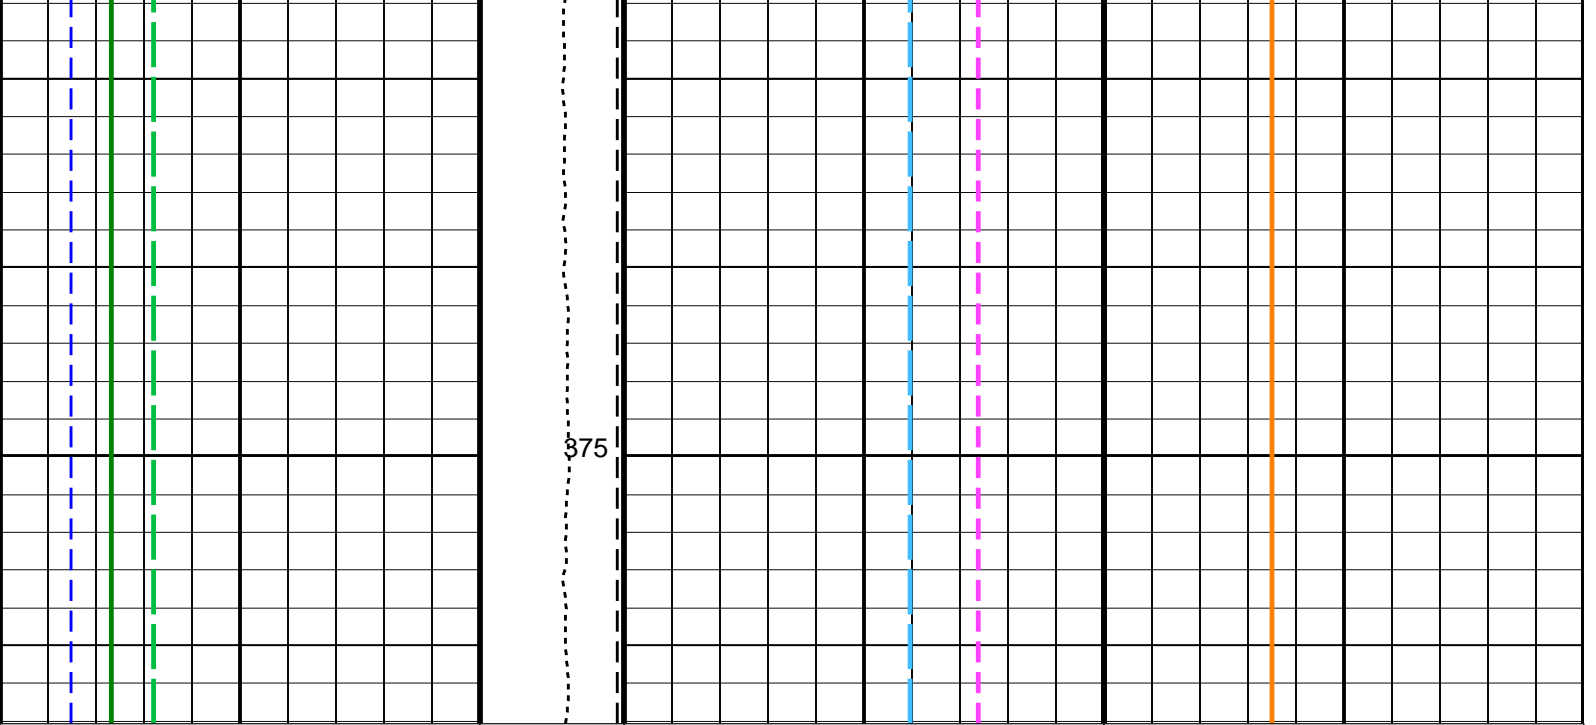

PIP SUMMARY

Time Mark Every 60 S

Parameters

DLIS Name	Description	Value
	HRLT-B: High Resolution Laterolog Array - B	
BHS	Borehole Status	OPEN
GCSE	Generalized Caliper Selection	BS
	HNGS-BA: Hostile Natural Gamma Ray Sonde	
BAR1	HNGS Detector 1 Barite Constant	1
BAR2	HNGS Detector 2 Barite Constant	1
BHK	HNGS Borehole Potassium Correction Concentration	0
BHS	Borehole Status	OPEN
CSD1	Inner Casing Outer Diameter	0 IN
CSD2	Outer Casing Outer Diameter	0 IN
CSW1	Inner Casing Weight	0 LB/F
CSW2	Outer Casing Weight	0 LB/F
DBCC	HNGS Barite Constant Correction Flag	NONE
GCSE	Generalized Caliper Selection	BS
H1P	HNGS Detector 1 Allow/Disallow In Processing	ALLOW
H2P	HNGS Detector 2 Allow/Disallow In Processing	ALLOW
HABK	HNGS Borehole Potassium Running Average	-0.00366021
HALF	HNGS Alpha Filter Length	60 IN
HCRB	HNGS Apply Borehole Potassium Correction	NONE
HMWM	Mud Weighting Material	BARI
HNPE	HNGS Processing Enable	YES
S1BI	HNGS Detector 1 Calibration Bismuth Count Rate	1.3 CPS
S2BI	HNGS Detector 2 Calibration Bismuth Count Rate	1.3 CPS
SGRC	HNGS Standard Gamma-Ray Correction Flag	YES
TPOS	Tool Position	ECCE

VBA1	HNGS Detector 1 Variable Barite Factor Running Average	1.02657	
VBA2	HNGS Detector 2 Variable Barite Factor Running Average	1.0199	
BHS	EDTC-B: Enhanced DTS Cartridge		
GCSE	Borehole Status	OPEN	
	Generalized Caliper Selection	BS	
	System and Miscellaneous		
BS	Bit Size	9.875	IN
DFD	Drilling Fluid Density	1.03	G/C3
DO	Depth Offset for Playback	-3171.5	M
PP	Playback Processing	RECOMPUTE	

Format: HNGSYields    Vertical Scale: 1:200    Graphics File Created: 26-Sep-2014 11:37

### OP System Version: 19C0-187

MSS_LDEO-A	19C0-187	HRLT-B	19C0-187
HLDS	19C0-187	LDSC-B	19C0-187
HNGC-B	19C0-187	HNGS-BA	19C0-187
EDTC-B	SKK-5169-EDTCB		

### Input DLIS Files

DEFAULT	Flip_MSS_LDEO_HRLA_018LUP	PRODUCER	26-Sep-2014 09:46	3557.9 M	3120.4 M
---------	---------------------------	----------	-------------------	----------	----------

### Output DLIS Files

DEFAULT	MSS_LDEO_HRLA_LDL_042PUP	FN:59	PRODUCER	26-Sep-2014 11:37	
CLIENT	MSS_LDEO_HRLA_LDL_042PUC	FN:60	CUSTOMER	26-Sep-2014 11:37	



**First Pass**

MAXIS Field Log

### Input DLIS Files

DEFAULT	MSS_LDEO_HRLA_LDL_008LUP	FN:8	PRODUCER	23-Sep-2014 06:10	3543.3 M	3310.4 M
---------	--------------------------	------	----------	-------------------	----------	----------

### Output DLIS Files

DEFAULT	MSS_LDEO_HRLA_LDL_032PUP	FN:39	PRODUCER	26-Sep-2014 11:23	372.6 M	139.9 M
CLIENT	MSS_LDEO_HRLA_LDL_032PUC	FN:40	CUSTOMER	26-Sep-2014 11:23	372.6 M	139.9 M


### OP System Version: 19C0-187




MSS_LDEO-A	19C0-187	HRLT-B	19C0-187
HLDS	19C0-187	LDSC-B	19C0-187
HNGC-B	19C0-187	HNGS-BA	19C0-187
EDTC-B	SKK-5169-EDTCB		

### PIP SUMMARY






Calibrated Downhole

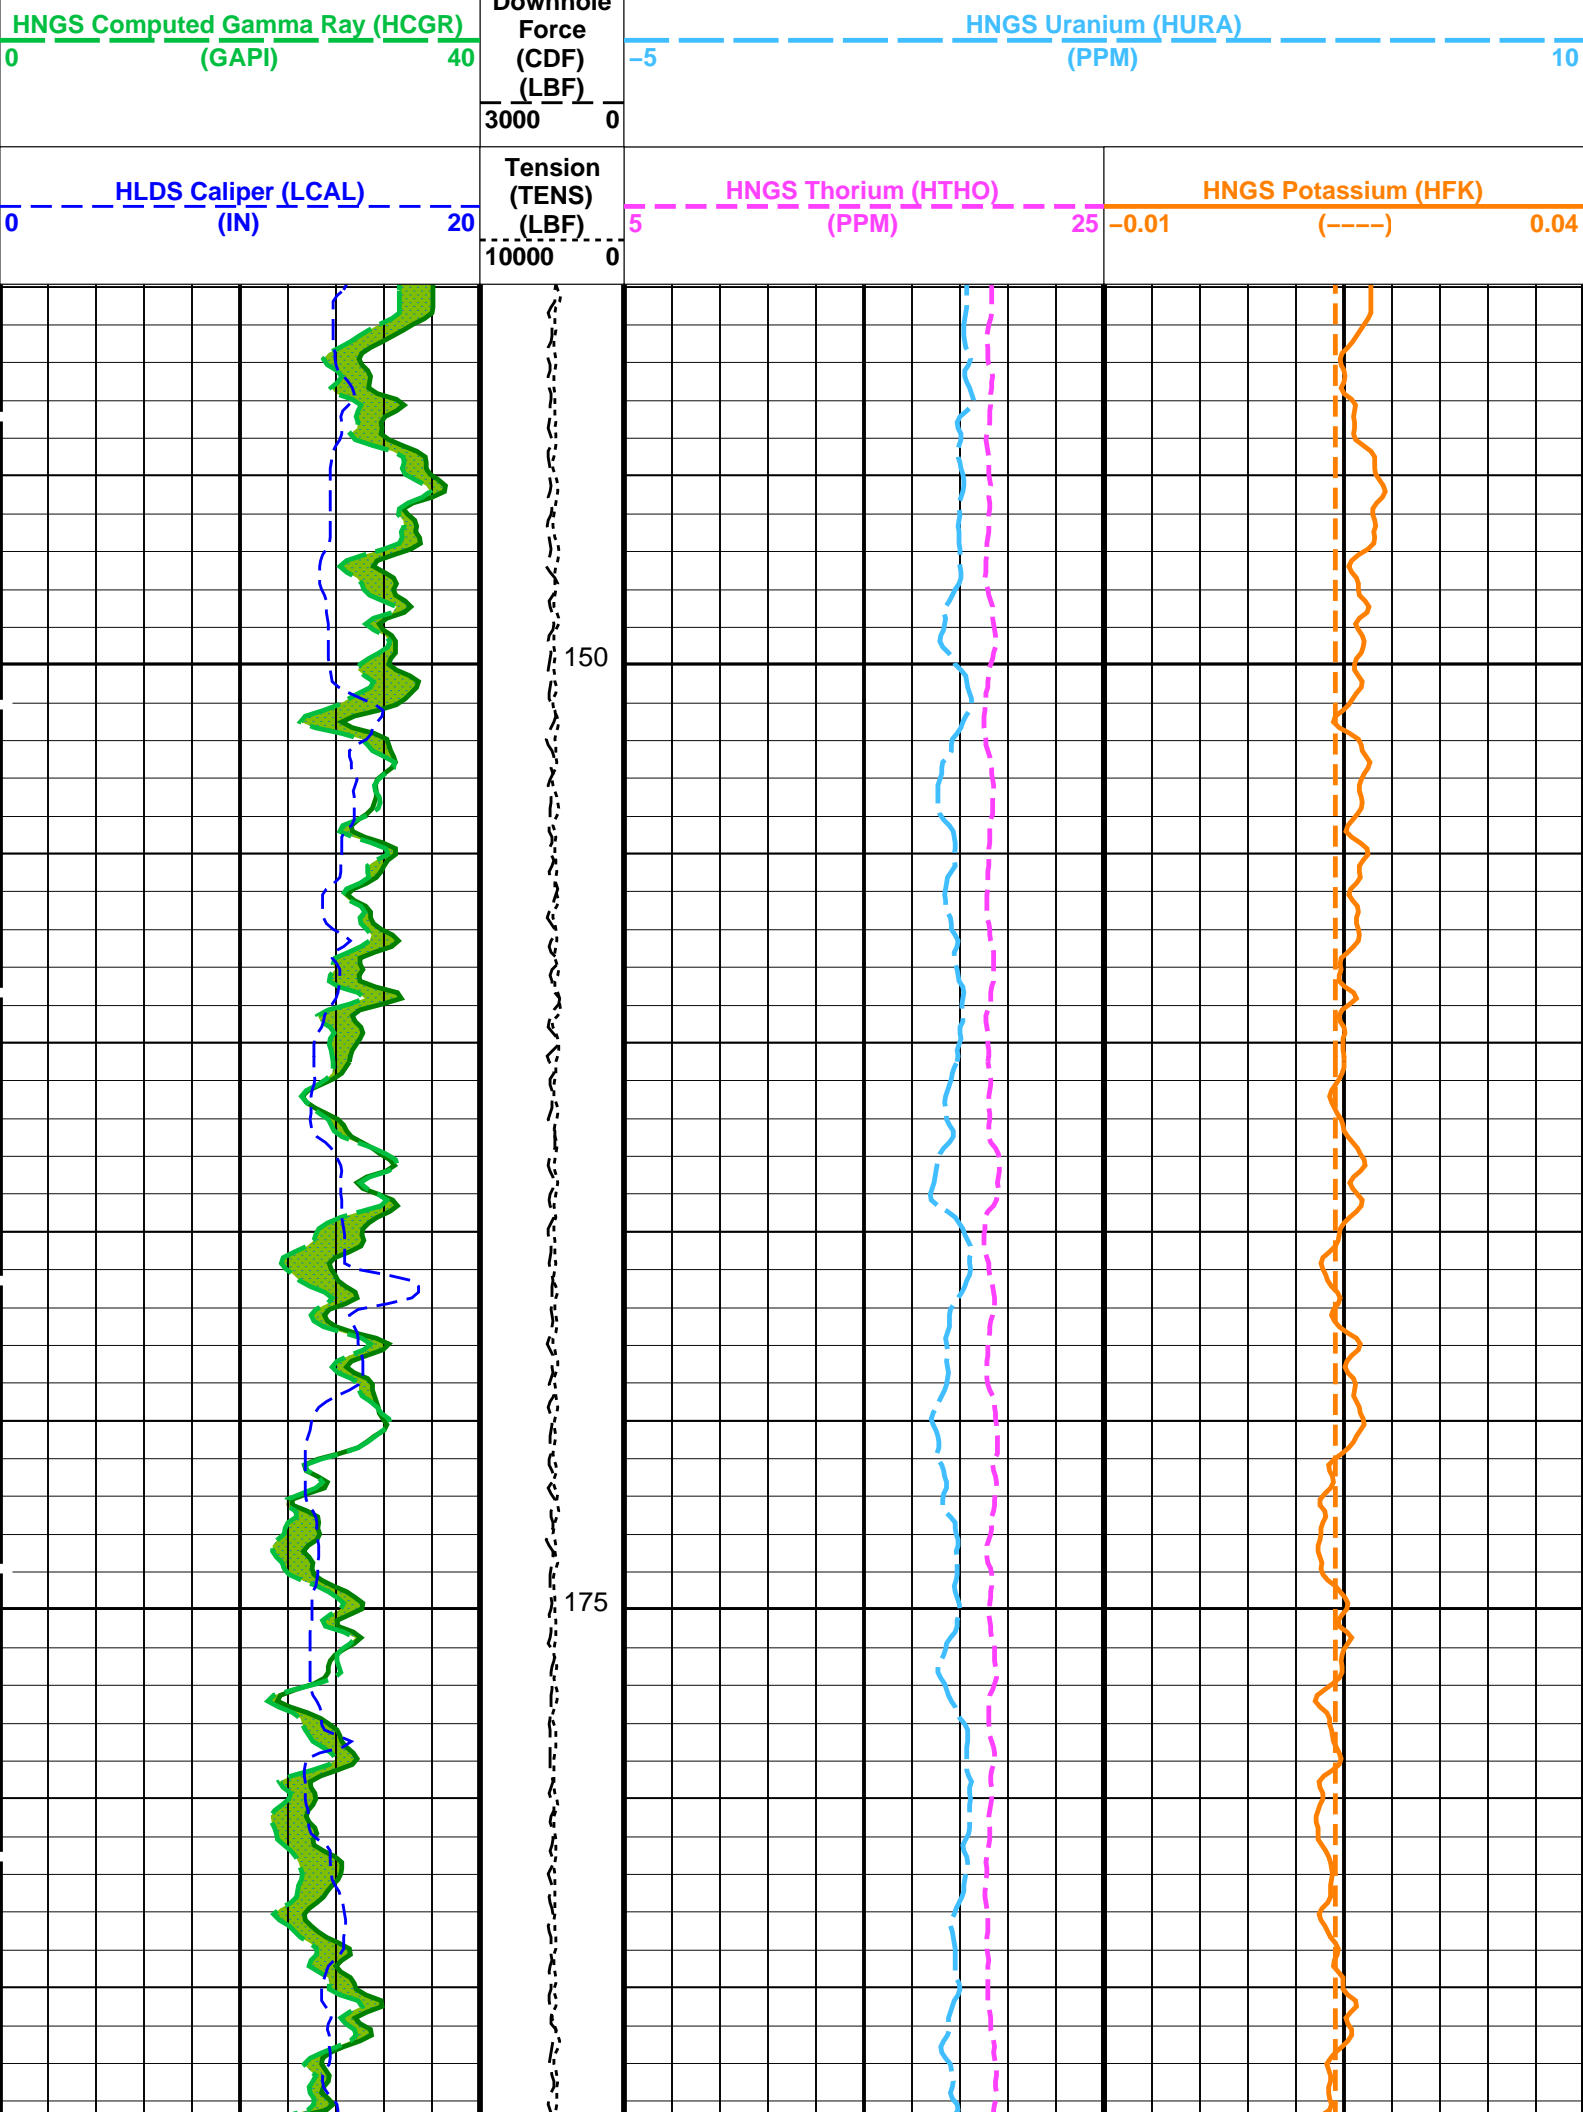


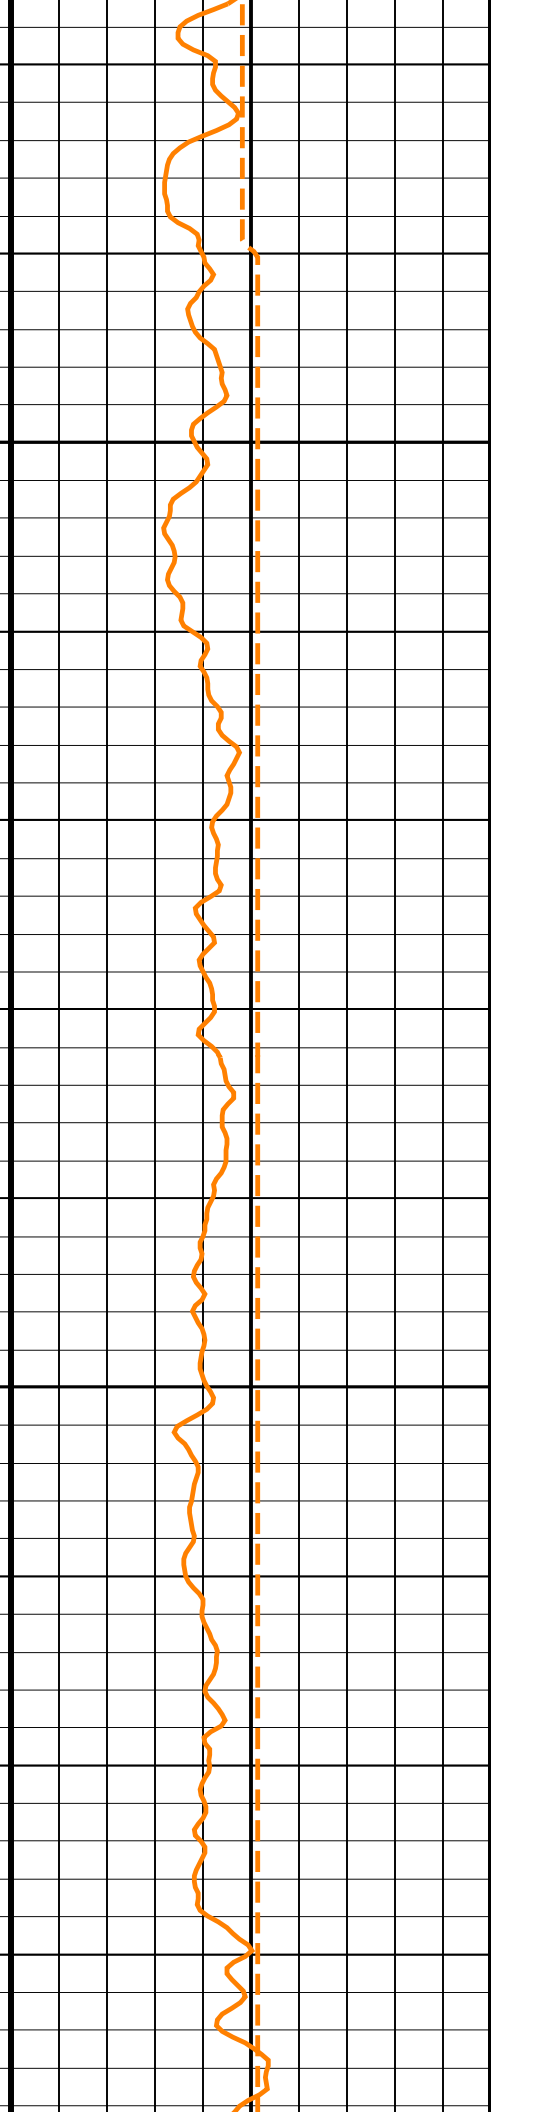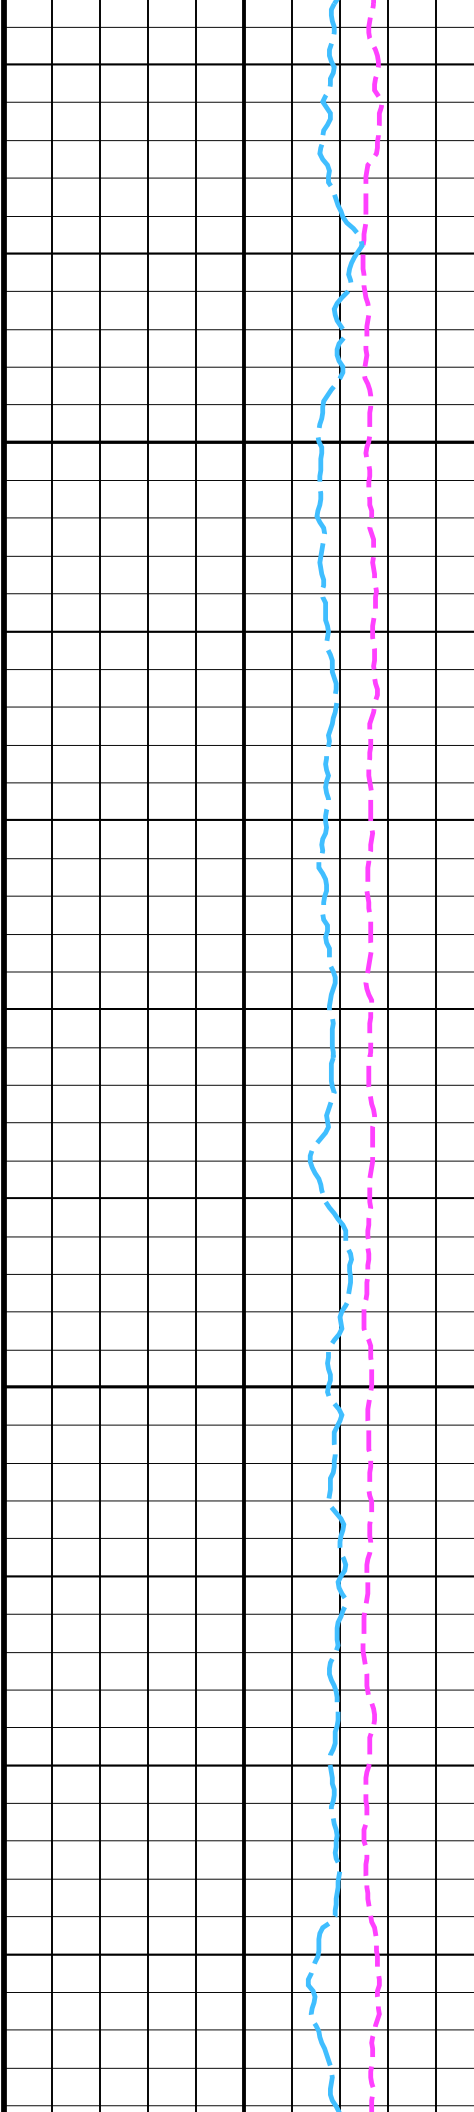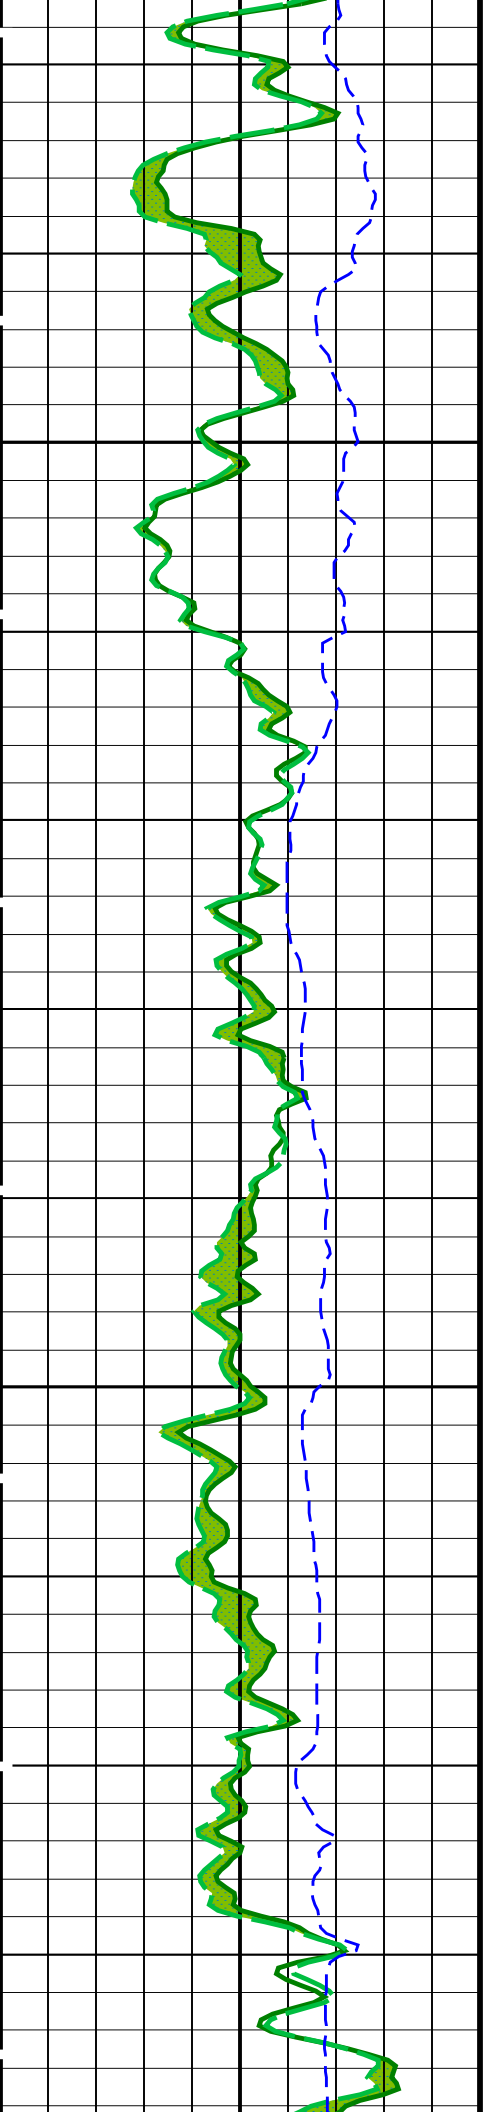



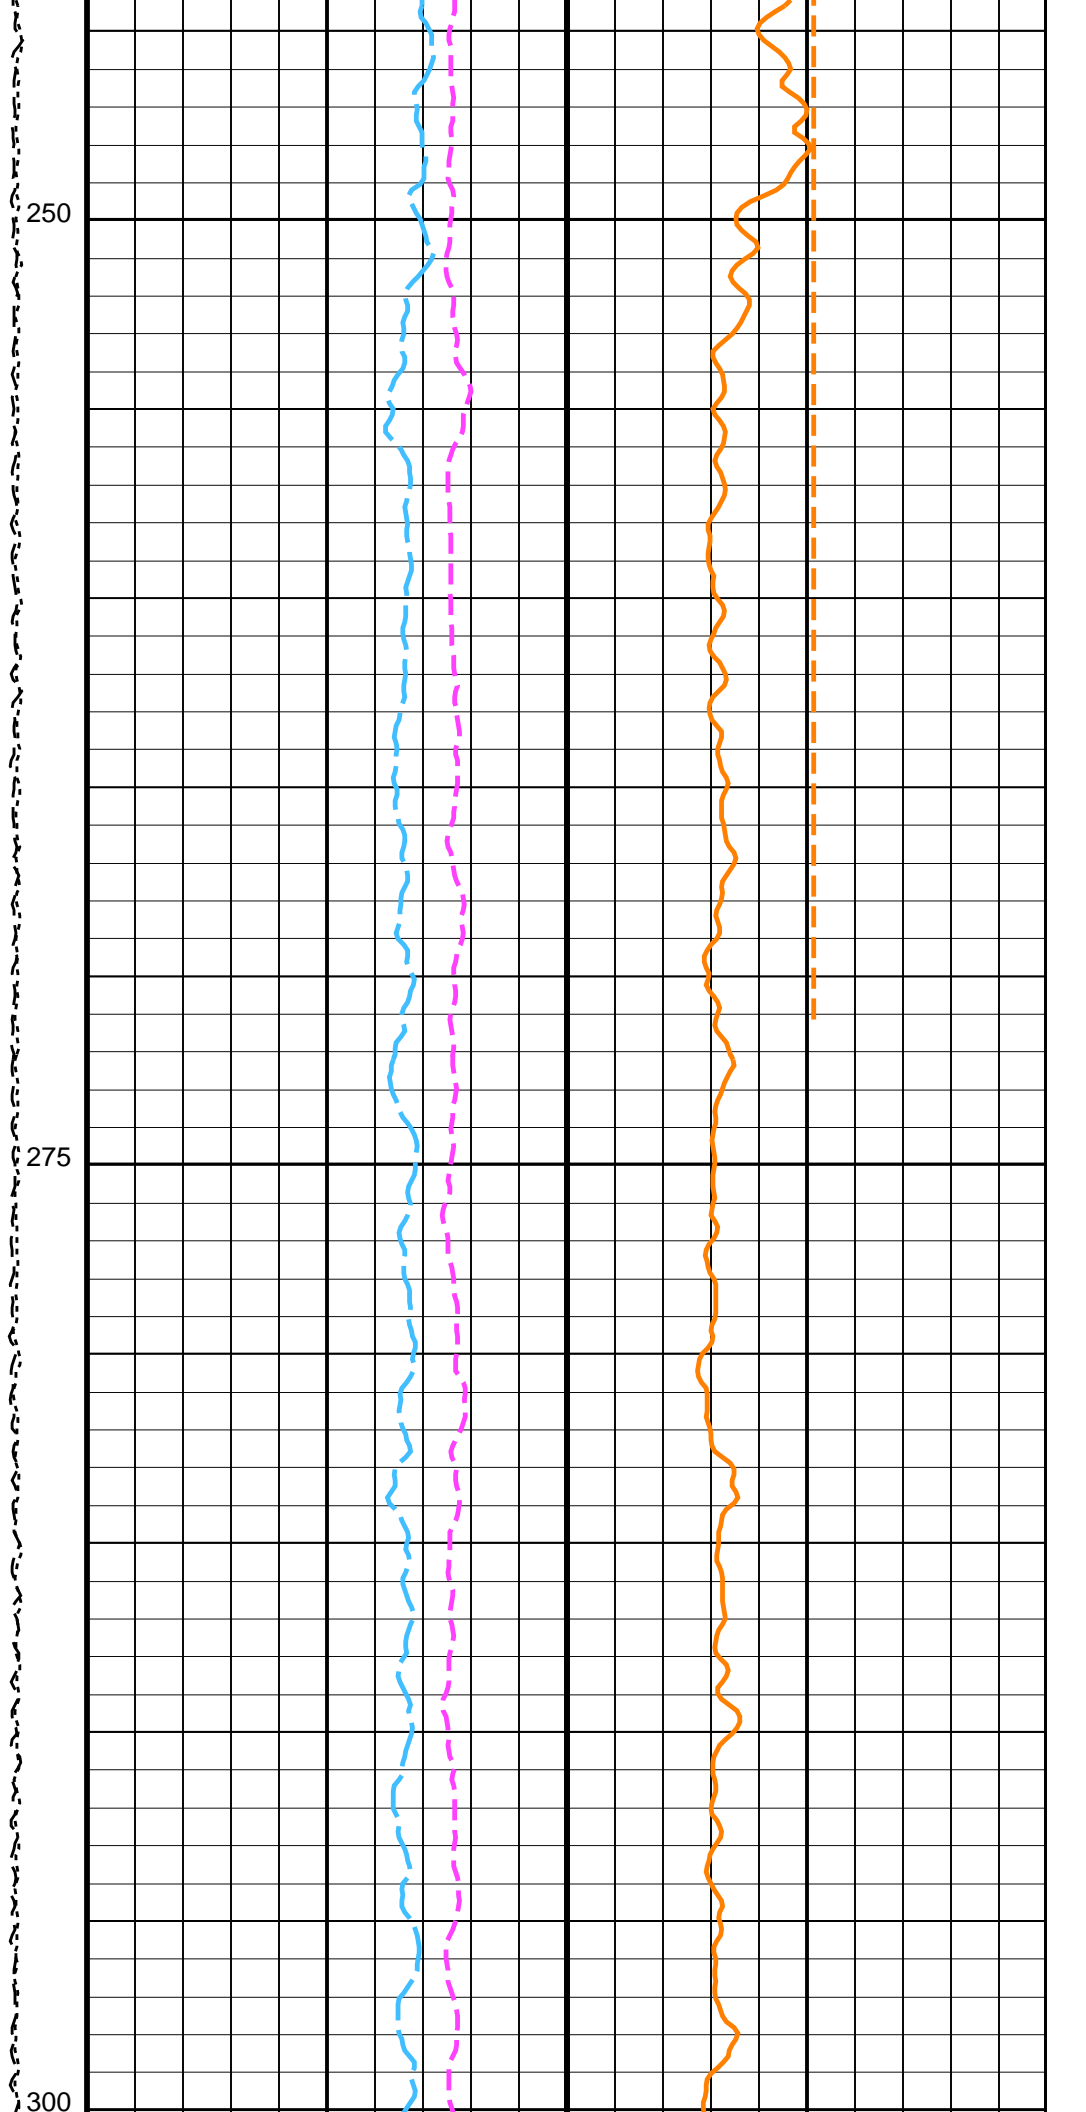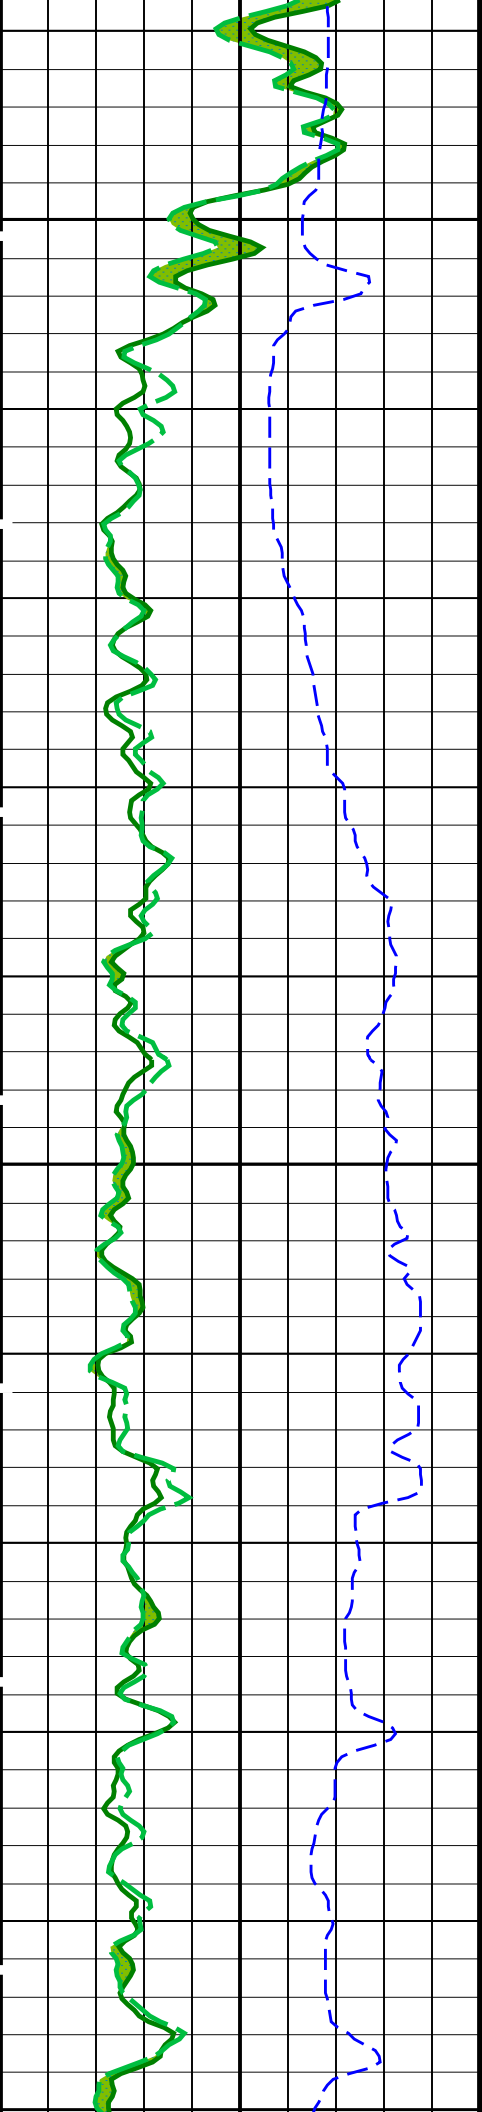

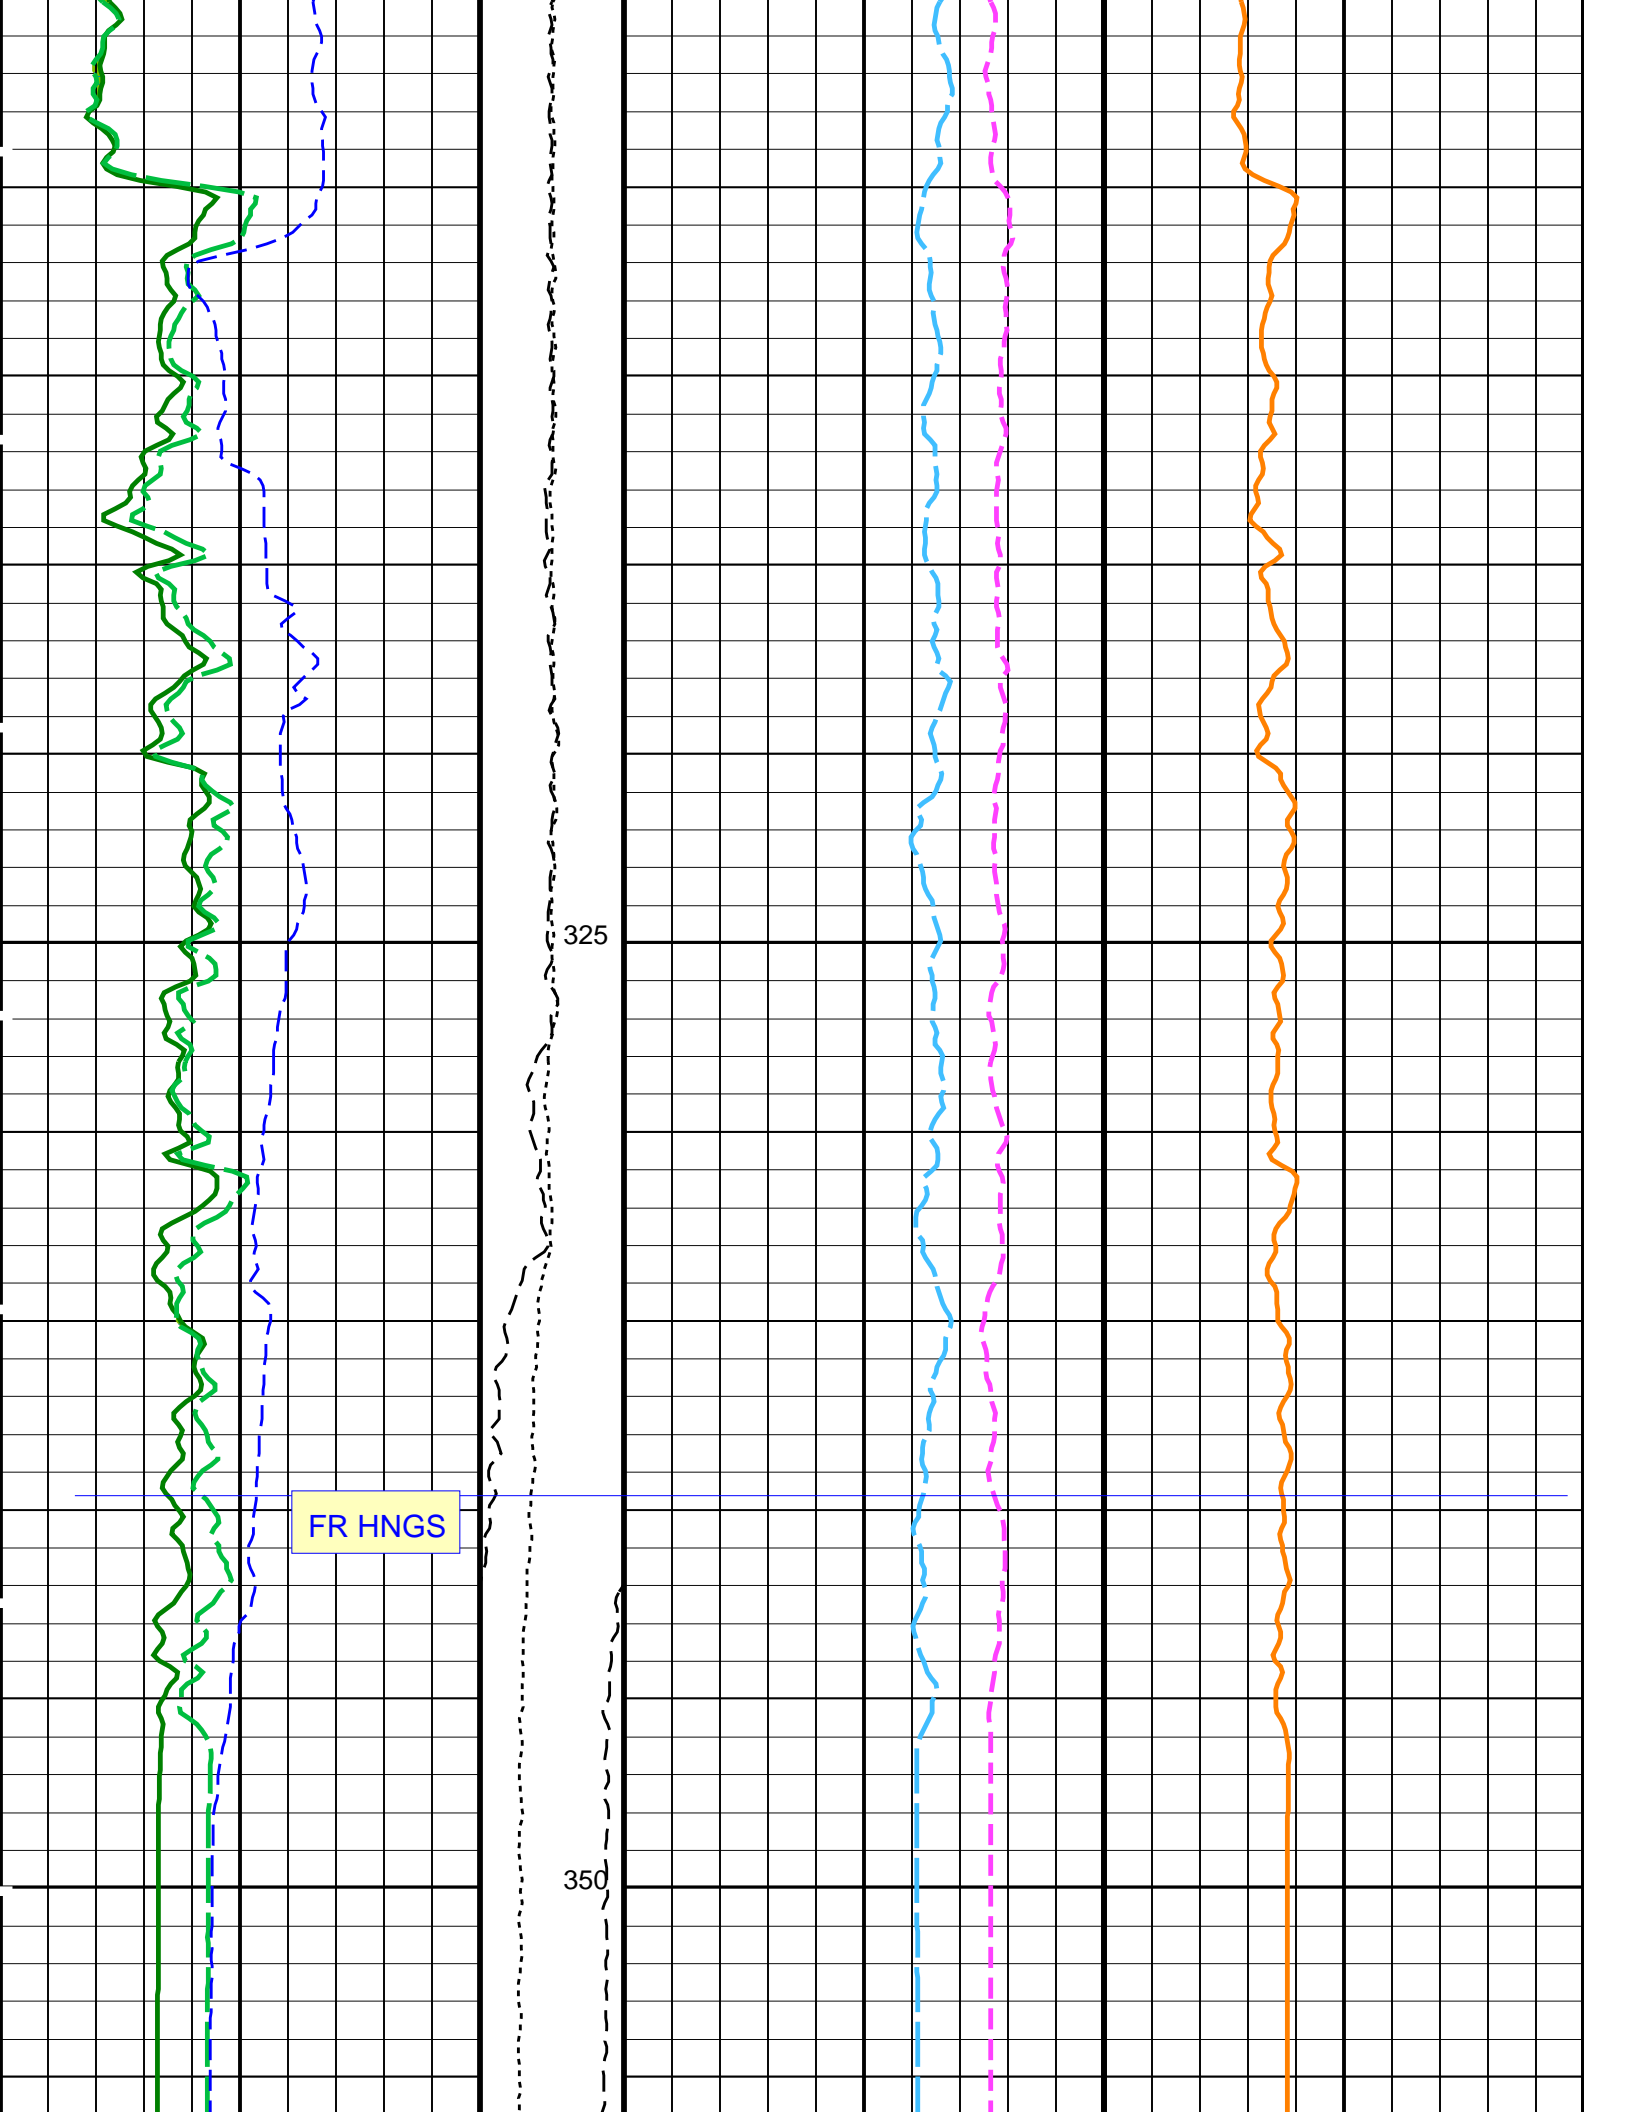

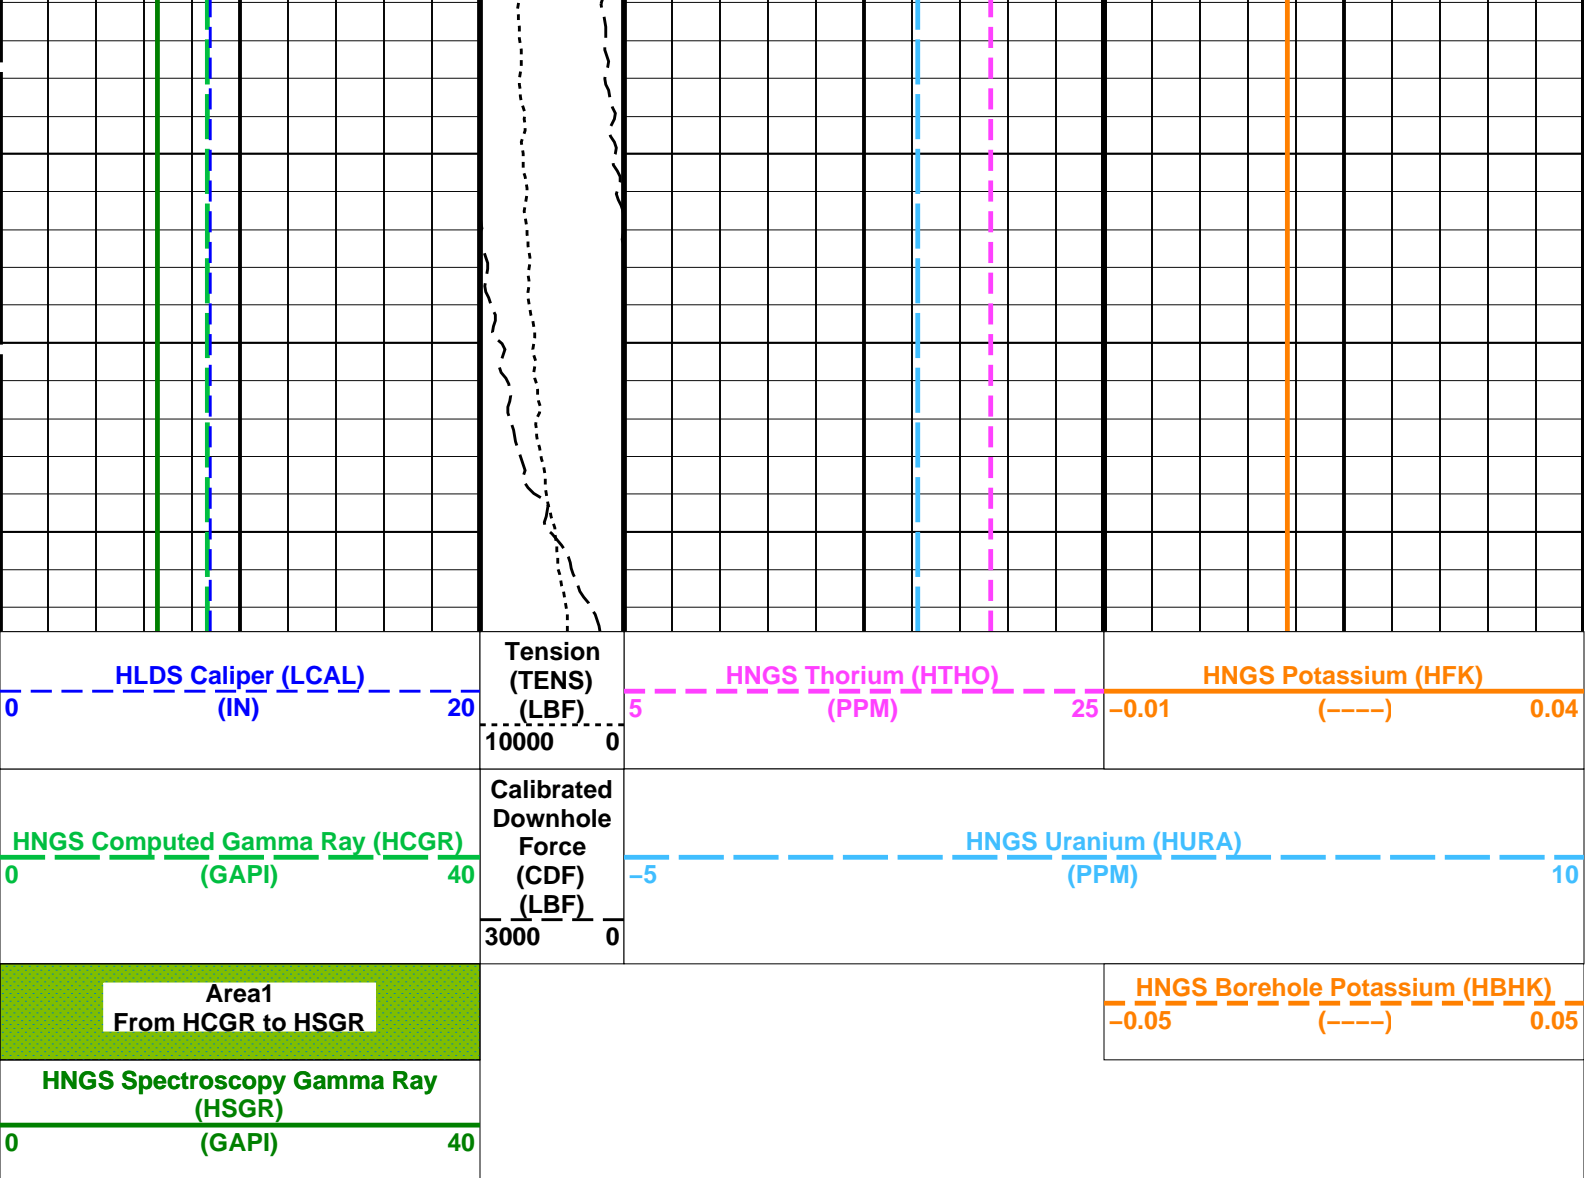

PIP SUMMARY

Time Mark Every 60 S

Parameters

DLIS Name	Description	Value	
HRLT-B: High Resolution Laterolog Array - B			
BHS	Borehole Status	OPEN	
GCSE	Generalized Caliper Selection	LCAL	
HNGS-BA: Hostile Natural Gamma Ray Sonde			
BAR1	HNGS Detector 1 Barite Constant	1	
BAR2	HNGS Detector 2 Barite Constant	1	
BHK	HNGS Borehole Potassium Correction Concentration	0	
BHS	Borehole Status	OPEN	
CSD1	Inner Casing Outer Diameter	0	IN
CSD2	Outer Casing Outer Diameter	0	IN
CSW1	Inner Casing Weight	0	LB/F
CSW2	Outer Casing Weight	0	LB/F
DBCC	HNGS Barite Constant Correction Flag	NONE	
GCSE	Generalized Caliper Selection	LCAL	
H1P	HNGS Detector 1 Allow/Disallow In Processing	ALLOW	
H2P	HNGS Detector 2 Allow/Disallow In Processing	ALLOW	
HABK	HNGS Borehole Potassium Running Average	-0.000422465	
HALF	HNGS Alpha Filter Length	60	IN
HCRB	HNGS Apply Borehole Potassium Correction	NONE	
HMWM	Mud Weighting Material	BARI	
HNPE	HNGS Processing Enable	YES	
S1BI	HNGS Detector 1 Calibration Bismuth Count Rate	1.3	CPS
S2BI	HNGS Detector 2 Calibration Bismuth Count Rate	1.3	CPS
SGRC	HNGS Standard Gamma-Ray Correction Flag	YES	
TPOS	Tool Position	ECCE	
VBA1	HNGS Detector 1 Variable Barite Factor Running Average	1.05286	
VBA2	HNGS Detector 2 Variable Barite Factor Running Average	1.01977	
EDTC-B: Enhanced DTS Cartridge			
BHS	Borehole Status	OPEN	

BS	Borehole Status	9.875	IN
GCSE	Generalized Caliper Selection	1.03	G/C3
	System and Miscellaneous	-3170.5	M
DO	Depth Offset for Playback	RECOMPUTE	
DFD	Drilling Fluid Density		
PP	Playback Processing		

Format: HNGSYields    Vertical Scale: 1:200    Graphics File Created: 26-Sep-2014 11:23

### OP System Version: 19C0-187

MSS_LDEO-A	19C0-187	HRLT-B	19C0-187
HLDS	19C0-187	LDSC-B	19C0-187
HNGC-B	19C0-187	HNGS-BA	19C0-187
EDTC-B	SKK-5169-EDTCB		

#### Input DLIS Files

DEFAULT	MSS_LDEO_HRLA_LDL_008LUP	FN:8	PRODUCER	23-Sep-2014 06:10	3543.3 M	3310.4 M
---------	--------------------------	------	----------	-------------------	----------	----------

#### Output DLIS Files

DEFAULT	MSS_LDEO_HRLA_LDL_032PUP	FN:39	PRODUCER	26-Sep-2014 11:23		
CLIENT	MSS_LDEO_HRLA_LDL_032PUC	FN:40	CUSTOMER	26-Sep-2014 11:23		



**Second Pass**

MAXIS Field Log

#### Input DLIS Files

DEFAULT	MSS_LDEO_HRLA_LDL_010LUP	FN:12	PRODUCER	23-Sep-2014 07:11	3477.0 M	3160.8 M
---------	--------------------------	-------	----------	-------------------	----------	----------

#### Output DLIS Files


DEFAULT	MSS_LDEO_HRLA_LDL_020PUP	FN:24	PRODUCER	26-Sep-2014 09:48	306.3 M	-9.6 M
CLIENT	MSS_LDEO_HRLA_LDL_020PUC	FN:25	CUSTOMER	26-Sep-2014 09:48	306.3 M	-9.6 M


### OP System Version: 19C0-187


MSS_LDEO-A	19C0-187	HRLT-B	19C0-187
HLDS	19C0-187	LDSC-B	19C0-187
HNGC-B	19C0-187	HNGS-BA	19C0-187
EDTC-B	SKK-5169-EDTCB		


#### PIP SUMMARY


Time Mark Every 60 S




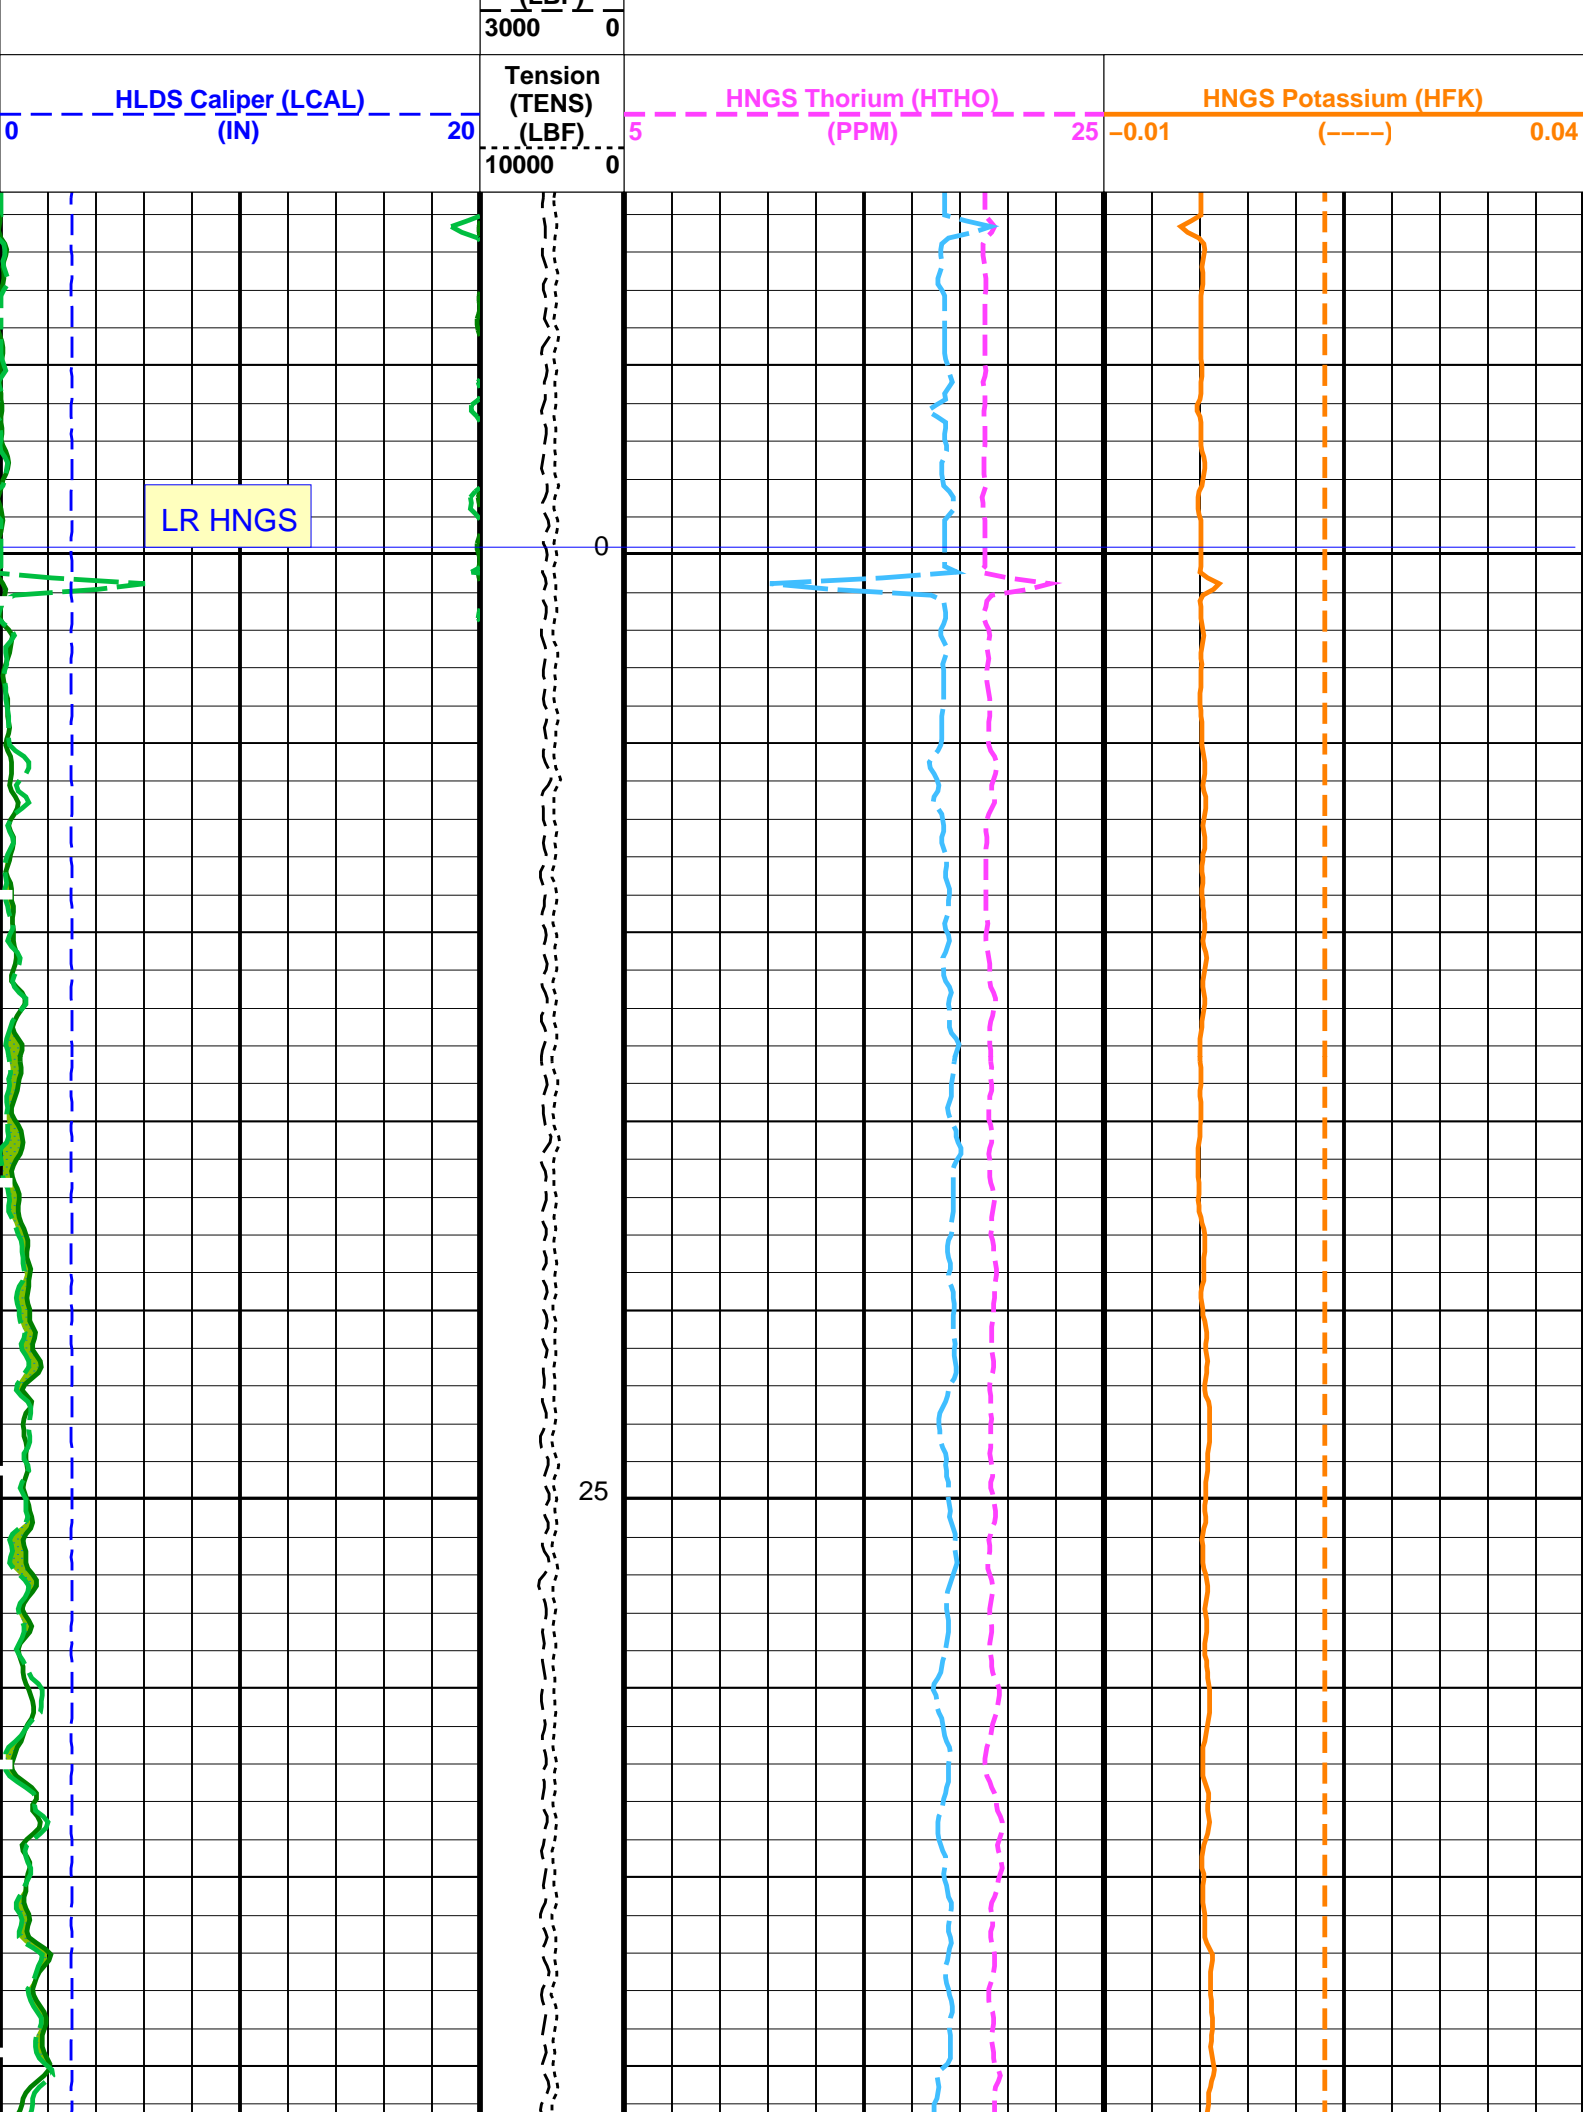


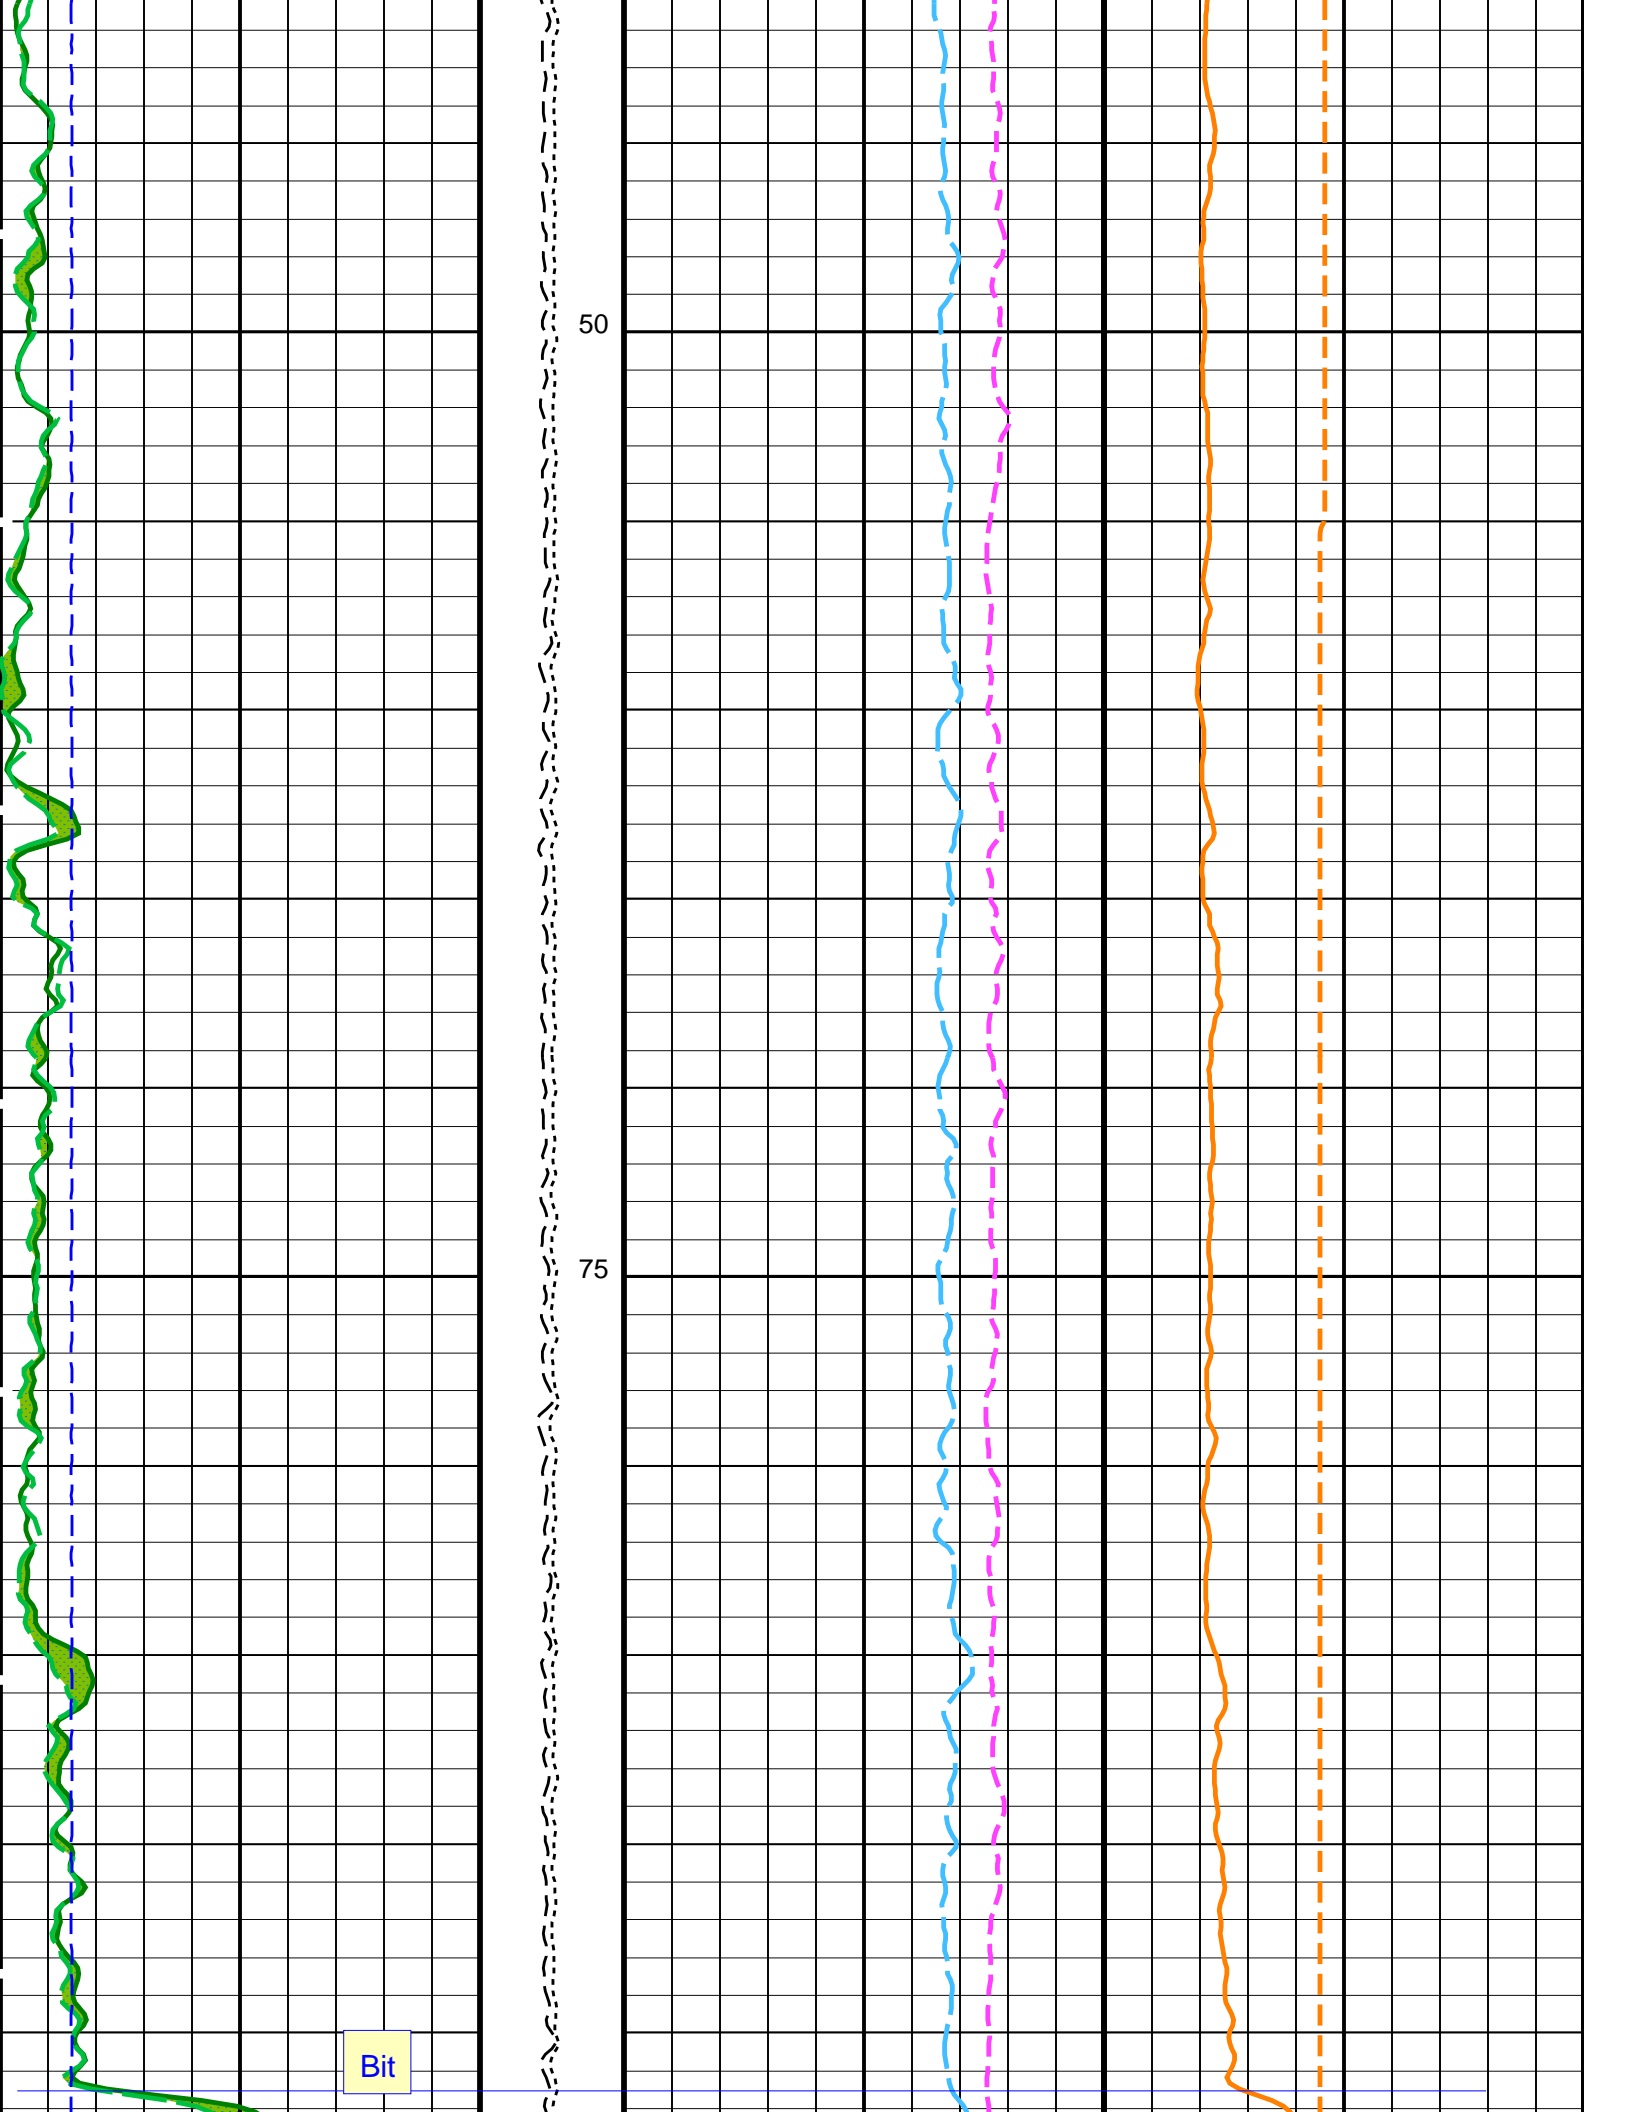



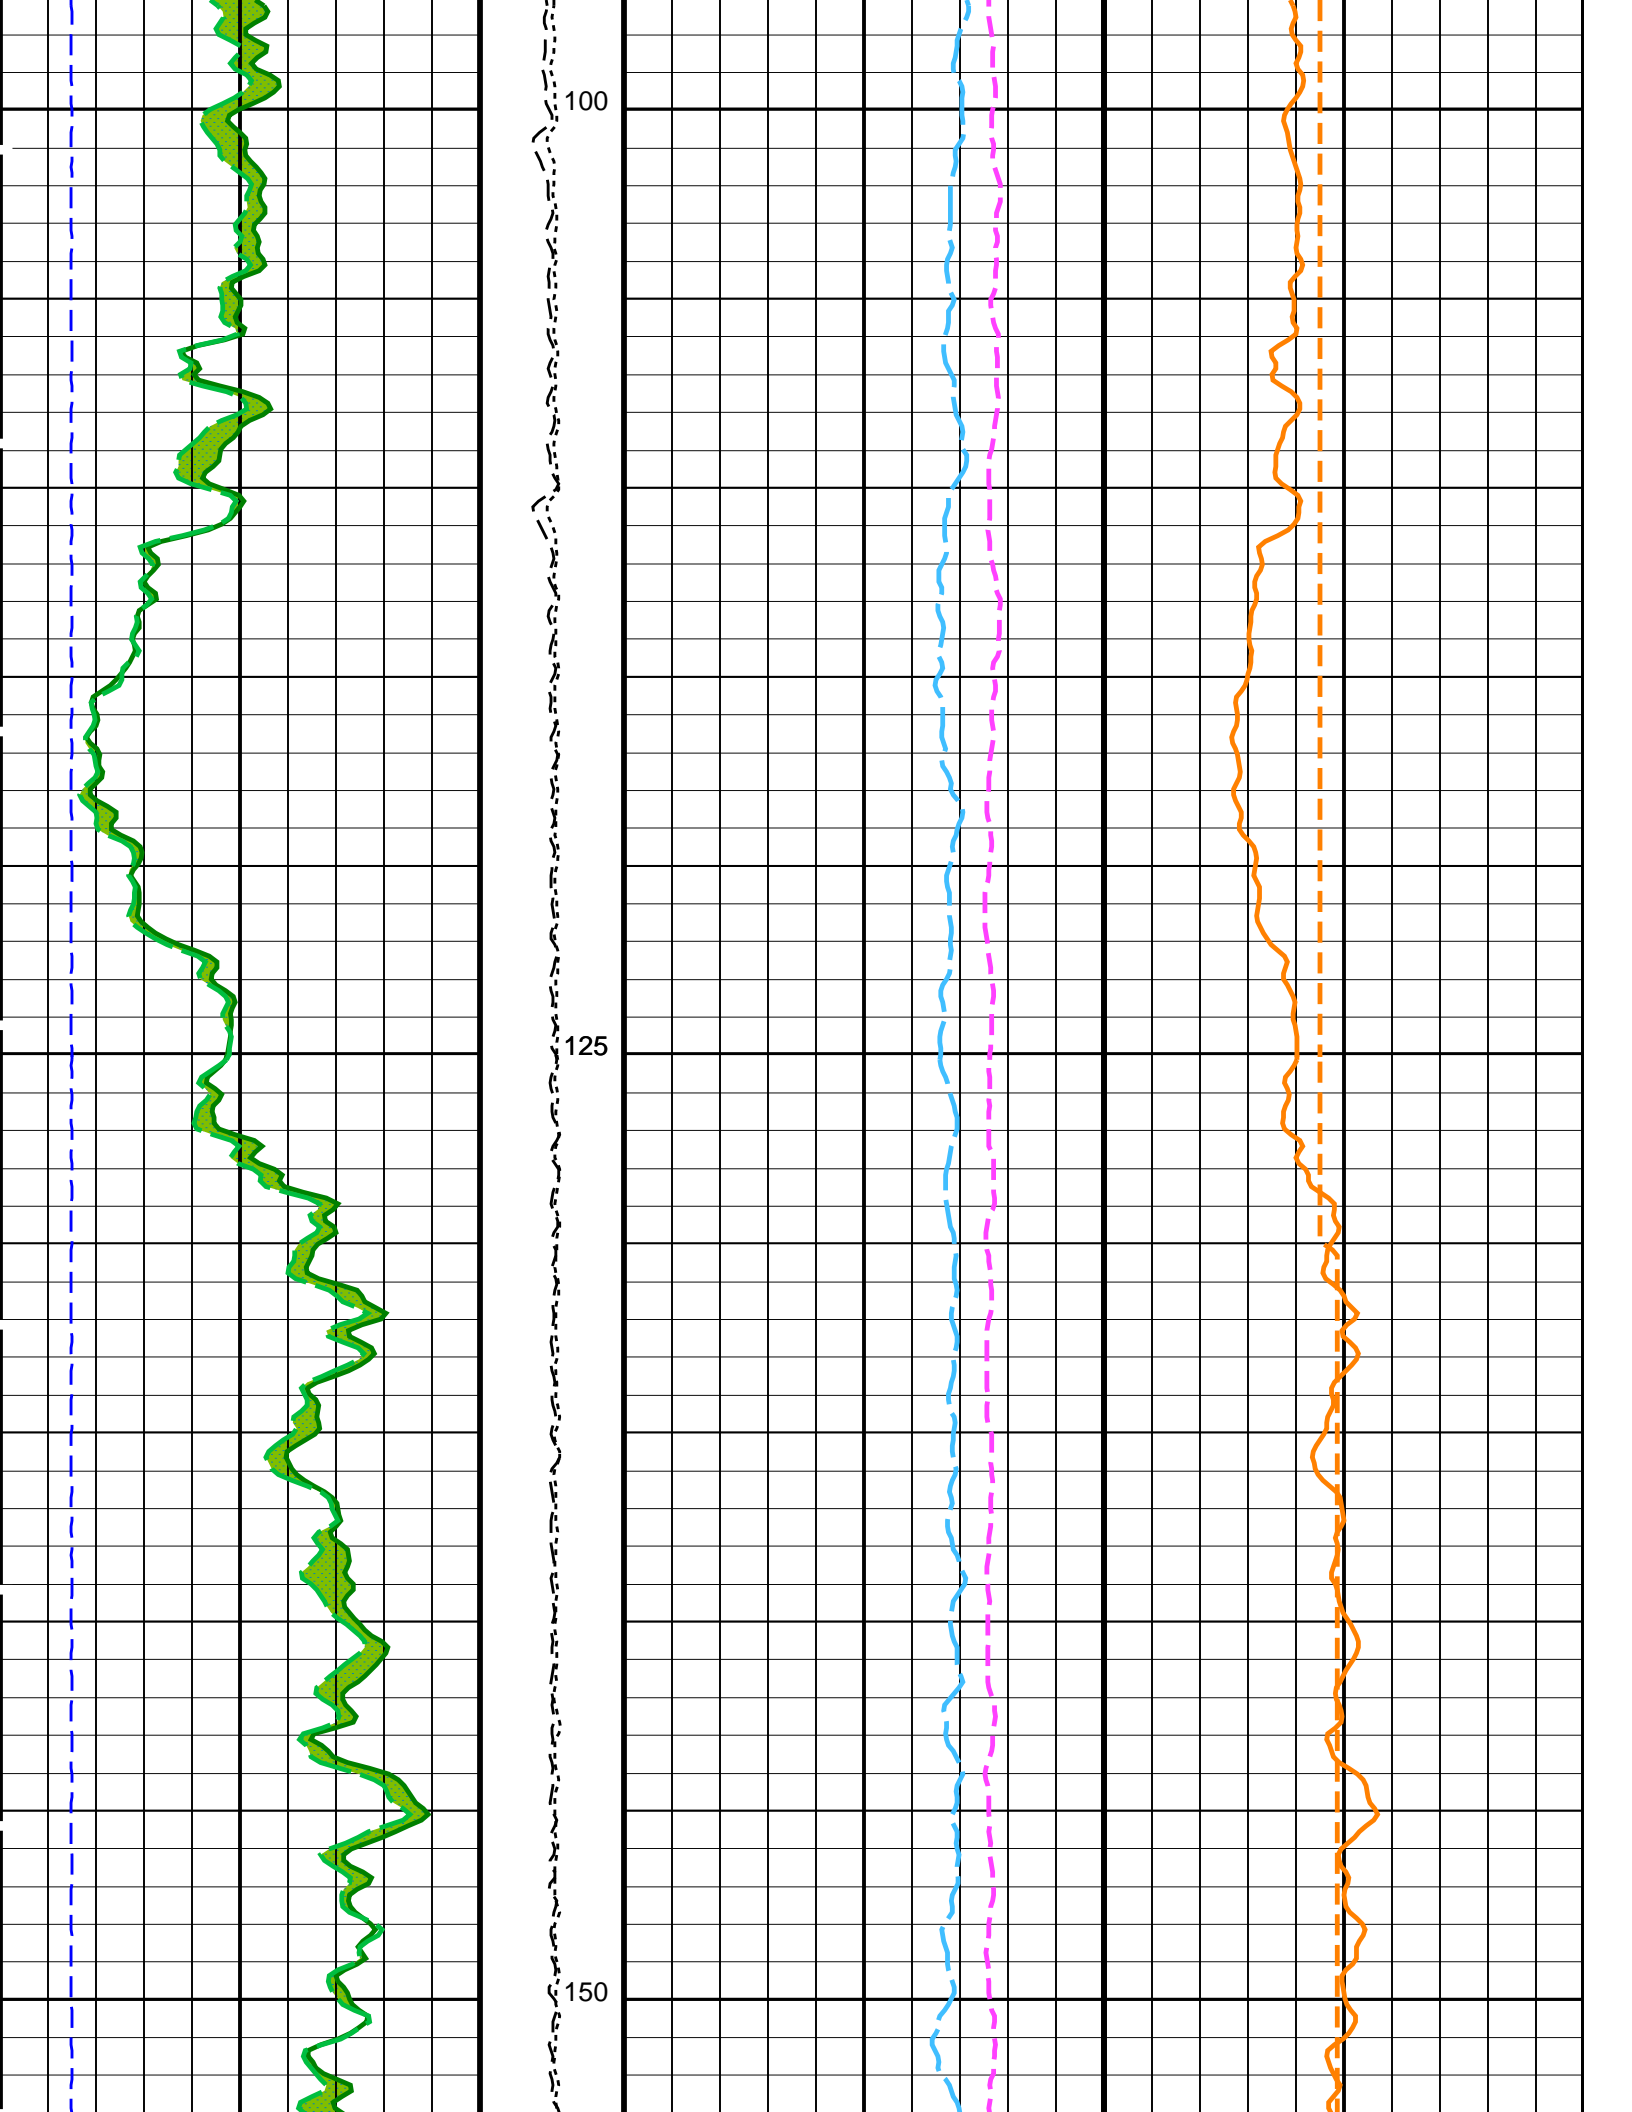


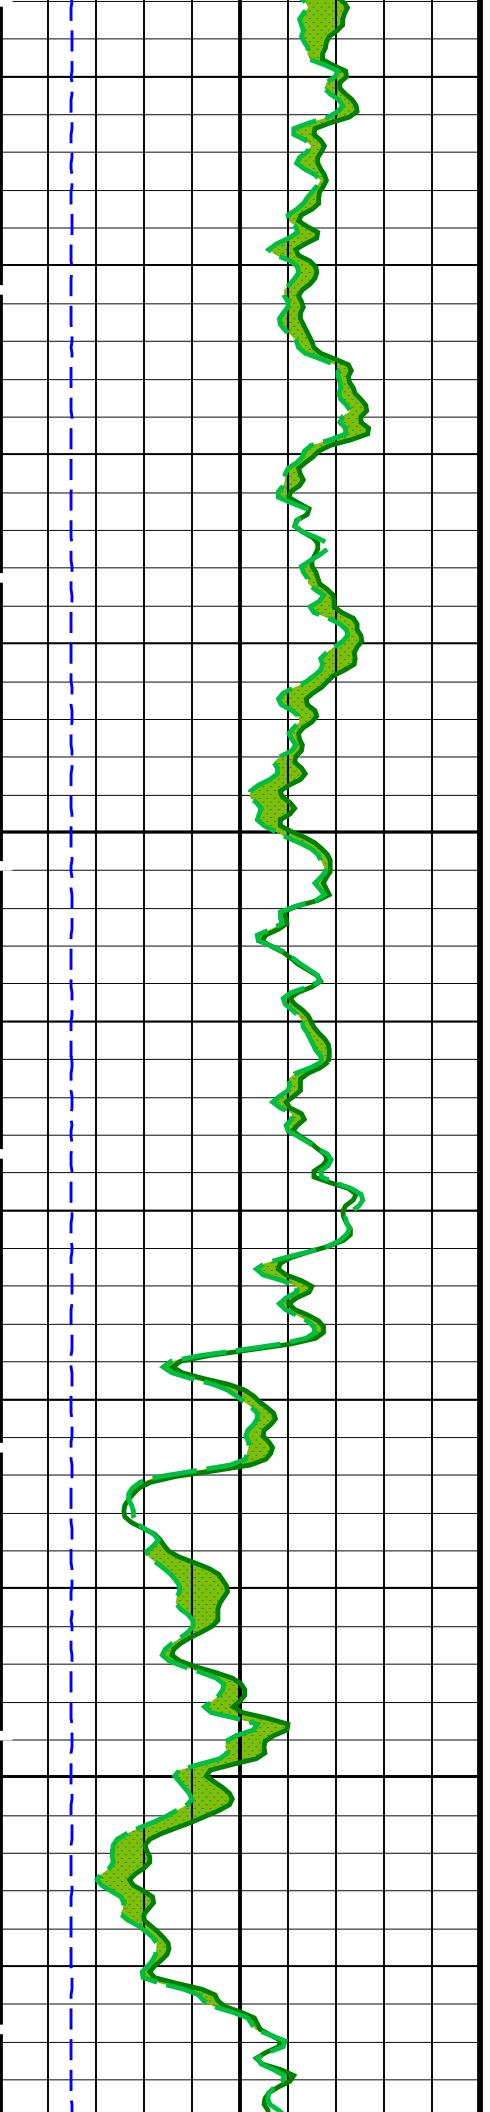


175  
200

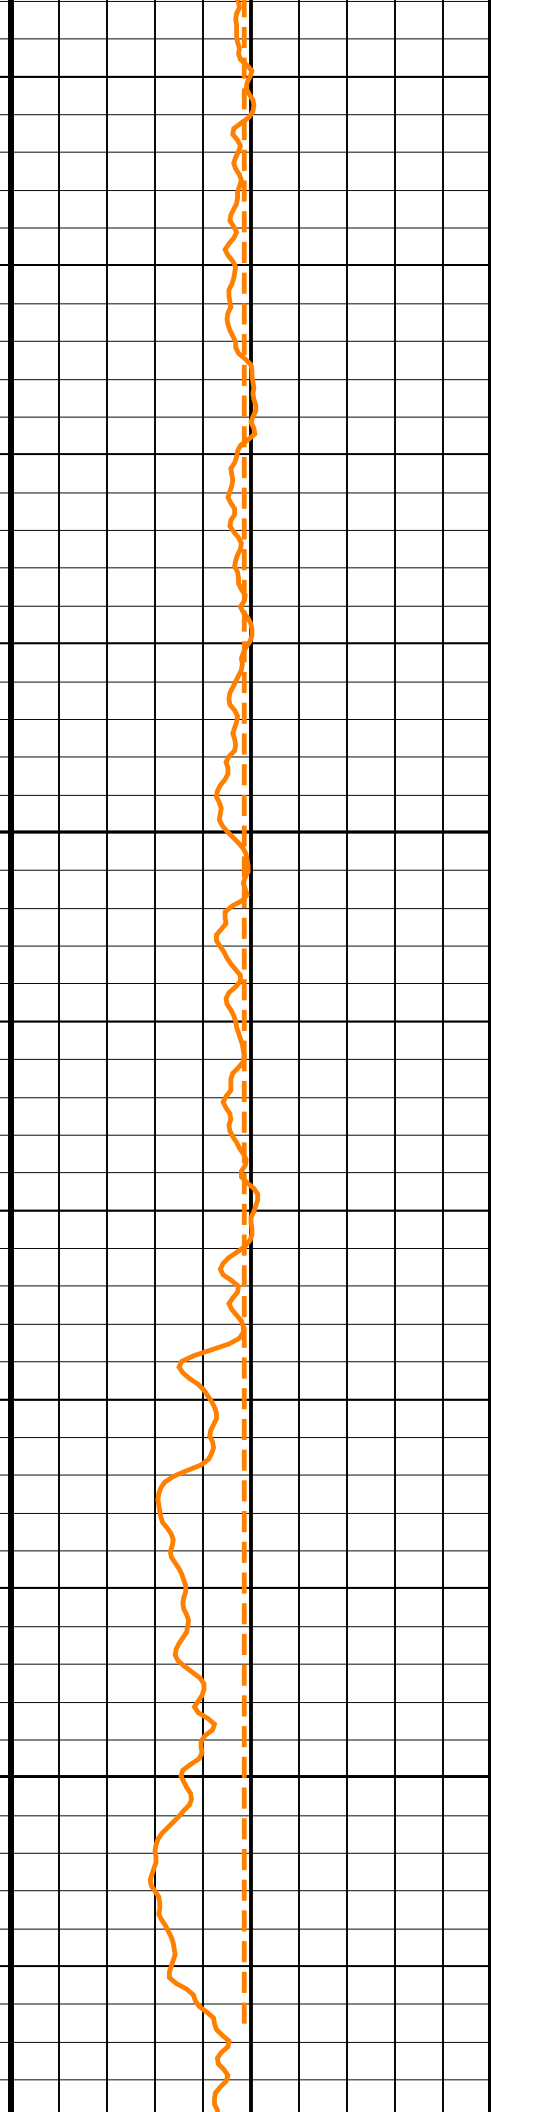
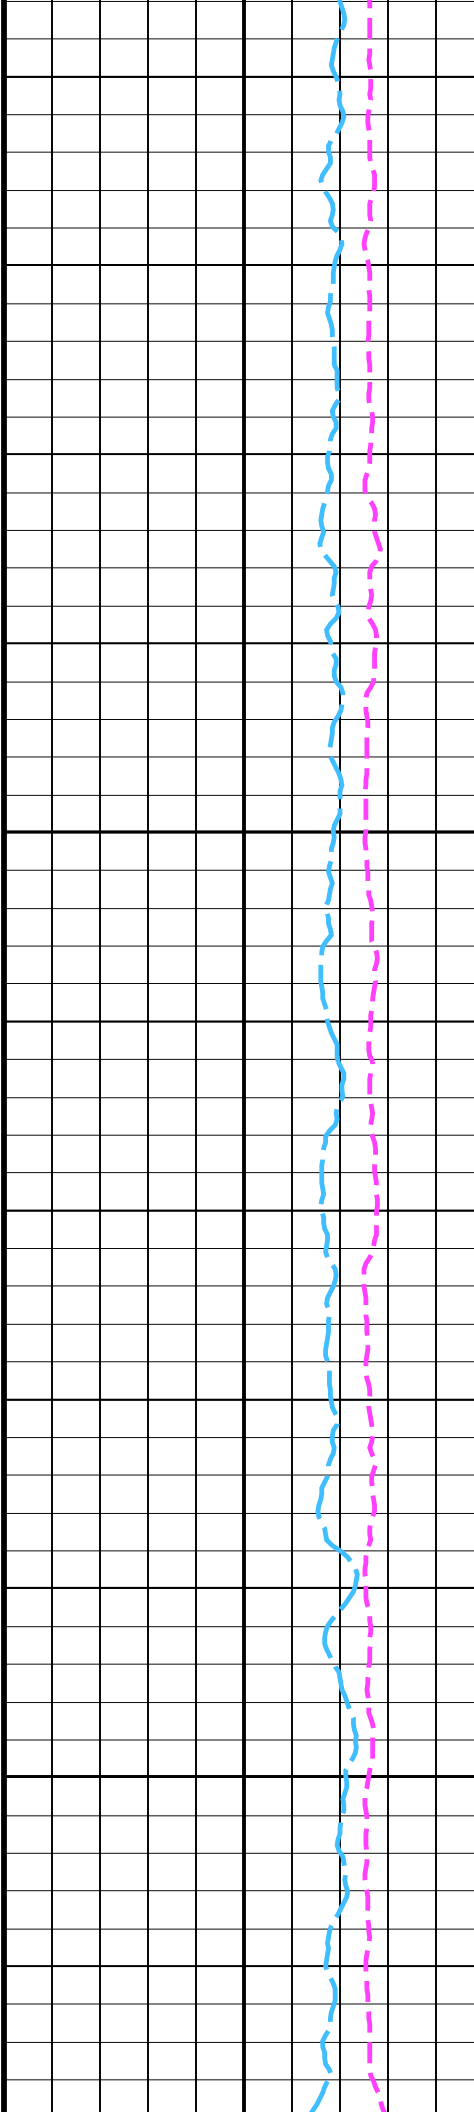




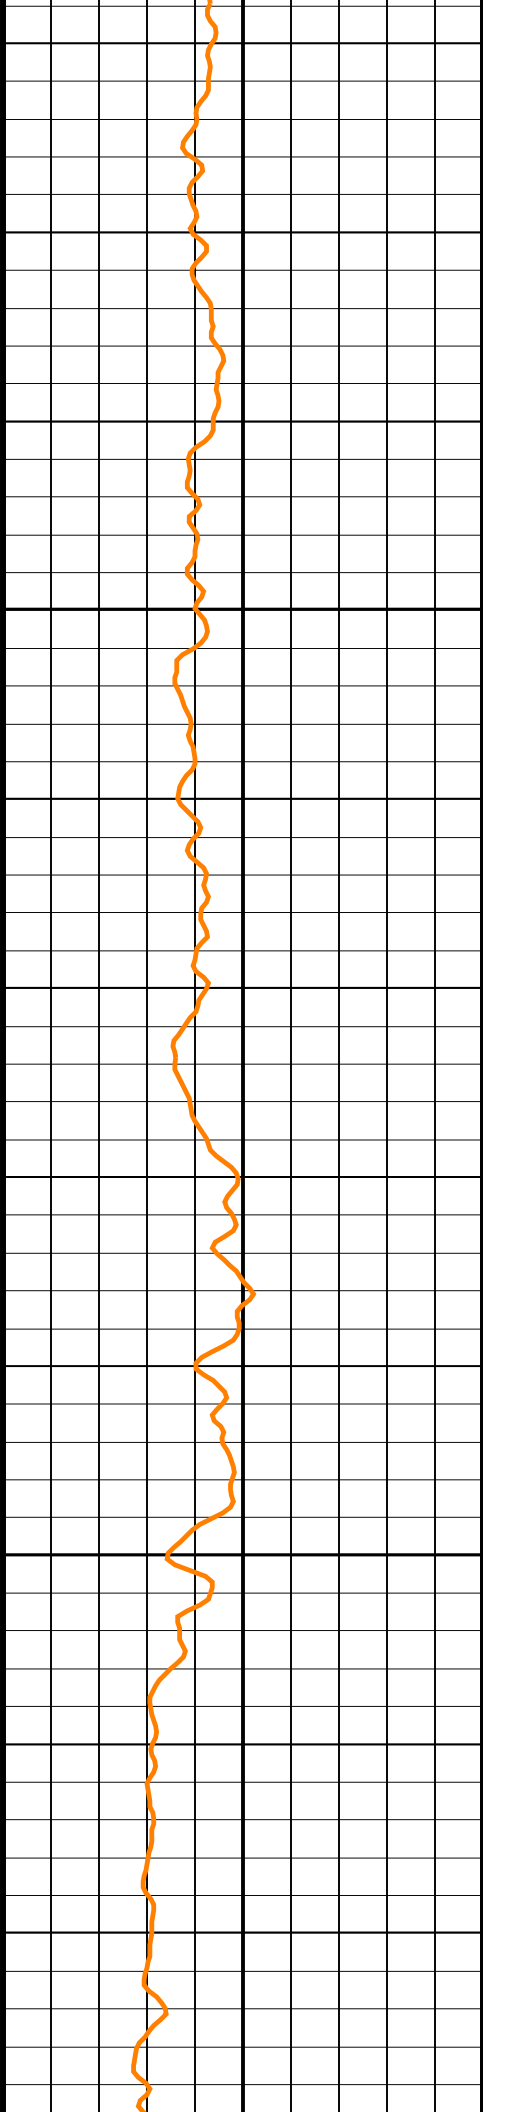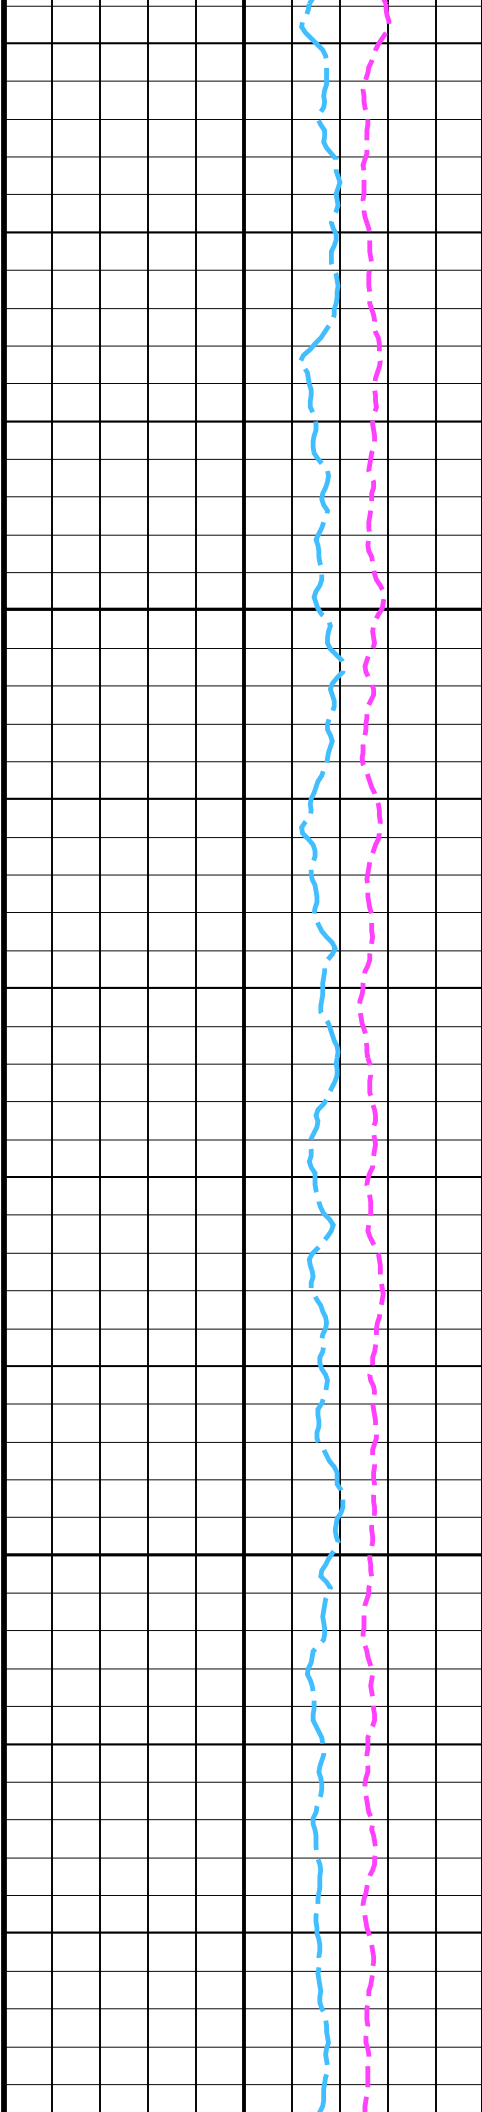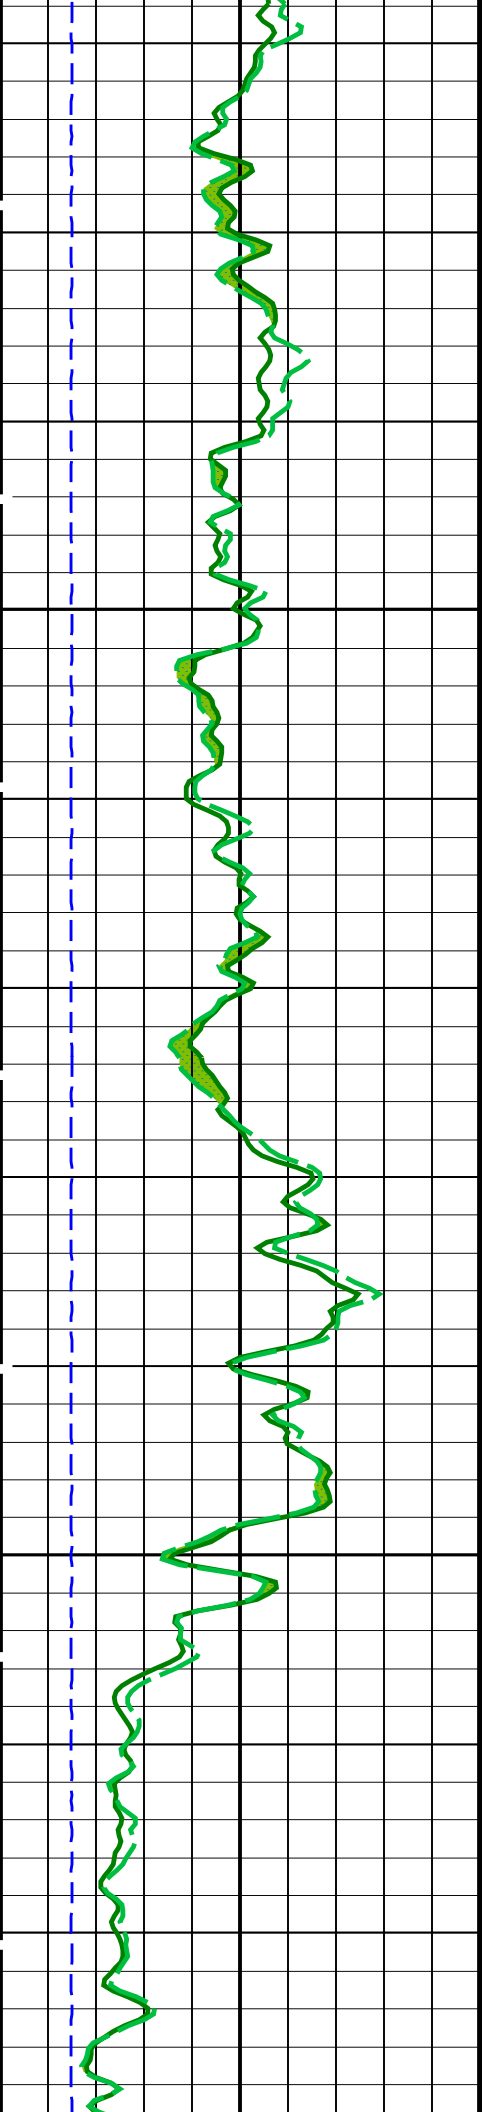

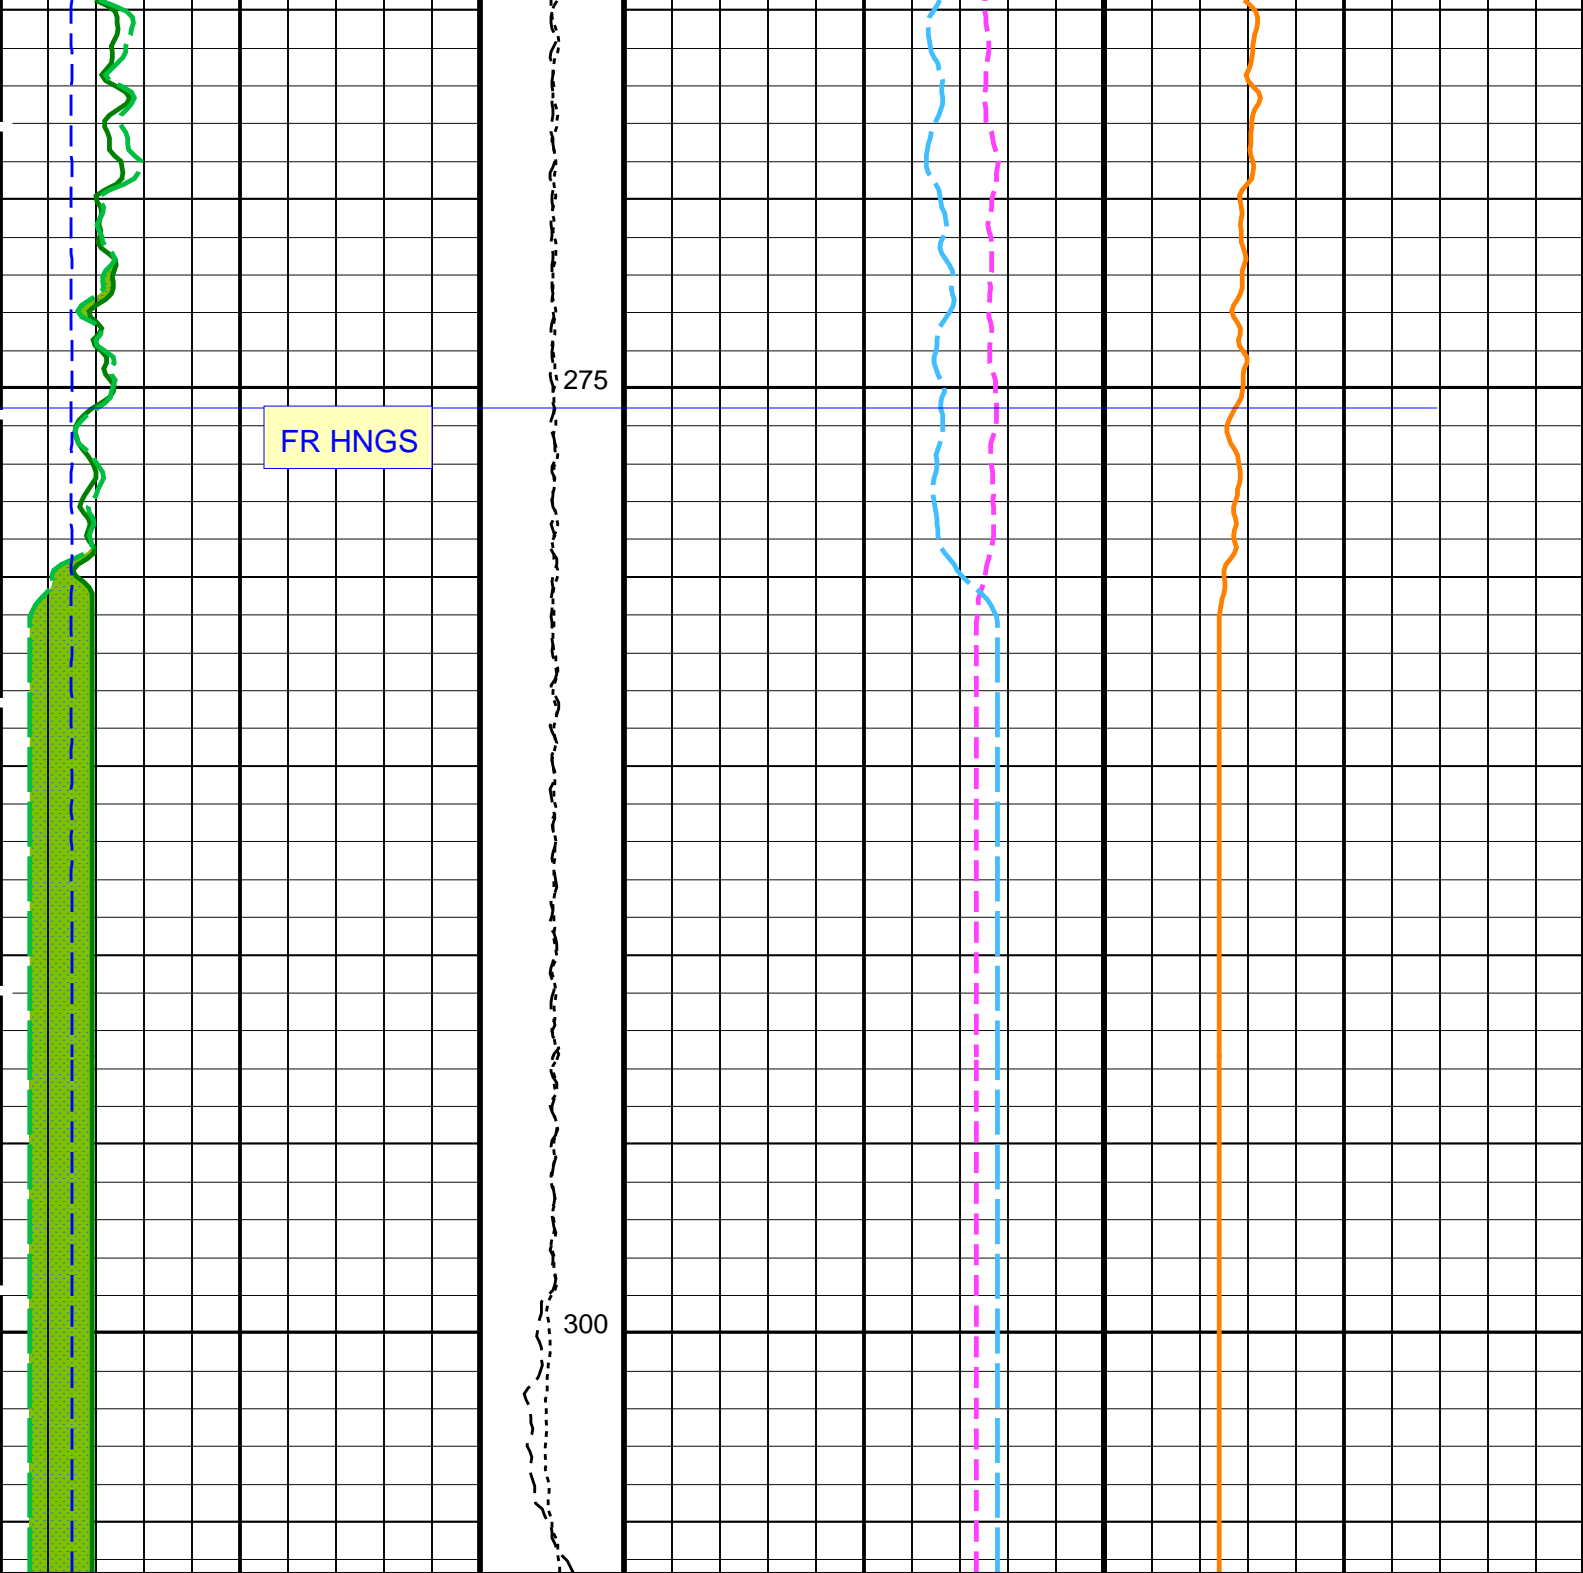

FR HNGS



### Parameters

DLIS Name	Description	Value	
	HRLT-B: High Resolution Laterolog Array - B		
BHS	Borehole Status	OPEN	
GCSE	Generalized Caliper Selection	BS	
	HNGS-BA: Hostile Natural Gamma Ray Sonde		
BAR1	HNGS Detector 1 Barite Constant	1	
BAR2	HNGS Detector 2 Barite Constant	1	
BHK	HNGS Borehole Potassium Correction Concentration	0	
BHS	Borehole Status	OPEN	
CSD1	Inner Casing Outer Diameter	0	IN
CSD2	Outer Casing Outer Diameter	0	IN
CSW1	Inner Casing Weight	0	LB/F
CSW2	Outer Casing Weight	0	LB/F
DBCC	HNGS Barite Constant Correction Flag	NONE	
GCSE	Generalized Caliper Selection	BS	
H1P	HNGS Detector 1 Allow/Disallow In Processing	ALLOW	
H2P	HNGS Detector 2 Allow/Disallow In Processing	ALLOW	
HABK	HNGS Borehole Potassium Running Average	-0.00343737	
HALF	HNGS Alpha Filter Length	60	IN
HCRB	HNGS Apply Borehole Potassium Correction	NONE	
HMWM	Mud Weighting Material	BARI	
HNPE	HNGS Processing Enable	YES	
S1BI	HNGS Detector 1 Calibration Bismuth Count Rate	1.3	CPS
S2BI	HNGS Detector 2 Calibration Bismuth Count Rate	1.3	CPS
SGRC	HNGS Standard Gamma-Ray Correction Flag	YES	
TPOS	Tool Position	ECCE	
VBA1	HNGS Detector 1 Variable Barite Factor Running Average	1.0244	
VBA2	HNGS Detector 2 Variable Barite Factor Running Average	1.01751	
	EDTC-B: Enhanced DTS Cartridge		
BHS	Borehole Status	OPEN	
GCSE	Generalized Caliper Selection	BS	
	System and Miscellaneous		
BS	Bit Size	9.875	IN
DFD	Drilling Fluid Density	1.03	G/C3
DO	Depth Offset for Playback	-3170.5	M
PP	Playback Processing	RECOMPUTE	

Format: HNGSYields Vertical Scale: 1:200 Graphics File Created: 26-Sep-2014 09:48

### OP System Version: 19C0-187

MSS_LDEO-A	19C0-187	HRLT-B	19C0-187
HLDS	19C0-187	LDSC-B	19C0-187
HNGC-B	19C0-187	HNGS-BA	19C0-187
EDTC-B	SKK-5169-EDTCB		

### Input DLIS Files

DEFAULT	MSS_LDEO_HRLA_LDL_010LUP	FN:12	PRODUCER	23-Sep-2014 07:11	3477.0 M	3160.8 M
---------	--------------------------	-------	----------	-------------------	----------	----------

### Output DLIS Files

DEFAULT	MSS_LDEO_HRLA_LDL_020PUP	FN:24	PRODUCER	26-Sep-2014 09:48		
CLIENT	MSS_LDEO_HRLA_LDL_020PUC	FN:25	CUSTOMER	26-Sep-2014 09:48		

Calibrations

Calibration and Check Summary

Measurement	Nominal	Master	Before	After	Change	Limit	Units
<b>High Resolution Laterolog Array – B Wellsite Calibration – HRLT M01</b>							
Before: 23-Sep-2014 3:35 After: 23-Sep-2014 9:31							
HRLT M0-M1 Voltage Plus – 0	0	N/A	-318.6	-319.0	-0.3972	9.681	UV
HRLT M0-M1 Voltage Plus – 1	0	N/A	-327.5	-330.6	-3.087	9.681	UV
HRLT M0-M1 Voltage Plus – 2	0	N/A	-330.5	-332.6	-2.123	9.681	UV
HRLT M0-M1 Voltage Plus – 3	0	N/A	-334.8	-336.7	-1.979	9.681	UV
HRLT M0-M1 Voltage Plus – 4	0	N/A	-324.8	-325.7	-0.9054	9.681	UV
HRLT M0-M1 Voltage Plus – 5	0	N/A	-321.5	-322.1	-0.5943	9.681	UV
HRLT M0-M1 Voltage Plus – 6	0	N/A	320.0	323.0	3.042	9.681	UV
HRLT M0-M1 Voltage Plus – 7	0	N/A	-322.7	-322.7	0	9.681	UV
<b>High Resolution Laterolog Array – B Wellsite Calibration – HRLT M12</b>							
Before: 23-Sep-2014 3:35 After: 23-Sep-2014 9:31							
HRLT M1-M2 Voltage Plus – 0	0	N/A	1754	1754	0.4924	53.42	UV
HRLT M1-M2 Voltage Plus – 1	0	N/A	1807	1822	15.27	53.42	UV
HRLT M1-M2 Voltage Plus – 2	0	N/A	1816	1827	10.23	53.42	UV
HRLT M1-M2 Voltage Plus – 3	0	N/A	1839	1848	8.822	53.42	UV
HRLT M1-M2 Voltage Plus – 4	0	N/A	1784	1787	3.019	53.42	UV
HRLT M1-M2 Voltage Plus – 5	0	N/A	1766	1767	1.385	53.42	UV
HRLT M1-M2 Voltage Plus – 6	0	N/A	-1774	-1789	-15.79	53.42	UV
HRLT M1-M2 Voltage Plus – 7	0	N/A	1781	1781	0	53.42	UV
<b>High Resolution Laterolog Array – B Wellsite Calibration – HRLT M23</b>							
Before: 23-Sep-2014 3:35 After: 23-Sep-2014 9:31							
HRLT M2-M3 Voltage Plus – 0	0	N/A	1741	1740	-0.8749	53.42	UV
HRLT M2-M3 Voltage Plus – 1	0	N/A	1806	1819	13.49	53.42	UV
HRLT M2-M3 Voltage Plus – 2	0	N/A	1817	1825	8.390	53.42	UV
HRLT M2-M3 Voltage Plus – 3	0	N/A	1843	1850	7.481	53.42	UV
HRLT M2-M3 Voltage Plus – 4	0	N/A	1781	1782	1.479	53.42	UV
HRLT M2-M3 Voltage Plus – 5	0	N/A	1764	1764	0.2654	53.42	UV
HRLT M2-M3 Voltage Plus – 6	0	N/A	-1762	-1776	-13.50	53.42	UV
HRLT M2-M3 Voltage Plus – 7	0	N/A	1781	1781	0	53.42	UV
<b>High Resolution Laterolog Array – B Wellsite Calibration – HRLT V34</b>							
Before: 23-Sep-2014 3:35 After: 23-Sep-2014 9:31							
HRLT A3-A4 Voltage Plus – 0	0	N/A	68360	68410	51.43	2100	UV
HRLT A3-A4 Voltage Plus – 1	0	N/A	70720	71340	622.7	2100	UV
HRLT A3-A4 Voltage Plus – 2	0	N/A	71420	71860	441.2	2100	UV
HRLT A3-A4 Voltage Plus – 3	0	N/A	72710	73090	387.9	2100	UV
HRLT A3-A4 Voltage Plus – 4	0	N/A	70240	70390	153.1	2100	UV
HRLT A3-A4 Voltage Plus – 5	0	N/A	69590	69670	80.90	2100	UV
HRLT A3-A4 Voltage Plus – 6	0	N/A	-68000	-68620	-617.2	2100	UV
HRLT A3-A4 Voltage Plus – 7	0	N/A	70000	70000	0	2100	UV
<b>High Resolution Laterolog Array – B Wellsite Calibration – HRLT V45</b>							
Before: 23-Sep-2014 3:35 After: 23-Sep-2014 9:31							
HRLT A4-A5 Voltage Plus – 0	0	N/A	68620	68690	69.00	2100	UV
HRLT A4-A5 Voltage Plus – 1	0	N/A	71090	71730	636.4	2100	UV
HRLT A4-A5 Voltage Plus – 2	0	N/A	71780	72220	433.8	2100	UV
HRLT A4-A5 Voltage Plus – 3	0	N/A	73050	73430	389.4	2100	UV
HRLT A4-A5 Voltage Plus – 4	0	N/A	70520	70690	170.5	2100	UV
HRLT A4-A5 Voltage Plus – 5	0	N/A	69850	69960	106.8	2100	UV
HRLT A4-A5 Voltage Plus – 6	0	N/A	-68380	-68990	-601.6	2100	UV
HRLT A4-A5 Voltage Plus – 7	0	N/A	70000	70000	0	2100	UV
<b>High Resolution Laterolog Array – B Wellsite Calibration – HRLT V56</b>							
Before: 23-Sep-2014 3:35 After: 23-Sep-2014 9:31							
HRLT A5-A6 Voltage Plus – 0	0	N/A	68530	68590	68.99	2100	UV
HRLT A5-A6 Voltage Plus – 1	0	N/A	70820	71460	631.8	2100	UV
HRLT A5-A6 Voltage Plus – 2	0	N/A	71540	71980	442.0	2100	UV
HRLT A5-A6 Voltage Plus – 3	0	N/A	72860	73260	399.2	2100	UV
HRLT A5-A6 Voltage Plus – 4	0	N/A	70390	70540	155.1	2100	UV
HRLT A5-A6 Voltage Plus – 5	0	N/A	69750	69850	93.20	2100	UV
HRLT A5-A6 Voltage Plus – 6	0	N/A	-68100	-68720	-623.2	2100	UV
HRLT A5-A6 Voltage Plus – 7	0	N/A	70000	70000	0	2100	UV
<b>High Resolution Laterolog Array – B Wellsite Calibration – HRLT VTP</b>							
Before: 23-Sep-2014 3:35 After: 23-Sep-2014 9:31							
HRLT Torpedo-M0 Voltage – 0	0	N/A	-68210	-68260	-50.92	2100	UV
HRLT Torpedo-M0 Voltage – 1	0	N/A	-71130	-71780	-646.8	2100	UV
HRLT Torpedo-M0 Voltage – 2	0	N/A	-71850	-72280	-430.9	2100	UV
HRLT Torpedo-M0 Voltage – 3	0	N/A	-73140	-73530	-395.6	2100	UV
HRLT Torpedo-M0 Voltage – 4	0	N/A	-70590	-70750	-154.5	2100	UV
HRLT Torpedo-M0 Voltage – 5	0	N/A	-69910	-70000	-85.94	2100	UV

HRLT Torpedo-M0 Voltage - 6	0	N/A	68370	68980	611.8	2100	UV
HRLT Torpedo-M0 Voltage - 7	0	N/A	-70000	-70000	0	2100	UV

High Resolution Laterolog Array - B Wellsite Calibration - HRLT VBD

Before: 23-Sep-2014 3:35 After: 23-Sep-2014 9:31

HRLT Bridle#9-M0 Voltage - 0	0	N/A	-68200	-68260	-64.10	2100	UV
HRLT Bridle#9-M0 Voltage - 1	0	N/A	-71110	-71770	-656.3	2100	UV
HRLT Bridle#9-M0 Voltage - 2	0	N/A	-71820	-72260	-442.6	2100	UV
HRLT Bridle#9-M0 Voltage - 3	0	N/A	-73110	-73510	-394.9	2100	UV
HRLT Bridle#9-M0 Voltage - 4	0	N/A	-70580	-70740	-167.2	2100	UV
HRLT Bridle#9-M0 Voltage - 5	0	N/A	-69900	-70000	-98.30	2100	UV
HRLT Bridle#9-M0 Voltage - 6	0	N/A	68340	68960	627.5	2100	UV
HRLT Bridle#9-M0 Voltage - 7	0	N/A	-70000	-70000	0	2100	UV

High Resolution Laterolog Array - B Wellsite Calibration - HRLT ISO

Before: 23-Sep-2014 3:35 After: 23-Sep-2014 9:31

HRLT Source Current Plus - 0	0	N/A	284.4	284.7	0.2599	8.520	UA
HRLT Source Current Plus - 1	0	N/A	281.1	281.1	0	8.520	UA
HRLT Source Current Plus - 2	0	N/A	281.1	281.1	0	8.520	UA
HRLT Source Current Plus - 3	0	N/A	281.1	281.1	0	8.520	UA
HRLT Source Current Plus - 4	0	N/A	281.1	281.1	0	8.520	UA
HRLT Source Current Plus - 5	0	N/A	281.1	281.1	0	8.520	UA
HRLT Source Current Plus - 6	0	N/A	281.1	281.1	0	8.520	UA
HRLT Source Current Plus - 7	0	N/A	281.1	281.1	0	8.520	UA

High Resolution Laterolog Array - B Wellsite Calibration - HRLT MV

Before: 23-Sep-2014 3:35 After: 23-Sep-2014 9:31

HRLT Vertical Voltage PI - 0	0	N/A	-321.4	-321.4	-0.02020	9.681	UV
HRLT Vertical Voltage PI - 1	0	N/A	-323.0	-325.8	-2.784	9.681	UV
HRLT Vertical Voltage PI - 2	0	N/A	-325.0	-326.6	-1.630	9.681	UV
HRLT Vertical Voltage PI - 3	0	N/A	-327.3	-328.7	-1.466	9.681	UV
HRLT Vertical Voltage PI - 4	0	N/A	-314.6	-315.0	-0.4435	9.681	UV
HRLT Vertical Voltage PI - 5	0	N/A	-326.3	-326.4	-0.1440	9.681	UV
HRLT Vertical Voltage PI - 6	0	N/A	328.4	331.3	2.980	9.681	UV
HRLT Vertical Voltage PI - 7	0	N/A	-322.7	-322.7	0	9.681	UV

Hostile Litho-Density Sonde Wellsite Calibration - Background Measurement

Master: 16-Jul-2014 4:36 Before: 23-Sep-2014 3:38 After: 23-Sep-2014 9:34

SS Cs Resolution Bkg	9.000	8.061	7.985	8.044	0.05823	1.800	%
LS Cs Resolution Bkg	9.000	8.137	8.095	8.222	0.1272	1.800	%
LSW1 Background	100.0	69.74	68.96	67.97	-0.9935	3.000	CPS
LSW2 Background	100.0	63.61	63.19	63.28	0.08903	3.000	CPS
LSW3 Background	200.0	141.8	140.7	140.4	-0.2910	6.000	CPS
LSW4 Background	250.0	172.4	172.6	170.6	-2.018	7.500	CPS
LSW5 Background	600.0	395.0	393.5	391.6	-1.914	18.00	CPS
SSW1 Background	100.0	78.54	77.91	76.86	-1.048	3.000	CPS
SSW2 Background	200.0	139.1	137.7	139.8	2.131	6.000	CPS
SSW3 Background	500.0	371.9	370.6	369.4	-1.204	15.00	CPS
SSW4 Background	270.0	195.4	194.2	194.0	-0.2188	8.100	CPS
SSW5 Background	200.0	142.5	140.7	138.7	-2.005	6.000	CPS

Hostile Litho-Density Sonde Wellsite Calibration - Aluminum Measurement

Master: 16-Jul-2014 5:05

LSW1 Aluminum	600.0	508.4	N/A	N/A	N/A	N/A	CPS
LSW2 Aluminum	900.0	733.7	N/A	N/A	N/A	N/A	CPS
LSW3 Aluminum	1100	883.4	N/A	N/A	N/A	N/A	CPS
LSW4 Aluminum	580.0	447.4	N/A	N/A	N/A	N/A	CPS
LSW5 Aluminum	570.0	407.5	N/A	N/A	N/A	N/A	CPS
SSW1 Aluminum	2800	2389	N/A	N/A	N/A	N/A	CPS
SSW2 Aluminum	8000	6455	N/A	N/A	N/A	N/A	CPS
SSW3 Aluminum	11600	8951	N/A	N/A	N/A	N/A	CPS
SSW4 Aluminum	5000	3637	N/A	N/A	N/A	N/A	CPS
SSW5 Aluminum	660.0	442.1	N/A	N/A	N/A	N/A	CPS

Hostile Litho-Density Sonde Wellsite Calibration - Lithology Measurement

Master: 16-Jul-2014 4:57

LSW1 Iron	400.0	349.8	N/A	N/A	N/A	N/A	CPS
LSW2 Iron	730.0	590.1	N/A	N/A	N/A	N/A	CPS
LSW3 Iron	1000	785.3	N/A	N/A	N/A	N/A	CPS
LSW4 Iron	520.0	408.9	N/A	N/A	N/A	N/A	CPS
LSW5 Iron	470.0	376.5	N/A	N/A	N/A	N/A	CPS
SSW1 Iron	2100	1743	N/A	N/A	N/A	N/A	CPS
SSW2 Iron	6800	5378	N/A	N/A	N/A	N/A	CPS
SSW3 Iron	10800	8163	N/A	N/A	N/A	N/A	CPS
SSW4 Iron	4600	3323	N/A	N/A	N/A	N/A	CPS
SSW5 Iron	580.0	390.1	N/A	N/A	N/A	N/A	CPS

Hostile Litho-Density Sonde Wellsite Calibration - Caliper Calibration

Before: 17-Jul-2014 5:38

HLDS Caliper Small Ring	12.00	N/A	15.84	N/A	N/A	N/A	IN
HLDS Caliper Large Ring	15.19	N/A	19.69	N/A	N/A	N/A	IN

Hostile Natural Gamma Ray Sonde Wellsite Calibration – Detector 1 Check

Master: 15-Jul-2014 0:16 Before: 23-Sep-2014 3:43 After: 23-Sep-2014 9:35

Na 511 Peak Loc	40.00	39.57	39.57	39.68	0.1186	1.000	
Na 511 Peak Res	15.50	15.78	15.35	14.71	-0.6379	2.000	%
High Voltage	1150	1197	1187	1186	-0.7285	N/A	V
Na 1785 Peak Loc	142.6	142.4	141.8	142.6	0.7831	7.000	
Na 1785 Peak Res	8.500	9.334	8.462	9.740	1.278	2.000	%
Temperature	15.50	37.42	35.70	33.88	-1.827	N/A	DEGC
Na Count Rate	45.00	10.91	9.927	9.941	0.01461	8.000	CPS

Hostile Natural Gamma Ray Sonde Wellsite Calibration – Detector 2 Check

Master: 15-Jul-2014 0:16 Before: 23-Sep-2014 3:43 After: 23-Sep-2014 9:35

Na 511 Peak Loc	40.00	39.46	39.49	39.67	0.1857	1.000	
Na 511 Peak Res	15.50	16.20	15.66	15.36	-0.2991	2.000	%
High Voltage	1150	1129	1121	1132	10.84	N/A	V
Na 1785 Peak Loc	142.6	141.8	140.7	142.8	2.092	7.000	
Na 1785 Peak Res	8.500	10.06	8.501	8.168	-0.3334	2.000	%
Temperature	15.50	38.37	35.89	35.35	-0.5446	N/A	DEGC
Na Count Rate	45.00	11.54	10.34	10.12	-0.2134	8.000	CPS

Hostile Natural Gamma Ray Sonde Wellsite Calibration – Ratio Of Detector 1 To Detector 2

Master: 15-Jul-2014 0:16 Before: 23-Sep-2014 3:43 After: 23-Sep-2014 9:35

Coincidence Count Rate Ratio	1.000	0.9495	0.9661	0.9843	0.01826	0.05000	
------------------------------	-------	--------	--------	--------	---------	---------	--

Enhanced DTS Cartridge Wellsite Calibration – EDTC Accelerometer Calibration

Before: 23-Sep-2014 3:45

EDTC Z-Axis Acceleration	9.810	N/A	9.750	N/A	N/A	N/A	M/S2
--------------------------	-------	-----	-------	-----	-----	-----	------

Enhanced DTS Cartridge Wellsite Calibration – Detector Calibration

Before: 23-Sep-2014 3:36 After: 23-Sep-2014 9:32

Gamma Ray (Jig – Bkg)	160.3	N/A	160.3	155.0	-5.277	14.57	GAPI
Gamma Ray (Calibrated)	165.0	N/A	165.0	159.6	-5.432	15.00	GAPI

High Resolution Laterolog Array – B / Equipment Identification

Primary Equipment:

HRLT Sonde

HRLS – B

Auxiliary Equipment:

HRLT lower Housing

HRLH – B

HRLT Lower Cartridge

HRLC – B

HRLT upper Housing

HRUH – B

HRLT Upper Cartridge

HRUC – B

High Resolution Laterolog Array – B Wellsite Calibration

HRLT M01

Idx	Phase	HRLT M0-M1 Voltage Plus UV	Value	Nominal	Maximum	Minimum
0	Before		-318.6	-322.7	-280.7	-379.7
	After		-319.0			
1	Before		-327.5	-322.7	-280.7	-379.7
	After		-330.6			
2	Before		-330.5	-322.7	-280.7	-379.7
	After		-332.6			
3	Before		-334.8	-322.7	-280.7	-379.7
	After		-336.7			
4	Before		-324.8	-322.7	-280.7	-379.7
	After		-325.7			
5	Before		-321.5	-322.7	-280.7	-379.7
	After		-322.1			
6	Before		320.0	322.7	379.7	280.7
	After		323.0			
7	Before		-322.7	-322.7	-280.7	-379.7
	After		-322.7			

After	-322.7			
(Minimum)	(Nominal)	(Maximum)		
Before: 23-Sep-2014 3:35				
After: 23-Sep-2014 9:31				

High Resolution Laterolog Array – B Wellsite Calibration						
HRLT M12						
Idx	Phase	HRLT M1–M2 Voltage Plus UV	Value	Nominal	Maximum	Minimum
0	Before		1754	1781	2095	1549
	After		1754			
1	Before		1807	1781	2095	1549
	After		1822			
2	Before		1816	1781	2095	1549
	After		1827			
3	Before		1839	1781	2095	1549
	After		1848			
4	Before		1784	1781	2095	1549
	After		1787			
5	Before		1766	1781	2095	1549
	After		1767			
6	Before		-1774	-1781	-1549	-2095
	After		-1789			
7	Before		1781	1781	2095	1549
	After		1781			
		(Minimum) (Nominal) (Maximum)				
Before: 23-Sep-2014 3:35						
After: 23-Sep-2014 9:31						

High Resolution Laterolog Array – B Wellsite Calibration						
HRLT M23						
Idx	Phase	HRLT M2–M3 Voltage Plus UV	Value	Nominal	Maximum	Minimum
0	Before		1741	1781	2095	1549
	After		1740			
1	Before		1806	1781	2095	1549
	After		1819			
2	Before		1817	1781	2095	1549
	After		1825			
3	Before		1843	1781	2095	1549
	After		1850			
4	Before		1781	1781	2095	1549
	After		1782			
5	Before		1764	1781	2095	1549
	After		1764			
6	Before		-1762	-1781	-1549	-2095
	After		-1776			
7	Before		1781	1781	2095	1549
	After		1781			
		(Minimum) (Nominal) (Maximum)				
Before: 23-Sep-2014 3:35						

Before: 23-Sep-2014 3:35

After: 23-Sep-2014 9:31

High Resolution Laterolog Array – B Wellsite Calibration						
HRLT V34						
Idx	Phase	HRLT A3–A4 Voltage Plus UV	Value	Nominal	Maximum	Minimum
0	Before		68360	70000	82360	60900
	After		68410			
1	Before		70720	70000	82360	60900
	After		71340			
2	Before		71420	70000	82360	60900
	After		71860			
3	Before		72710	70000	82360	60900
	After		73090			
4	Before		70240	70000	82360	60900
	After		70390			
5	Before		69590	70000	82360	60900
	After		69670			
6	Before		-68000	-70000	-60900	-82360
	After		-68620			
7	Before		70000	70000	82360	60900
	After		70000			
		(Minimum) (Nominal) (Maximum)				

Before: 23-Sep-2014 3:35

After: 23-Sep-2014 9:31

High Resolution Laterolog Array – B Wellsite Calibration						
HRLT V45						
Idx	Phase	HRLT A4–A5 Voltage Plus UV	Value	Nominal	Maximum	Minimum
0	Before		68620	70000	82360	60900
	After		68690			
1	Before		71090	70000	82360	60900
	After		71730			
2	Before		71780	70000	82360	60900
	After		72220			
3	Before		73050	70000	82360	60900
	After		73430			
4	Before		70520	70000	82360	60900
	After		70690			
5	Before		69850	70000	82360	60900
	After		69960			
6	Before		-68380	-70000	-60900	-82360
	After		-68990			
7	Before		70000	70000	82360	60900
	After		70000			
		(Minimum) (Nominal) (Maximum)				

Before: 23-Sep-2014 3:35

After: 23-Sep-2014 9:31

High Resolution Laterolog Array – B Wellsite Calibration



High Resolution Laterolog Array – B Wellsite Calibration

HRLT V56

Idx	Phase	HRLT A5–A6 Voltage Plus UV	Value	Nominal	Maximum	Minimum
0	Before		68530	70000	82360	60900
	After		68590			
1	Before		70820	70000	82360	60900
	After		71460			
2	Before		71540	70000	82360	60900
	After		71980			
3	Before		72860	70000	82360	60900
	After		73260			
4	Before		70390	70000	82360	60900
	After		70540			
5	Before		69750	70000	82360	60900
	After		69850			
6	Before		-68100	-70000	-60900	-82360
	After		-68720			
7	Before		70000	70000	82360	60900
	After		70000			
		(Minimum) (Nominal) (Maximum)				

Before: 23-Sep-2014 3:35

After: 23-Sep-2014 9:31

High Resolution Laterolog Array – B Wellsite Calibration

HRLT VTP

Idx	Phase	HRLT Torpedo–M0 Voltage Plus UV	Value	Nominal	Maximum	Minimum
0	Before		-68210	-70000	-60900	-82360
	After		-68260			
1	Before		-71130	-70000	-60900	-82360
	After		-71780			
2	Before		-71850	-70000	-60900	-82360
	After		-72280			
3	Before		-73140	-70000	-60900	-82360
	After		-73530			
4	Before		-70590	-70000	-60900	-82360
	After		-70750			
5	Before		-69910	-70000	-60900	-82360
	After		-70000			
6	Before		68370	70000	82360	60900
	After		68980			
7	Before		-70000	-70000	-60900	-82360
	After		-70000			
		(Minimum) (Nominal) (Maximum)				

Before: 23-Sep-2014 3:35

After: 23-Sep-2014 9:31

High Resolution Laterolog Array – B Wellsite Calibration

HRLT VBD

Idx	Phase	HRLT Bridle#9–M0 Voltage Plus UV	Value	Nominal	Maximum	Minimum
0	Before					
	After					

0	Before		-68200	-70000	-60900	-82360
	After		-68260			
1	Before		-71110	-70000	-60900	-82360
	After		-71770			
2	Before		-71820	-70000	-60900	-82360
	After		-72260			
3	Before		-73110	-70000	-60900	-82360
	After		-73510			
4	Before		-70580	-70000	-60900	-82360
	After		-70740			
5	Before		-69900	-70000	-60900	-82360
	After		-70000			
6	Before		68340	70000	82360	60900
	After		68960			
7	Before		-70000	-70000	-60900	-82360
	After		-70000			
			(Minimum)	(Nominal)	(Maximum)	

Before: 23-Sep-2014 3:35

After: 23-Sep-2014 9:31

High Resolution Laterolog Array – B Wellsite Calibration						
HRLT ISO						
Idx	Phase	HRLT Source Current Plus UA	Value	Nominal	Maximum	Minimum
0	Before		284.4	284.0	334.1	247.0
	After		284.7			
1	Before		281.1	281.1	330.7	244.4
	After		281.1			
2	Before		281.1	281.1	330.7	244.4
	After		281.1			
3	Before		281.1	281.1	330.7	244.4
	After		281.1			
4	Before		281.1	281.1	330.7	244.4
	After		281.1			
5	Before		281.1	281.1	330.7	244.4
	After		281.1			
6	Before		281.1	281.1	330.7	244.4
	After		281.1			
7	Before		281.1	281.1	330.7	244.4
	After		281.1			
			(Minimum)	(Nominal)	(Maximum)	

Before: 23-Sep-2014 3:35

After: 23-Sep-2014 9:31

High Resolution Laterolog Array – B Wellsite Calibration						
HRLT MV						
Idx	Phase	HRLT Vertical Voltage Plus UV	Value	Nominal	Maximum	Minimum
0	Before		-321.4	-322.7	-280.7	-379.7
	After		-321.4			

1	Before		-323.0	-322.7	-280.7	-379.7
	After		-325.8			
2	Before		-325.0	-322.7	-280.7	-379.7
	After		-326.6			
3	Before		-327.3	-322.7	-280.7	-379.7
	After		-328.7			
4	Before		-314.6	-322.7	-280.7	-379.7
	After		-315.0			
5	Before		-326.3	-322.7	-280.7	-379.7
	After		-326.4			
6	Before		328.4	322.7	379.7	280.7
	After		331.3			
7	Before		-322.7	-322.7	-280.7	-379.7
	After		-322.7			
			(Minimum)	(Nominal)	(Maximum)	
Before: 23-Sep-2014 3:35						
After: 23-Sep-2014 9:31						

### Hostile Litho-Density Sonde / Equipment Identification

**Primary Equipment:**

Hostile Litho Density Sonde	HLDS - D	45
Hostile Litho Density High Voltage	HLDV - D	45
Gamma Source Radioactive	GSR - Z	8113

**Auxiliary Equipment:**

Hostile Litho Density Pad	HLDP - C	45
Hostile Litho Density High Voltage Housi	HEH - H	47

### Hostile Litho-Density Sonde Wellsite Calibration

Background Measurement									
Phase	SS Cs Resolution Bkg %	Value	Phase	LS Cs Resolution Bkg %	Value	Phase	LSW1 Background CPS	Value	
Master		8.061	Master		8.137	Master		69.74	
Before		7.985	Before		8.095	Before		68.96	
After		8.044	After		8.222	After		67.97	
7.000 (Minimum) 9.000 (Nominal) 11.00 (Maximum)			7.000 (Minimum) 9.000 (Nominal) 11.00 (Maximum)			55.00 (Minimum) 100.0 (Nominal) 150.0 (Maximum)			
Phase	LSW2 Background CPS	Value	Phase	LSW3 Background CPS	Value	Phase	LSW4 Background CPS	Value	
Master		63.61	Master		141.8	Master		172.4	
Before		63.19	Before		140.7	Before		172.6	
After		63.28	After		140.4	After		170.6	
50.00 (Minimum) 100.0 (Nominal) 140.0 (Maximum)			110.0 (Minimum) 200.0 (Nominal) 290.0 (Maximum)			140.0 (Minimum) 250.0 (Nominal) 360.0 (Maximum)			
Phase	LSW5 Background CPS	Value	Phase	SSW1 Background CPS	Value	Phase	SSW2 Background CPS	Value	
Master		395.0	Master		78.54	Master		139.1	
Before		393.5	Before		77.91	Before		137.7	
After		391.6	After		76.86	After		139.8	
330.0 (Minimum) 600.0 (Nominal) 830.0 (Maximum)			55.00 (Minimum) 100.0 (Nominal) 150.0 (Maximum)			100.0 (Minimum) 200.0 (Nominal) 260.0 (Maximum)			
Phase	SSW3 Background CPS	Value	Phase	SSW4 Background CPS	Value	Phase	SSW5 Background CPS	Value	
Master		371.9	Master		195.4	Master		142.5	
Before		370.6	Before		194.2	Before		140.7	
After		369.4	After		194.0	After		138.7	
280.0 (Minimum) 500.0 (Nominal) 700.0 (Maximum)			150.0 (Minimum) 270.0 (Nominal) 380.0 (Maximum)			110.0 (Minimum) 200.0 (Nominal) 270.0 (Maximum)			

Litho-Density Spectroscopy Cartridge - B / Equipment Identification

Primary Equipment: LDSC Cartridge	LDSC - B	521
Auxiliary Equipment: LDSC Housing	LDSH - A	319

Hostile Natural Gamma Ray Cartridge - B / Equipment Identification

Primary Equipment: HNGC Cartridge	HNGC - B	300
Auxiliary Equipment: HNGC Housing	HNGH - A	115

Hostile Natural Gamma Ray Sonde / Equipment Identification

Primary Equipment: HNGS Sonde	HNGS - BA	194
Auxiliary Equipment: HNGS Sonde Housing Gamma Source Radioactive	HNSH - BA GSR - U	205 616008

Hostile Natural Gamma Ray Sonde Wellsite Calibration

Detector 1 Check

Phase	Na 511 Peak Loc	Value	Phase	Na 511 Peak Res %	Value	Phase	High Voltage V	Value
Master		39.57	Master		15.78	Master		1197
Before		39.57	Before		15.35	Before		1187
After		39.68	After		14.71	After		1186
	37.50 (Minimum) 40.00 (Nominal) 43.50 (Maximum)			12.00 (Minimum) 15.50 (Nominal) 19.00 (Maximum)			900.0 (Minimum) 1150 (Nominal) 1600 (Maximum)	
Phase	Na 1785 Peak Loc	Value	Phase	Na 1785 Peak Res %	Value	Phase	Temperature DEGC	Value
Master		142.4	Master		9.334	Master		37.42
Before		141.8	Before		8.462	Before		35.70
After		142.6	After		9.740	After		33.88
	135.0 (Minimum) 142.6 (Nominal) 150.3 (Maximum)			7.000 (Minimum) 8.500 (Nominal) 11.00 (Maximum)			-28.89 (Minimum) 15.50 (Nominal) 60.00 (Maximum)	
Phase	Na Count Rate CPS	Value						
Master		10.91						
Before		9.927						
After		9.941						
	10.00 (Minimum) 45.00 (Nominal) 100.0 (Maximum)							

Hostile Natural Gamma Ray Sonde Wellsite Calibration

Detector 2 Check

Phase	Na 511 Peak Loc	Value	Phase	Na 511 Peak Res %	Value	Phase	High Voltage V	Value
Master		39.46	Master		16.20	Master		1129
Before		39.49	Before		15.66	Before		1121
After		39.67	After		15.36	After		1132
	37.50 (Minimum) 40.00 (Nominal) 43.50 (Maximum)			12.00 (Minimum) 15.50 (Nominal) 19.00 (Maximum)			900.0 (Minimum) 1150 (Nominal) 1600 (Maximum)	
Phase	Na 1785 Peak Loc	Value	Phase	Na 1785 Peak Res %	Value	Phase	Temperature DEGC	Value

Master		141.8	Master		10.06	Master		38.37
Before		140.7	Before		8.501	Before		35.89
After		142.8	After		8.168	After		35.35
135.0 (Minimum) 142.6 (Nominal) 150.3 (Maximum)			7.000 (Minimum) 8.500 (Nominal) 11.00 (Maximum)			-28.89 (Minimum) 15.50 (Nominal) 60.00 (Maximum)		
Phase	Na Count Rate CPS		Value					
Master			11.54					
Before			10.34					
After			10.12					
10.00 (Minimum) 45.00 (Nominal) 100.0 (Maximum)								
Master: 15-Jul-2014 0:16			Before: 23-Sep-2014 3:43			After: 23-Sep-2014 9:35		

Hostile Natural Gamma Ray Sonde Wellsite Calibration		
Ratio Of Detector 1 To Detector 2		
Phase	Coincidence Count Rate Ratio	Value
Master	<b>EXCEEDS LIMIT</b>	0.9495
Before		0.9661
After		0.9843
0.9500 (Minimum) 1.000 (Nominal) 1.050 (Maximum)		
Master: 15-Jul-2014 0:16		
Before: 23-Sep-2014 3:43		
After: 23-Sep-2014 9:35		

Enhanced DTS Cartridge / Equipment Identification		
Primary Equipment:		
EDTC Gamma Ray Detector	EDTG - A/B	8305
Enhanced DTS Cartridge	EDTC - B	8317
Auxiliary Equipment:		
EDTC Housing	EDTH - B	8303

Enhanced DTS Cartridge Wellsite Calibration		
EDTC Accelerometer Calibration		
Phase	EDTC Z-Axis Acceleration M/S2	Value
Before		9.750
9.610 (Minimum) 9.810 (Nominal) 10.01 (Maximum)		
Before: 23-Sep-2014 3:45		

Enhanced DTS Cartridge Wellsite Calibration								
Detector Calibration								
Phase	Gamma Ray Background GAPI	Value	Phase	Gamma Ray (Jig - Bkg) GAPI	Value	Phase	Gamma Ray (Calibrated) GAPI	Value
Before		1.756	Before		160.3	Before		165.0
After		7.977	After		155.0	After		159.6
0 (Minimum) 30.00 (Nominal) 120.0 (Maximum)			145.7 (Minimum) 160.3 (Nominal) 174.9 (Maximum)			150.0 (Minimum) 165.0 (Nominal) 180.0 (Maximum)		
Before: 23-Sep-2014 3:36			After: 23-Sep-2014 9:32					

Well: Expedition 352, Site U1442A  
Field: IBM-3 Forearc  
Rig: JOIDES Resolution  
Country:

HNGS Spectral GR
